

# KLEINZEE SOLAR PV FACILITY, NORTHERN CAPE PROVINCE


Environmental Management Programme for the  
132kV power line

May 2023

savannah  
environmental

APPENDIX 1  
GENERIC ENVIRONMENTAL MANAGEMENT PROGRAMME (EMPr) FOR THE  
DEVELOPMENT AND EXPANSION OF OVERHEAD ELECTRICITY  
TRANSMISSION AND DISTRIBUTION INFRASTRUCTURE

---

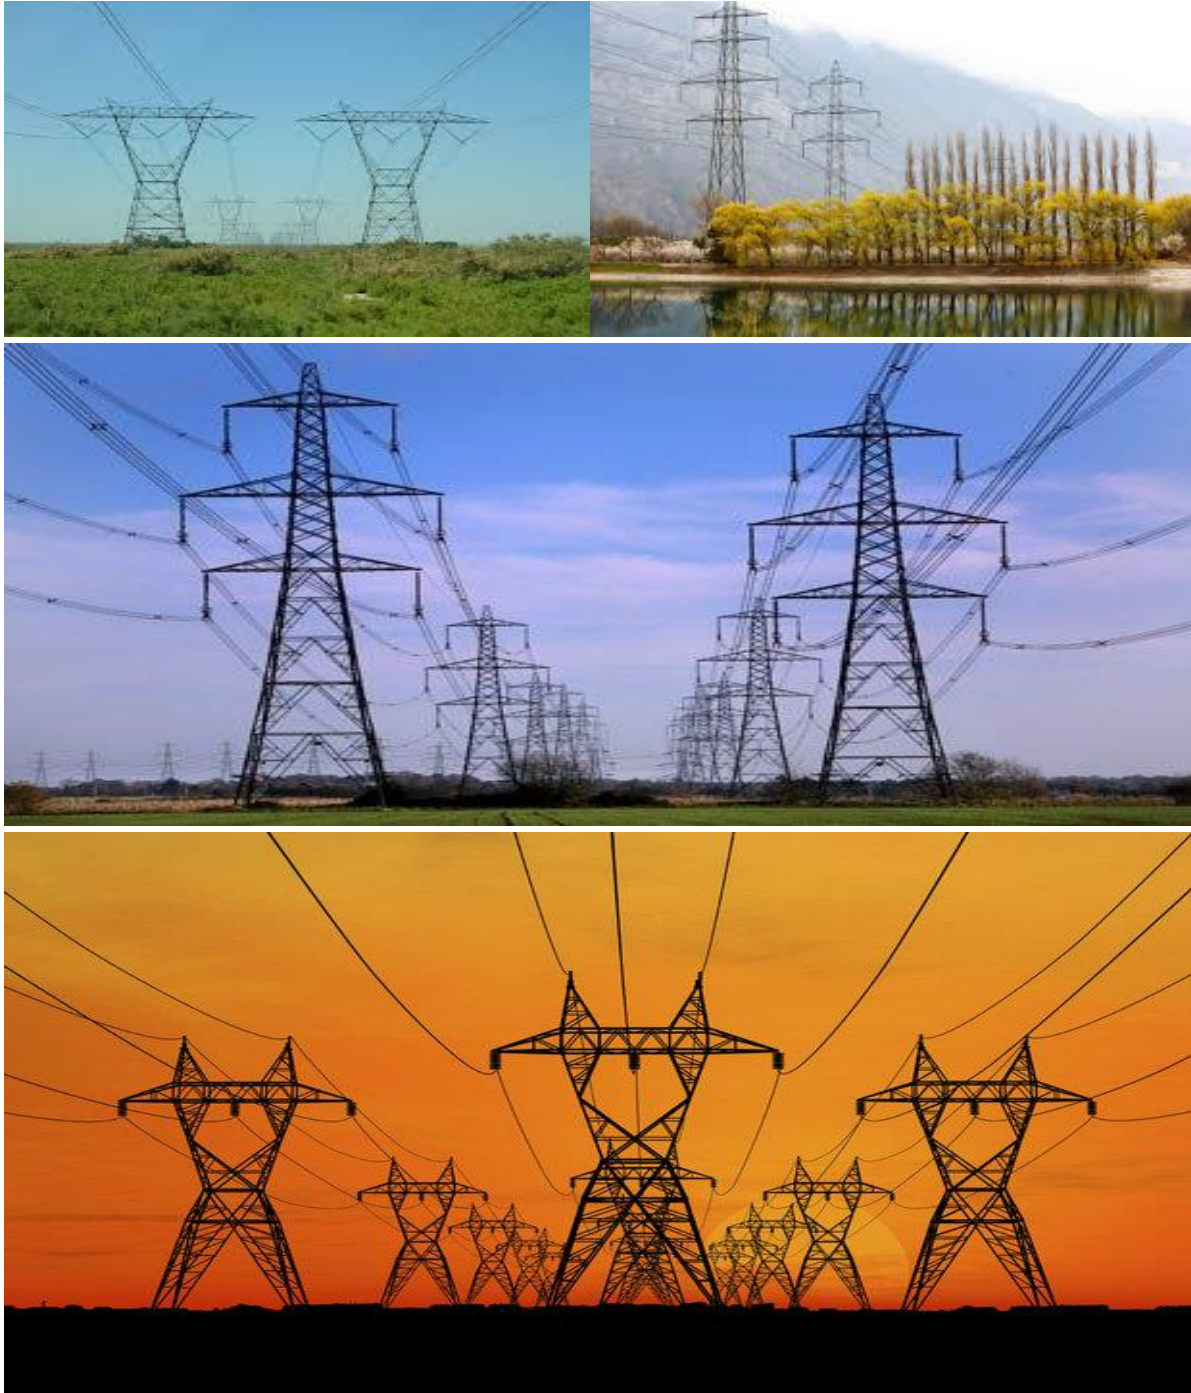

**environmental affairs**

Department:  
Environmental Affairs  
REPUBLIC OF SOUTH AFRICA

## TABLE OF CONTENTS

	<b>PAGE</b>
INTRODUCTION .....	1
1. Background.....	1
2. Purpose.....	1
3. Objective .....	1
4. Scope.....	1
5. Structure of this document.....	2
6. Completion of part B: section 1: the pre-approved generic EMPr template .....	4
7. Amendments of the impact management outcomes and impact management actions .....	4
8. Documents to be submitted as part of part B: section 2 site specific information and declaration 5	
(a) Amendments to Part B: Section 2 – site specific information and declaration .....	5
PART A – GENERAL INFORMATION .....	6
1. DEFINITIONS .....	6
2. ACRONYMS and ABBREVIATIONS.....	7
National Environmental Management: Biodiversity Act ,2004 (Act No. 10 of 2004) .....	7
3. ROLES AND RESPONSIBILITIES FOR ENVIRONMENTAL MANAGEMENT PROGRAMME (EMPr) IMPLEMENTATION.....	8
4. ENVIRONMENTAL DOCUMENTATION REPORTING AND COMPLIANCE.....	14
4.1 Document control/Filing system .....	14
4.2 Documentation to be available.....	14
4.3 Weekly Environmental Checklist .....	14
4.4 Environmental site meetings .....	15
4.5 Required Method Statements .....	15
4.6 Environmental Incident Log (Diary) .....	16
4.7 Non-compliance.....	16
4.8 Corrective action records .....	17
4.9 Photographic record .....	17
4.10 Complaints register.....	18
4.11 Claims for damages.....	18
4.12 Interactions with affected parties .....	18
4.13 Environmental audits.....	19
4.14 Final environmental audits .....	19
PART B: SECTION 1: Pre-approved generic EMPr template .....	20
5. IMPACT MANAGEMENT OUTCOMES AND IMPACT MANAGEMENT ACTIONS.....	20
5.1 Environmental awareness training .....	21
5.2 Site Establishment development.....	24

5.3	Access restricted areas .....	25
5.4	Access roads .....	27
5.5	Fencing and Gate installation .....	30
5.6	Water Supply Management .....	35
5.7	Storm and wastewater management .....	36
5.8	Solid and hazardous waste management .....	37
5.9	Protection of watercourses .....	40
5.10	Vegetation clearing .....	44
5.11	Protection of fauna .....	49
5.12	Protection of heritage resources .....	53
5.13	Safety of the public .....	55
5.14	Sanitation .....	57
5.15	Prevention of disease.....	59
5.16	Emergency procedures.....	61
5.17	Hazardous substances.....	63
5.18	Workshop, equipment maintenance and storage.....	70
5.19	Batching plants.....	72
5.20	Dust emissions.....	75
5.21	Blasting.....	77
5.22	Noise .....	77
5.23	Fire prevention .....	79
5.24	Stockpiling and stockpile areas .....	80
5.25	Finalising tower positions .....	82
5.26	Excavation and Installation of foundations .....	83
5.27	Assembly and erecting towers.....	85
5.28	Stringing .....	90
5.29	Socio-economic .....	93
5.30	Temporary closure of site .....	95
5.31	Landscaping and rehabilitation .....	99
6	ACCESS TO THE GENERIC EMPr .....	103
PART B: SECTION 2 .....		103
7	SITE SPECIFIC INFORMATION AND DECLARATION .....	104
7.1	Sub-section 1: contact details and description of the project .....	104
7.2	Sub-section 2: Development footprint site map.....	109
7.3	Sub-section 3: Declaration .....	123
7.4	Sub-section 4: amendments to site specific information (Part B; section 2) .....	123
PART C .....		123
8	SITE SPECIFIC ENVIRONMENTAL ATTRIBUTES.....	123

<b>CONSTRUCTION AND DECOMMISSIONING OUTCOMES AND ACTIONS</b> .....	125
7.1 <b>Ecology (Fauna and Flora)</b> .....	125
7.2 <b>Aquatic Ecology</b> .....	<b>Error! Bookmark not defined.</b>
7.3 <b>Avifauna</b> .....	137
7.4 <b>Land Use, Soils and Agricultural Potential</b> .....	137
7.5 <b>Heritage</b> .....	142
7.6 <b>Visual</b> .....	144
7.7 <b>Socio-Economic</b> .....	148
<b>OPERATIONAL PHASE OUTCOMES AND ACTIONS</b> .....	158
7.8 <b>Ecology (Fauna and Flora)</b> .....	<b>Error! Bookmark not defined.</b>
7.9 <b>Aquatic Ecology</b> .....	<b>Error! Bookmark not defined.</b>
7.10 <b>Avifauna</b> .....	163
7.11 <b>Land Use, Soils and Agricultural Potential</b> .....	164
7.12 <b>Visual</b> .....	166
7.13 <b>Socio-Economic</b> .....	166
APPENDIX 1: METHOD STATEMENTS .....	172
APPENDIX 2: CV OF THE EAP .....	173

## List of tables

Table 1: <i>Guide to roles and responsibilities for implementation of an EMPr</i> .....	8
---	---

## **INTRODUCTION**

### **1. Background**

The National Environmental Management Act, 1998 (Act No. 107 of 1998) (NEMA) requires that an environmental management programme (EMPr) be submitted where an environmental impact assessment (EIA) has been identified as the environmental instrument to be utilised as the basis for a decision on an application for environmental authorisation (EA). The content of an EMPr must either contain the information set out in Appendix 4 of the Environmental Impact Assessment Regulations, 2014, as amended, (EIA Regulations) or must be a generic EMPr relevant to an application as identified and gazetted by the Minister in a government notice. Once the Minister has identified, through a government notice, that a generic EMPr is relevant to an application for EA, that generic EMPr must be applied by all parties involved in the EA process, including, but not limited to, the applicant and the competent authority (CA).

### **2. Purpose**

This document constitutes a generic EMPr relevant to applications for the development or expansion of overhead electricity transmission and distribution infrastructure, and all listed and specified activities necessary for the realisation of such infrastructure.

### **3. Objective**

The objective of this generic EMPr is to prescribe and pre-approve generally accepted impact management outcomes and impact management actions, which can commonly and repeatedly be used for the avoidance, management and mitigation of impacts and risks associated with the development or expansion of overhead electricity transmission and distribution infrastructure. The use of a generic EMPr is intended to reduce the need to prepare and review individual EMPrs for applications of a similar nature.

### **4. Scope**

The scope of this generic EMPr applies to the development or expansion of overhead electricity transmission and distribution infrastructure requiring EA in terms of NEMA, i.e. with a capacity of 33 kilovolts or more. This generic EMPr applies to activities requiring EA, mainly activity 11 and 47 of the Environmental Impact Assessment Regulations Listing Notice 1 of 2014, as amended, and activity 9 of the Environmental Impact Assessment Regulations Listing Notice 2 of 2014, as amended, and all associated listed or specified activities necessary for the realisation of such infrastructure.

## 5. Structure of this document

This document is structured in three parts with an Appendix as indicated in the table below:

Part	Section	Heading	Content
A		Provides general guidance and information and is <b>not legally binding</b>	Definitions, acronyms, roles & responsibilities and documentation and reporting.
B	1	Pre-approved generic EMPr template	<p>Contains generally accepted impact management outcomes and impact management actions required for the avoidance, management and mitigation of impacts and risks associated with the development or expansion of overhead electricity transmission and distribution infrastructure, which are presented in the form of a template that has been pre-approved.</p> <p>The template in this section is to be completed by the contractor, with each completed page signed and dated by the holder of the EA prior to commencement of the activity.</p> <p>Where an impact management outcome is not relevant, the words "not applicable" can be inserted in the template under the "responsible persons" column.</p> <p>Once completed and signed, the template represents the EMPr for the activity approved by the CA and is legally binding. The template <b>is not required</b> to be submitted to the CA as once the generic EMPr is gazetted for implementation, it has been approved by the CA.</p> <p>To allow interested and affected parties access to the pre-approved EMPr template for consideration through the decision-making process, the EAP on behalf of the applicant /proponent must make the hard copy of this EMPr available at a public location and where the applicant has a website, the EMPr should also be made available on such publicly accessible website.</p>
	2	Site specific information	Contains preliminary infrastructure layout and a declaration that the applicant/holder of the EA

Part	Section	Heading	Content
			<p>will comply with the pre-approved generic EMPr template contained in <u>Part B: Section 1</u>, and understands that the impact management outcomes and impact management actions are <b>legally binding</b>. The preliminary infrastructure layout must be finalized to inform the final EMPr that is to be submitted with the basic assessment report (BAR) or environmental impact assessment report (EIAR), ensuring that all impact management outcomes and actions have been either pre-approved or approved in terms of <u>Part C</u>.</p> <p>This section <b>must be</b> submitted to the CA together with the final BAR or EIAR. The information submitted to the CA will be considered to be incomplete should a signed copy of <u>Part B: section 2</u> not be submitted. Once approved, this Section forms part of the EMPr for the development and is legally binding.</p>
C		Site specific sensitivities/ attributes	<p>If any specific environmental sensitivities/ attributes are present on the site which require site specific impact management outcomes and impact management actions, not included in the pre-approved generic EMPr, to manage impacts, these specific impact management outcomes and impact management actions must be included in this section. These specific environmental attributes must be referenced spatially, and impact management outcomes and impact management actions must be provided. These specific impact management outcomes and impact management actions must be presented in the format of the pre-approved EMPr template (<u>Part B: section 1</u>)</p> <p>This section will not be required should the site contain no specific environmental sensitivities or attributes. However, if <u>Part C</u> is applicable to the site, it <b>is required</b> to be submitted together with the BAR or EIAR, for consideration of, and decision on, the application for EA. The information in this section must be prepared by an EAP and must contain his/her name and</p>



Part	Section	Heading	Content
			<p>expertise including a curriculum vitae. Once approved, Part C forms part of the EMPr for the site and is legally binding.</p> <p>This section applies only <b>to additional</b> impact management outcomes and impact management actions that are necessary for the avoidance, management and mitigation of impacts and risks associated with the specific development or expansion and which are not already included in <u>Part B: section 1</u>.</p>
	Appendix 1		Contains the method statements to be prepared prior to commencement of the activity. The method statements are <b>not required</b> to be submitted to the competent authority.

## 6. Completion of part B: section 1: the pre-approved generic EMPr template

The template is to be completed prior to commencement of the activity, by providing the following information for each environmental impact management action:

- For implementation
  - a 'responsible person';
  - a method for implementation; and
  - a timeframe for implementation.
- For monitoring
  - a 'responsible person';
  - Frequency; and
  - evidence of compliance.

The completed template must be signed and dated by the holder of the EA prior to commencement of the activity. The method statements prepared and agreed to by the holder of the EA must be appended to the template as Appendix 1. Each method statement must be signed and dated on each page by the holder of the EA. This template, once signed and dated, is legally binding. The holder of the EA will remain responsible for its implementation.

## 7. Amendments of the impact management outcomes and impact management actions

Once the activity has commenced, a holder of an EA may make amendments to the impact management outcomes and impact management actions in the following manner:

- Amendment of the impact management outcomes: in line with the process contemplated in regulation 37 of the EIA Regulations; and
- Amendment of the impact management actions: in line with the process contemplated in regulation 36 of the EIA Regulations.

## **8. Documents to be submitted as part of part B: section 2 site specific information and declaration**

Part B: Section 2 has three distinct sub-sections. The first and third sub-sections are in a template format. Sub-section two requires a map to be produced.

Sub-section 1 contains the project name, the applicant's name and contact details, the site information, which includes coordinates of the corridor in which the proposed overhead electricity transmission and distribution infrastructure is proposed as well as the 21-digit Surveyor General code of each cadastral land parcel and, where available, the farm name.

Sub-section 2 is to be prepared by an EAP and must contain his/her name and expertise including a curriculum vitae. This sub-section must include a map of the site sensitivity overlaid with the preliminary infrastructure layout using the national web based environmental screening tool, when available for compulsory use at: <https://screening.environment.gov.za/screeningtool>. The sensitivity map shall identify the nature of each sensitive feature e.g. raptor nest, threatened plant species, archaeological site, etc. Sensitivity maps must identify features both within the planned working area and any known sensitive features in the surrounding landscape within 50m from the development footprint. The overhead transmission and distribution profile must be illustrated at an appropriate resolution to enable fine scale interrogation. It is recommended that <20 km of overhead transmission and distribution length is illustrated per page in A3 landscape format. Where considered appropriate, photographs of sensitive features in the context of tower positions must be used.

Sub-section 3 is the declaration that the applicant/proponent or holder of the EA in the case of a change of ownership must complete, which confirms that the applicant/EA holder will comply with the pre-approved generic EMPr template in Section 1 and understands that the impact management outcomes and actions are legally binding.

### **(a) Amendments to Part B: Section 2 – site specific information and declaration**

Should the EA be transferred, Part B: Section 2 must be completed by the new applicant/proponent and submitted with the application for an amendment of the EA in terms of Regulations 29 or 31 of the EIA Regulations, whichever applies. The information submitted as part of such an application for an amendment to an EA will be considered to be incomplete should a signed copy of Part B: Section 2 not be submitted. Once approved, Part B: Section 2 forms part of the EMPr for the development and the EMPr becomes legally binding to the new EA holder.

## PART A – GENERAL INFORMATION

### 1. DEFINITIONS

In this EMPr any word or expression to which a meaning has been assigned in the NEMA or EIA Regulations has that meaning, and unless the context requires otherwise –

**"clearing"** means the clearing and removal of vegetation, whether partially or in whole, including trees and shrubs, as specified;

**"construction camp"** is the area designated for key construction infrastructure and services, including but not limited to offices, overnight vehicle parking areas, stores, the workshop, stockpile and lay down areas, hazardous storage areas (including fuels), the batching plant (if one is located at the construction camp), designated access routes, equipment cleaning areas and the placement of staff accommodation, cooking and ablution facilities, waste and wastewater management;

**"contractor"** - The Contractor has overall responsibility for ensuring that all work, activities, and actions linked to the delivery of the contract, are in line with the Environmental Management Programme and that Method Statements are implemented as described.

**"hazardous substance"** is a substance governed by the Hazardous Substances Act, 1973 (Act No. 15 of 1973) as well as the Hazardous Chemical and Substances Regulations, 1995;

**"method statement"** means a written submission by the Contractor to the Project Manager in response to this EMPr or a request by the Project Manager and ECO. The method statement must set out the equipment, materials, labour and method(s) the Contractor proposes using to carry out an activity identified by the Project Manager when requesting the Method Statement. This must be done in such detail that the Project Manager and ECO is able to assess whether the Contractor's proposal is in accordance with this specification and/or will produce results in accordance with this specification;

The method statement must cover applicable details with regard to:

- (i) Construction procedures;
- (ii) Plant, materials and equipment to be used;
- (iii) Transporting the equipment to and from site;
- (iv) How the plant/ material/ equipment will be moved while on site;
- (v) How and where the plant/ material/ equipment will be stored;
- (vi) The containment (or action to be taken if containment is not possible) of leaks or spills of any liquid or material that may occur;
- (vii) Timing and location of activities;
- (viii) Compliance/ non-compliance; and
- (ix) Any other information deemed necessary by the Project Manager.

**"slope"** means the inclination of a surface expressed as one unit of rise or fall for so many horizontal units;

“**solid waste**” means all solid waste, including construction debris, hazardous waste, excess cement/ concrete, wrapping materials, timber, cans, drums, wire, nails, food and domestic waste (e.g. plastic packets and wrappers);

“**spoil**” means excavated material which is unsuitable for use as material in the construction works or is material which is surplus to the requirements of the construction works;

“**topsoil**” means a varying depth (up to 300 mm) of the soil profile irrespective of the fertility, appearance, structure, agricultural potential, fertility and composition of the soil; and

“**works**” means the works to be executed in terms of the Contract.

## 2. ACRONYMS and ABBREVIATIONS

<b>CA</b>	Competent Authority
<b>cEO</b>	Contractors Environmental Officer
<b>dEO</b>	Developer Environmental Officer
<b>DPM</b>	Developer Project Manager
<b>DSS</b>	Developer Site Supervisor
<b>EAR</b>	Environmental Audit Report
<b>ECA</b>	Environment Conservation Act No. 73 of 1989
<b>ECO</b>	Environmental Control Officer
<b>EA</b>	Environmental Authorisation
<b>EIA</b>	Environmental Impact Assessment
<b>ERAP</b>	Emergency Response Action Plan
<b>EMPr</b>	Environmental Management Programme Report
<b>EAP</b>	Environmental Assessment Practitioner
<b>FPA</b>	Fire Protection Agency
<b>HCS</b>	Hazardous chemical Substance
<b>NEMA</b>	National Environmental Management Act, 1998 (Act No. 107 of 1998)
<b>NEMBA</b>	National Environmental Management: Biodiversity Act ,2004 (Act No. 10 of 2004)
<b>NEMWA</b>	National Environmental Management: Waste Act, 2008 (Act No. 59 of 2008)
<b>MSDS</b>	Material Safety Data Sheet
<b>RI&amp;APs</b>	Registered interested and affected parties

### 3. ROLES AND RESPONSIBILITIES FOR ENVIRONMENTAL MANAGEMENT PROGRAMME (EMPr) IMPLEMENTATION

The effective implementation of this generic EMPr is dependent on established and clear roles, responsibilities and reporting lines within an institutional framework. This section of the EMPr gives guidance to the various environmental roles and reporting lines, however, project specific requirements will ultimately determine the need for the appointment of specific person(s) to undertake specific roles and or responsibilities. As such, it must be noted that in the event that no specific person, for example, an environmental control officer (ECO) is appointed, the holder of the EA remains responsible for ensuring that the duties indicated in this document for action by the ECO are undertaken.

**Table 1:** Guide to roles and responsibilities for implementation of an EMPr

Responsible Person (s)	Role and Responsibilities
Developer's Project Manager (DPM)	<p><u>Role</u></p> <p>The Project Developer is accountable for ensuring compliance with the EMPr and any conditions of approval from the competent authority (CA). Where required, an environmental control officer (ECO) must be contracted by the Project Developer to objectively monitor the implementation of the EMPr according to relevant environmental legislation, and the conditions of the environmental authorisation (EA). The Project Developer is further responsible for providing and giving mandate to enable the ECO to perform responsibilities, and he must ensure that the ECO is integrated as part of the project team while remaining independent.</p> <p><u>Responsibilities</u></p> <ul style="list-style-type: none"> <li>- Be fully conversant with the conditions of the EA;</li> <li>- Ensure that all stipulations within the EMPr are communicated and adhered to by the Developer and its Contractor(s);</li> <li>- Issuing of site instructions to the Contractor for corrective actions required;</li> <li>- Monitor the implementation of the EMPr throughout the project by means of site inspections and meetings. Overall management of the project and EMPr implementation; and</li> <li>- Ensure that periodic environmental performance audits are undertaken on the project implementation.</li> </ul>
Developer Site Supervisor (DSS)	<u>Role</u>

Responsible Person (s)	Role and Responsibilities
	<p>The DSS reports directly to the DPM, oversees site works, liaises with the contractor(s) and the ECO. The DSS is responsible for the day to day implementation of the EMPr and for ensuring the compliance of all contractors with the conditions and requirements stipulated in the EMPr.</p> <p><u>Responsibilities</u></p> <ul style="list-style-type: none"> <li>- Ensure that all contractors identify a contractor's Environmental Officer (cEO);</li> <li>- Must be fully conversant with the conditions of the EA. Oversees site works, liaison with Contractor, DPM and ECO;</li> <li>- Must ensure that all landowners have the relevant contact details of the site staff, ECO and cEO;</li> <li>- Issuing of site instructions to the Contractor for corrective actions required;</li> <li>- Will issue all non-compliances to contractors; and</li> <li>- Ratify the Monthly Environmental Report.</li> </ul>
Environmental Control Officer (ECO)	<p><u>Role</u></p> <p>The ECO should have appropriate training and experience in the implementation of environmental management specifications. The primary role of the ECO is to act as an independent quality controller and monitoring agent regarding all environmental concerns and associated environmental impacts. In this respect, the ECO is to conduct periodic site inspections, attend regular site meetings, pre-empt problems and suggest mitigation and be available to advise on incidental issues that arise. The ECO is also required to conduct compliance audits, verifying the monitoring reports submitted by the cEO and dEO. The ECO provides feedback to the DSS and Project Manager regarding all environmental matters. The Contractor, cEO and dEO are answerable to the Environmental Control Officer for non- compliance with the Performance Specifications as set out in the EA and EMPr.</p> <p>The ECO provides feedback to the DSS and Project Manager, who in turn reports back to the Contractor and potential and Registered Interested &amp;Affected Parties (RI&amp;APs), as required. Issues of non-compliance raised by the ECO must be taken up by the Project Manager, and resolved with the Contractor as per the conditions of his contract. Decisions regarding environmental procedures, specifications and requirements which have a cost implication (i.e. those that are deemed to be a</p>

Responsible Person (s)	Role and Responsibilities
	<p>variation, not allowed for in the Performance Specification) must be endorsed by the Project Manager. The ECO must also, as specified by the EA, report to the relevant CA as and when required.</p> <p><u>Responsibilities</u></p> <p>The responsibilities of the ECO will include the following:</p> <ul style="list-style-type: none"> <li>- Be aware of the findings and conclusions of all EA related to the development;</li> <li>- Be familiar with the recommendations and mitigation measures of this EMPr;</li> <li>- Be conversant with relevant environmental legislation, policies and procedures, and ensure compliance with them;</li> <li>- Undertake regular and comprehensive site inspections / audits of the construction site according to the generic EMPr and applicable licenses in order to monitor compliance as required;</li> <li>- Educate the construction team about the management measures contained in the EMPr and environmental licenses;</li> <li>- Compilation and administration of an environmental monitoring plan to ensure that the environmental management measures are implemented and are effective;</li> <li>- Monitoring the performance of the Contractors and ensuring compliance with the EMPr and associated Method Statements;</li> <li>- In consultation with the Developer Site Supervisor order the removal of person(s) and/or equipment which are in contravention of the specifications of the EMPr and/or environmental licenses;</li> <li>- Liaison between the DPM, Contractors, authorities and other lead stakeholders on all environmental concerns;</li> <li>- Compile a regular environmental audit report highlighting any non-compliance issues as well as satisfactory or exceptional compliance with the EMPr;</li> <li>- Validating the regular site inspection reports, which are to be prepared by the contractor Environmental Officer (cEO);</li> <li>- Checking the cEO's record of environmental incidents (spills, impacts, legal transgressions etc) as well as corrective and preventive actions taken;</li> </ul>

Responsible Person (s)	Role and Responsibilities
	<ul style="list-style-type: none"> <li>- Checking the cEO's public complaints register in which all complaints are recorded, as well as action taken;</li> <li>- Assisting in the resolution of conflicts;</li> <li>- Facilitate training for all personnel on the site – this may range from carrying out the training, to reviewing the training programmes of the Contractor;</li> <li>- In case of non-compliances, the ECO must first communicate this to the Senior Site Supervisor, who has the power to ensure this matter is addressed. Should no action or insufficient action be taken, the ECO may report this matter to the authorities as non-compliance;</li> <li>- Maintenance, update and review of the EMPr;</li> <li>- Communication of all modifications to the EMPr to the relevant stakeholders.</li> </ul>
<p>developer Environmental Officer (dEO)</p>	<p><u>Role</u></p> <p>The dEOs will report to the Project Manager and are responsible for implementation of the EMPr, environmental monitoring and reporting, providing environmental input to the Project Manager and Contractor's Manager, liaising with contractors and the landowners as well as a range of environmental coordination responsibilities.</p> <p><u>Responsibilities</u></p> <ul style="list-style-type: none"> <li>- Be fully conversant with the EMPr;</li> <li>- Be familiar with the recommendations and mitigation measures of this EMPr, and implement these measures;</li> <li>- Ensure that all stipulations within the EMPr are communicated and adhered to by the Employees, Contractor(s) ;</li> <li>- Confine the development site to the demarcated area;</li> <li>- Conduct environmental internal audits with regards to EMPr and authorisation compliance (on cEO);</li> <li>- Assist the contractors in addressing environmental challenges on site;</li> <li>- Assist in incident management;</li> <li>- Reporting environmental incidents to developer and ensuring that corrective action is taken, and lessons learnt shared;</li> </ul>



Responsible Person (s)	Role and Responsibilities
	<ul style="list-style-type: none"> <li>- Assist the contractor in investigating environmental incidents and compile investigation reports;</li> <li>- Follow-up on pre-warnings, defects, non-conformance reports;</li> <li>- Measure and communicate environmental performance to the Contractor;</li> <li>- Conduct environmental awareness training on site together with ECO and cEO;</li> <li>- Ensure that the necessary legal permits and / or licenses are in place and up to date;</li> <li>- Acting as Developer's Environmental Representative on site and work together with the ECO and contractor;</li> </ul>
Contractor	<p><u>Role</u></p> <p>The Contractor appoints the cEO and has overall responsibility for ensuring that all work, activities, and actions linked to the delivery of the contract are in line with the EMPr and that Method Statements are implemented as described. External contractors must ensure compliance with this EMPr while performing the onsite activities as per their contract with the Project Developer. The contractors are required, where specified, to provide Method Statements setting out in detail how the impact management actions contained in the EMPr will be implemented during the development or expansion for overhead electricity transmission and distribution infrastructure activities.</p> <p><u>Responsibilities</u></p> <ul style="list-style-type: none"> <li>- project delivery and quality control for the development services as per appointment;</li> <li>- employ a suitably qualified person to monitor and report to the Project Developer's appointed person on the daily activities on-site during the construction period;</li> <li>- ensure that safe, environmentally acceptable working methods and practices are implemented and that equipment is properly operated and maintained, to facilitate proper access and enable any operation to be carried out safely;</li> <li>- attend on site meeting(s) prior to the commencement of activities to confirm the procedure and designated activity zones;</li> <li>- ensure that contractors' staff repair, at their own cost, any environmental damage as a result of a contravention of the specifications contained in EMPr, to the satisfaction of the ECO.</li> </ul>

Responsible Person (s)	Role and Responsibilities
contractor Environmental Officer (cEO)	<p><u>Role</u></p> <p>Each Contractor affected by the EMPr should appoint a cEO, who is responsible for the on-site implementation of the EMPr (or relevant sections of the EMPr). The Contractor's representative can be the site agent; site engineer; a dedicated environmental officer; or an independent consultant. The Contractor must ensure that the Contractor's Representative is suitably qualified to perform the necessary tasks and is appointed at a level such that she/he can interact effectively with other site Contractors, labourers, the Environmental Control Officer and the public. As a minimum the cEO shall meet the following criteria:</p> <p><u>Responsibilities</u></p> <ul style="list-style-type: none"> <li>- Be on site throughout the duration of the project and be dedicated to the project;</li> <li>- Ensure all their staff are aware of the environmental requirements, conditions and constraints with respect to all of their activities on site;</li> <li>- Implementing the environmental conditions, guidelines and requirements as stipulated within the EA, EMPr and Method Statements;</li> <li>- Attend the Environmental Site Meeting;</li> <li>- Undertaking corrective actions where non-compliances are registered within the stipulated timeframes;</li> <li>- Report back formally on the completion of corrective actions;</li> <li>- Assist the ECO in maintaining all the site documentation;</li> <li>- Prepare the site inspection reports and corrective action reports for submission to the ECO;</li> <li>- Assist the ECO with the preparing of the monthly report; and</li> <li>- Where more than one Contractor is undertaking work on site, each company appointed as a Contractor will appoint a cEO representing that company.</li> </ul>

## 4. ENVIRONMENTAL DOCUMENTATION REPORTING AND COMPLIANCE

To ensure accountable and demonstrated implementation of the EMPr, a number of reporting systems, documentation controls and compliance mechanisms must be in place for all overhead electricity transmission and distribution infrastructure projects as a minimum requirement.

### 4.1 Document control/Filing system

The holder of the EA is solely responsible for the upkeep and management of the EMPr file. At a minimum, all documentation detailed below will be stored in the EMPr file. A hard copy of all documentation shall be filed, while an electronic copy may be kept where relevant. A duplicate file will be maintained in the office of the DSS (where applicable). This duplicate file must remain current and up-to-date. The filing system must be updated and relevant documents added as required. The EMPr file must be made available at all times on request by the CA or other relevant authorities. The EMPr file will form part of any environmental audits undertaken as prescribed in the EIA Regulations.

### 4.2 Documentation to be available

At the outset of the project the following preliminary list of documents shall be placed in the filing system and be accessible at all times:

- Full copy of the signed EA from the CA in terms of NEMA, granting approval for the development or expansion;
- Copy of the generic and site specific EMPr as well as any amendments thereof;
- Copy of declaration of implementing generic EMPr and subsequent approval of site specific EMPr and amendments thereof;
- All method statements;
- Completed environmental checklists;
- Minutes and attendance register of environmental site meetings;
- An up-to-date environmental incident log;
- A copy of all instructions or directives issued;
- A copy of all corrective actions signed off. The corrective actions must be filed in such a way that a clear reference is made to the non-compliance record; and
- Complaints register.

### 4.3 Weekly Environmental Checklist

The ECOs are required to complete a Weekly Environmental Checklist, the format of which is to be agreed prior to commencement of the activity. The ECOs are required to sign and date the checklist, retain a copy in the EMPr file and submit a copy of the completed checklist to the DSS on a weekly basis.

The checklists will form the basis for the Monthly Environmental Reports. Copies of all completed checklists will be attached as Annexures to the Environmental Audit Report as required in terms of the EIA Regulations.

#### 4.4 Environmental site meetings

Minutes of the environmental site meetings shall be kept. The minutes must include an attendance register and will be attached to the Monthly Report that is distributed to attendees. Each set of minutes must clearly record "Matters for Attention" that will be reviewed at the next meeting.

#### 4.5 Required Method Statements

The method statement will be done in such detail that the ECOs are enabled to assess whether the contractor's proposal is in accordance with the EMPr.

The method statement must cover applicable details with regard to:

- development procedures;
- materials and equipment to be used;
- getting the equipment to and from site;
- how the equipment/ material will be moved while on site;
- how and where material will be stored;
- the containment (or action to be taken if containment is not possible) of leaks or spills of any liquid or material that may occur;
- timing and location of activities;
- compliance/ non-compliance with the EMPr; and
- any other information deemed necessary by the ECOs.

Unless indicated otherwise by the Project Manager, the Contractor shall provide the following method statements to the Project Manager no less than 14 days prior to the commencement date of the activity:

- Site establishment – Camps, Lay-down or storage areas, satellite camps, infrastructure;
- Batch plants;
- Workshop or plant servicing;
- Handling, transport and storage of Hazardous Chemical Substances;
- Vegetation management – Protected, clearing, aliens, felling;
- Access management – Roads, gates, crossings etc.;
- Fire plan;
- Waste management – transport, storage, segregation, classification, disposal (all waste streams);
- Social interaction – complaints management, compensation claims, access to properties etc.;
- Water – use (source, abstraction and disposal), access and all related information, crossings and mitigation;
- Emergency preparedness – Spills, training, other environmental emergencies;
- Dust and noise management methodologies;
- Fauna interaction and risk management – only if the risk was identified – wildlife interaction especially on game farms; and
- Heritage and palaeontology management.

The ECOs shall monitor and ensure that the contractors perform in accordance with these method statements. Completed and agreed method statements between the holder of the EA and the contractor shall be captured in Appendix 1.

#### 4.6 Environmental Incident Log (Diary)

The ECOs are required to maintain an up-to-date and current Environmental Incident Log (environmental diary). The Environmental Incident Log is a means to record all environmental incidents and/or all non-compliance notice would not be issued. An environmental incident is defined as:

- Any deviation from the listed impact management actions (listed in this EMPr) that may be addressed immediately by the ECOs. (For example a contractor's staff member littering or a drip tray that has not been emptied);
- Any environmental impact resulting from an action or activity by a contractor in contravention of the environmental stipulations and guidelines listed in the EMPr which as a single event would have a minor impact but which if cumulative and continuous would have a significant effect (for example no toilet paper available in the ablutions for an afternoon); and
- General environmental information such as road kills or injured wildlife.

The ECOs are to record all environmental incidents in the Environmental Incident Log. All incidents regardless of severity must be reported to the Developer. The Log is to be kept in the EMPr file and at a minimum the following will be recorded for each environmental incident:

- The date and time of the incident;
- Description of the incident;
- The name of the Contractor responsible;
- The incident must be listed as significant or minor;
- If the incident is listed as significant, a non-compliance notice must be issued, and recorded in the log;
- Remedial or corrective action taken to mitigate the incident; and
- Record of repeat minor offences by the same contractor or staff member.

The Environmental Incident Log will be captured in the EAR.

#### 4.7 Non-compliance

A non-compliance notice will be issued to the responsible contractor by the ECOs via the DSS or Project Manager. The non-compliance notice will be issued in writing; a copy filed in the EMPr file and will at a minimum include the following:

- Time and date of the non-compliance;
- Name of the contractor responsible;
- Nature and description of the non-compliance;
- Recommended / required corrective action; and
- Date by which the corrective action to be completed.

- The contractors shall act immediately when a notice of non-compliance is received and correct whatever is the cause for the issuing of the notice. Complaints received regarding activities on the development site pertaining to the environment shall be recorded in a dedicated register and the response noted with the date and action taken. The ECO should be made aware of any complaints. Any non-compliance with the agreed procedures of the EMPr is a transgression of the various statutes and laws that define the manner by which the environment is managed. Failure to redress the cause shall be reported to the relevant CA for them to deal with the transgression, as it deems fit. The contractor is deemed not to have complied with the EMPr if, inter alia, There is a deviation from the environmental conditions, impact management outcomes and impact management actions , as approved in generic and site specific EMPr as relevant as set out in the EMPr, which deviation has, or may cause, an environmental impact.

#### 4.8 Corrective action records

For each non-compliance notice issued, a documented corrective action must be recorded. On receiving a non-compliance notice from the DSS, the contractor's cEO will ensure that the corrective actions required take place within the stipulated timeframe. On completion of the corrective action the cEO is to issue a Corrective Action Report in writing to the ECOs. If satisfied that the corrective action has been completed, the ECOs are to sign-off on the Corrective Action Report, and attach the report to the non-compliance notice in the EMPr file. A corrective action is considered complete once the report has signed off by the ECOs.

#### 4.9 Photographic record

A digital photographic record will be kept. The photographic record will be used to show before, during and post rehabilitation evidence of the project as well used in cases of damages claims if they arise. Each image must be dated and a brief description note attached.

The Contractor shall:

1. Allow the ECOs access to take photographs of all areas, activities and actions.

The ECOs shall keep an electronic database of photographic records which will include:

1. Pictures of all areas designated as work areas, camp areas, development sites and storage areas taken before these areas are set up;
2. All bunding and fencing;
3. Road conditions and road verges;
4. Condition of all farm fences;
5. Topsoil storage areas;
6. All areas to be cordoned off during construction;
7. Waste management sites;
8. Ablution facilities (inside and out);
9. Any non-conformances deemed to be "significant";
10. All completed corrective actions for non-compliances;
11. All required signage;

12. Photographic recordings of incidents;
13. All areas before, during and post rehabilitation; and
14. Include relevant photographs in the Final Environmental Audit Report.

#### 4.10 Complaints register

The ECOs shall keep a current and up-to-date complaints register. The complaints register is to be a record of all complaints received from communities, stakeholders and individuals. The Complaints Record shall:

1. Record the name and contact details of the complainant;
2. Record the time and date of the complaint;
3. Contain a detailed description of the complaint;
4. Where relevant and appropriate, contain photographic evidence of the complaint or damage (ECOs to take relevant photographs); and
5. Contain a copy of the ECOs written response to each complaint received and keep a record of any further correspondence with the complainant. The ECO's written response will include a description of any corrective action to be taken and must be signed by the Contractor, ECO and affected party. Where a damage claim is issued by the complainant, the ECOs shall respond as described in **(section 4.11)** below.

#### 4.11 Claims for damages

In the event that a Claim for Damages is submitted by a community, landowner or individual, the ECOs shall:

1. Record the full detail of the complaint as described in **(section 4.10)** above;
2. The DPM will evaluate the claim and associated damage and submit the evaluation to the Senior Site Representative for approval;
3. Following consideration by the DPM, the claim is to be resolved and settled immediately, or the reason for not accepting the claim communicated in writing to the claimant. Should the claimant not accept this, the ECO shall, in writing report the incident to the Developer's negotiator and legal department; and
4. A formal record of the response by the ECOs to the claimant as well as the rectification of the method of making payments not amount will be recorded in the EMPr file.

#### 4.12 Interactions with affected parties

Open, transparent and good relations with affected landowners, communities and regional staff are an essential aspect to the successful management and mitigation of environmental impacts.

The ECOs shall:

1. Ensure that all queries, complaints and claims are dealt within an agreed timeframe;

2. Ensure that any or all agreements are documented, signed by all parties and a record of the agreement kept in the EMPr file;
3. Ensure that a complaints telephone numbers are made available to all landowners and affected parties; and
4. Ensure that contact with affected parties is courteous at all times;

#### 4.13 Environmental audits

Internal environmental audits of the activity and implementation of the EMPr must be undertaken. The findings and outcomes must be included in the EMPr file and be submitted to the CA at intervals as indicated in the EA.

An Environmental Audit Report must be prepared monthly. The report will be tabled as the key point on the agenda of the Environmental Site Meeting. The Report is submitted for acceptance at the meeting and the final report will be circulated to the Project Manager and filed in the EMPr file. At a frequency determined by the EA, the ECOs shall submit the monthly reports to the CA. At a minimum the monthly report is to cover the following:

- Weekly Environmental Checklists;
- Deviations and non-compliances with the checklists;
- Non-compliances issued;
- Completed and reported corrective actions;
- Environmental Monitoring;
- General environmental findings and actions; and
- Minutes of the Bi-monthly Environmental Site Meetings.

#### 4.14 Final environmental audits

On final completion of the rehabilitation and/or requirements of the EA a final EAR is to be prepared and submitted to the CA. The EAR must comply with Appendix 7 of the EIA Regulations.



## **PART B: SECTION 1: Pre-approved generic EMPr template**

### **5. IMPACT MANAGEMENT OUTCOMES AND IMPACT MANAGEMENT ACTIONS**

This section provides a pre-approved generic EMPr template with aspects that are common to the development of overhead electricity transmission and distribution infrastructure. There is a list of aspects identified for the development or expansion of overhead electricity transmission and distribution infrastructure, and for each aspect a set of prescribed impact management outcomes and associated impact management actions have been identified. Holders of EAs are responsible to ensure the implementation of these outcomes and actions for all projects as a minimum requirement, in order to mitigate the impact of such aspects identified for the development or expansion of overhead electricity transmission and distribution infrastructure.

The template provided below is to be completed by providing the information under each heading for each environmental impact management action.

The completed template must be signed and dated on each page by both the contractor and the holder of the EA prior to commencement of the activity. The method statements prepared and agreed to by the holder of the EA must be appended to the template as Appendix 1. Each method statement must also be duly signed and dated on each page by the contractor and the holder of the EA. This template, once signed and dated, is legally binding. The holder of the EA will remain responsible for its implementation.

## 5.1 Environmental awareness training

**Impact management outcome:** All onsite staff are aware and understand the individual responsibilities in terms of this EMPr.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– All staff must receive environmental awareness training prior to commencement of the activities.	ECO / cEO / dEO	Hold environmental awareness training workshops	Pre-construction Construction and Operations	ECO dEO	Monthly and as and when required	Attendance registers and training minutes / notes for the record
– The Contractor must allow for sufficient sessions to train all personnel with no more than 20 personnel attending each course.	Contractor	Scheduling of sufficient sessions through consultation with the ECO / cEO / dEO	Pre-construction Construction	ECO dEO	Monthly and as and when required	Attendance registers and training minutes / notes for the record
– Refresher environmental awareness training is available as and when required.	cEO / dEO in consultation with the ECO	Hold refresher environmental awareness training workshops	During the construction phase	ECO dEO	Monthly and as and when required	Attendance registers and training minutes / notes for the record
– All staff are aware of the conditions and controls linked to the EA and within the EMPr and made aware of their individual roles and responsibilities in achieving compliance with the EA and EMPr.	cEO / dEO	Hold training workshops and ensure that the EA and EMPr is readily available	During the construction phase	ECO dEO	Monthly and as and when required	Attendance registers and training minutes / notes for the record
– The Contractor must erect and maintain information posters at key locations on site, and the posters must include the following information as a minimum: a) Safety notifications; and b) No littering.	Contractor	Develop and place appropriate posters at key locations	Pre-construction Construction	ECO dEO cEO	Monthly	Photographic record

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<p>– Environmental awareness training must include as a minimum the following:</p> <ul style="list-style-type: none"> <li>a) Description of significant environmental impacts, actual or potential, related to their work activities;</li> <li>b) Mitigation measures to be implemented when carrying out specific activities;</li> <li>c) Emergency preparedness and response procedures;</li> <li>d) Emergency procedures;</li> <li>e) Procedures to be followed when working near or within sensitive areas;</li> <li>f) Wastewater management procedures;</li> <li>g) Water usage and conservation;</li> <li>h) Solid waste management procedures;</li> <li>i) Sanitation procedures;</li> <li>j) Fire prevention; and</li> <li>k) Disease prevention.</li> </ul>	cEO / dEO in consultation with the ECO	Develop environmental awareness training material which covers the minimum requirements	Pre-construction Construction	ECO dEO	Prior to the commencement of the environmental awareness training	Environmental awareness training material requirements checklist
– A record of all environmental awareness training courses undertaken as part of the EMPr must be available.	ECO / cEO / dEO	Filing system including all proof of training (i.e. attendance register and training minutes / notes for the record)	During the construction phase	ECO dEO	Monthly	Completed and up to date filing system with proof of training
– Educate workers on the dangers of open and/or unattended fires.	cEO / dEO in consultation with the ECO	Develop environmental awareness training material	Pre-construction Construction	ECO dEO	Prior to the commencement of the environmental	Environmental awareness training material

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		which covers the dangers of open and/or unattended fire			awareness training	requirements checklist
– A staff attendance register of all staff to have received environmental awareness training must be available.	ECO / cEO / dEO	Filing system including all proof of training (i.e., attendance register)	During the construction phase	ECO dEO	Monthly	Completed and up to date filing system inclusive of all attendance registers
– Course material must be available and presented in appropriate languages that all staff can understand.	ECO / cEO / dEO	Develop environmental awareness training material in the required languages. Training material must be readily available to all staff	During the construction phase	ECO dEO	Monthly	Environmental awareness training material requirements checklist and the training register which must indicate the language of the training

## 5.2 Site Establishment development

**Impact management outcome:** Impacts on the environment are minimised during site establishment and the development footprint are kept to demarcated development area.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>A method statement must be provided by the contractor prior to any onsite activity that includes the layout of the construction camp in the form of a plan showing the location of key infrastructure and services (where applicable), including but not limited to offices, overnight vehicle parking areas, stores, the workshop, stockpile and lay down areas, hazardous materials storage areas (including fuels), the batching plant (if one is located at the construction camp), designated access routes, equipment cleaning areas and the placement of staff accommodation, cooking and ablution facilities, waste and wastewater management.</li> </ul>	Contractor	Development of an appropriate method statement	Pre-construction	ECO dEO	Once, prior to construction	Availability of the method statement which complies with the minimum requirements listed
<ul style="list-style-type: none"> <li>Location of construction camps must be within approved area to ensure that the site does not impact on sensitive areas identified in the environmental assessment or site walk through.</li> </ul>	DPM	Place construction camps outside of sensitive areas identified in the Basic Assessment Report	Pre-construction Construction	ECO dEO	Once, prior to construction	Availability of a layout and sensitivity map indicating avoidance of sensitive areas
<ul style="list-style-type: none"> <li>Sites must be located where possible on previously disturbed areas.</li> </ul>	DPM	Place site outside of sensitive areas and within	Pre-construction	ECO dEO	Once, prior to construction	Availability of a layout and sensitivity map indicating

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		previously disturbed areas identified in the BA Report				avoidance of sensitive areas and placement within disturbed areas
– The camp must be fenced in accordance with <b>Section 5.5: Fencing and gate installation.</b>	DPM	Design and implementation of fencing as per the requirements of Section 5.5 of this EMPr	Pre-construction & Construction	ECO dEO	Once, prior to construction and once during the construction of the fencing	The camp is fenced in accordance with Section 5.5 of this EMPr
– The use of existing accommodation for contractor staff, where possible, is encouraged.	Not applicable – the development of new accommodation is not proposed. Employees will be accommodated in the nearby towns such as Richmond and Victoria West and transported to and from site daily.					

### 5.3 Access restricted areas

**Impact management outcome:** Access to restricted areas prevented.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Identification of access restricted areas is to be informed by the environmental assessment, site walk through, and any additional areas identified during development.	dEO / cEO in consultation with the ECO	Spatially demarcate access restricted areas informed by the BA Report	Pre-construction	ECO	Once, prior to construction	Access restricted areas are identified and provided in a spatial format

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
- Erect, demarcate and maintain a temporary barrier with clear signage around the perimeter of any access restricted area, colour coding could be used if appropriate.	dEO / cEO in consultation with the ECO	Erect appropriate temporary barriers around access restricted areas	At the commencement and for the duration of the construction phase	ECO	Monthly	Access restricted areas are closed-off through temporary barriers and barriers are maintained to a sufficient standard
- Unauthorised access and development related activity inside access restricted areas is prohibited.	Contractor / dEO / cEO	Erect appropriate temporary barriers around access restricted areas and provide clear signage of restricted status	During the construction phase	ECO	Monthly, and as and when required	Photographic evidence and notes of compliance that no unauthorised access or activities has taken place within the access restricted areas

#### 5.4 Access roads

**Impact management outcome:** Minimise impact to the environment through the planned and restricted movement of vehicles on site.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Access to the servitude and tower positions must be negotiated with the relevant landowner and must fall within the assessed and authorised area.	DPM	Undertake negotiations for access to the servitude and tower positions with landowners affected by the power line	Pre-construction Construction Operation	dEO	Ongoing throughout construction and operation	Proof of negotiations with affected landowners and requirements for access to the servitude and tower positions in the form of written and signed agreements
– An access agreement must be formalised and signed by the DPM, Contractor and landowner before commencing with the activities.	DPM Contractor	Develop access agreements with the affected landowners. Ensure that agreements are approved and signed	Pre-construction	dEO ECO	Once, prior to construction	Availability of approved and signed negotiations
– The access roads to tower positions must be signposted after access has been negotiated and before the commencement of the activities.	Contractor	Develop and install signs to indicate access	Pre-construction	cEO / ECO	Once, prior to construction	Photographic record of signposted access roads and GPS co-ordinates of



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						where these are placed
– All private roads used for access to the servitude must be maintained and upon completion of the works, be left in at least the original condition.	Contractor	Undertake maintenance activities on private roads used for construction as degradation takes place	During the construction phase	cEO / ECO	Weekly	Photographic record of the pre-construction condition and degradation of roads, and records of the implementation and effectiveness of maintenance activities
– All contractors must be made aware of all the access routes.	dEO / cEO	Develop a map illustrating all access routes associated with the project and present and provide the map to all contractors	Pre-construction Construction	ECO	Once, prior to construction	Access routes map readily available
– Any access route deviation from that in the written agreement must be closed and re-vegetated immediately, at the contractor's expense.	Contractor	All access routes developed that are not in-line with the access route	Construction and Rehabilitation	cEO ECO	Bi-weekly (every two weeks)	Photographic record of the closure of access roads

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		agreements must be closed and re-habilitated to the pre-disturbance state				and re-vegetation
– Maximum use of both existing servitudes and existing roads must be made to minimise further disturbance through the development of new roads.	Contractor	Existing access routes to be used must be specified and the development of new roads must be avoided as far as possible	Construction and operation	cEO Operation and maintenance team	Weekly	Implementation of the approved layout
– In circumstances where private roads must be used, the condition of the said roads must be recorded in accordance with section 4.9: photographic record; prior to use and the condition thereof agreed by the landowner, the DPM, and the contractor.	dEO / cEO	Record the conditions of private roads to be used (prior to use) as per the requirements of section 4.9 and agree on the required condition of the roads with the landowner, DPM and contractor	During the construction phase	ECO	Prior to the use of private roads	Photographic record and proof of the road conditions agreed upon with the relevant parties

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Access roads in flattish areas must follow fence lines and tree belts to avoid fragmentation of vegetated areas or croplands.	DPM and Contractor	Design access roads to follow fence lines and avoid vegetated areas	Pre-construction	ECO	Once during the design and once prior to construction	Implementation of the approved layout
– Access roads must only be developed on pre-planned and approved roads.	Contractor	Construction of access roads only on pre-planned and approved access roads	During the construction phase	ECO once during the design dEO	Once during the design and weekly during the construction of access roads	Implementation of the approved layout

### 5.5 Fencing and Gate installation

**Impact management outcome:** Minimise impact to the environment and ensure safe and controlled access to the site through the erection of fencing and gates where required.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Use existing gates provided to gain access to all parts of the area authorised for development, where possible.	Contractor	Identify and inform all relevant staff of the existing gates to be used	Pre-construction & Construction	dEO	Monthly	Existing gates are utilised on a frequent basis and only limited new access gates are developed

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Existing and new gates to be recorded and documented in accordance with section 4.9: photographic record.	ECO	Existing and new gates will be recorded and documented as per the requirements of section 4.9	During the construction phase	ECO	Once, when the construction of all new gates have been completed	Photographic record of the existing and new gates as per the requirements of section 4.9
– All gates must be fitted with locks and be kept locked at all times during the development phase, unless otherwise agreed with the landowner.	Contractor	Ensure all relevant gates are fitted with locks and are always locked	Construction and Operation	ECO monthly, Operation and maintenance team and cEO	Bi-weekly (every second week)	All gates are locked and no complaints from landowners are received in this regard
– At points where the line crosses an existing fence in which there is no suitable gate within the extent of the line servitude, on the instruction of the DPM, a gate must be installed at the approval of the landowner.	dEO	Install new gates where required with the approval of the affected landowner	During the construction phase	ECO	Once, prior to construction and during the construction phase, as and when required	New gates are installed where the power line crosses fences
– Care must be taken that the gates must be so erected that there is a gap of no more than 100 mm between the bottom of the gate and the ground.	Contractor	Install gates in a manner so that there is a gap of no more than 100mm between the bottom of the gate and the ground	During the construction phase	cEO	Once, during the erection of the gates during the construction phase	New gates installed as per the requirement

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Where gates are installed in jackal proof fencing, a suitable reinforced concrete sill must be provided beneath the gate.	Contractor	Implement a reinforced concrete sill beneath gates installed for jackal proofing	During the construction phase	cEO	Once, during the erection of the gates during the construction phase	New gates installed as per the requirement
– Original tension must be maintained in the fence wires.	Contractor	Maintain original tension of fences through required activities	During the construction phase	ECO	Monthly	No tension reduction on fence wires
– All gates installed in electrified fencing must be re-electrified.	Contractor	Electrify gates installed in electrified fencing	During the construction phase	ECO	Once, during the erection of the gates during the construction phase	Gates installed in electrified fencing is electrified
– All demarcation fencing and barriers must be maintained in good working order for the duration of overhead transmission and distribution electricity infrastructure development activities.	Contractor	Undertake maintenance activities on fences and barriers	During the construction phase	ECO	Monthly	Photographic record of maintained fences and barriers
– Fencing must be erected around the camp, batching plants, hazardous storage areas, and all designated access restricted areas, where appropriate and would not cause harm to the sensitive flora.	Contractor	Fence construction camps, batching plants, hazardous storage areas and access restricted areas.	During the construction phase	ECO	Once during the erection of fencing	Photographic record of fences erected

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		Avoid sensitive flora				
– Any temporary fencing to restrict the movement of livestock must only be erected with the permission of the landowner.	dEO/ cEO Contractor	Obtain written approval from the relevant landowner where temporary fencing is required to restrict livestock movement	During the construction phase	ECO	To be monitored as temporary fencing is required	Written approval to be provided by the dEO
– All fencing must be developed of high-quality material bearing the SABS mark.	Contractor	Make use of high-quality materials approved by SABS	During the construction phase	cEO	To be monitored as fencing is erected during the construction phase	Use of high-quality materials for fencing approved by SABS
– The use of razor wire as fencing must be avoided as far as possible.	Contractor	Razor wire must not be sourced or used for the erection of fencing	During the construction phase	ECO	To be monitored as fencing is erected during the construction phase	Fences erected do not make use of razor wire
– Fenced areas with gate access must remain locked after hours, during weekends and on holidays if staff is away from site. Site security will be required at all times.	DSS and Contractor	Ensure fenced areas are locked as required through the implementation of a formalised	During the construction phase	DPM and Contractor	DPM and Contractor	Fences are locked and no complaints from landowners are received. A security

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		process. Appoint a security company				company is appointed
- On completion of the development phase all temporary fences are to be removed.	Contractor	Removal of all temporary fences	At the end of the Construction Phase	ECO dEO	Once, following the completion of the construction phase	No temporary fences associated with the project is present following the completion of the construction phase
- The contractor must ensure that all fence uprights are appropriately removed, ensuring that no uprights are cut at ground level but rather removed completely.	Contractor	Appropriate removal of all fence uprights	At the end of the Construction Phase	ECO dEO	Once, following the completion of the construction phase	No fence uprights associated with the project is present following the completion of the construction phase

## 5.6 Water Supply Management

**Impact management outcome:** Undertake responsible water usage.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>- All abstraction points or bore holes must be registered with the DWS and suitable water meters installed to ensure that the abstracted volumes are measured on a daily basis;</li> </ul>	DPM and Contractor	Obtaining relevant registrations from DWS and installation of water meters	Pre-construction	cEO	To be monitored with the installation of water meters and daily during construction and operation	Use of high-quality water meters
<ul style="list-style-type: none"> <li>- The Contractor must ensure the following:               <ul style="list-style-type: none"> <li>a. The vehicle abstracting water from a river does not enter or cross it and does not operate from within the river;</li> <li>b. No damage occurs to the riverbed or banks and that the abstraction of water does not entail stream diversion activities; and</li> <li>c. All reasonable measures to limit pollution or sedimentation of the downstream watercourse are implemented.</li> </ul> </li> </ul>	Not applicable - water will not be abstracted from a river					
<ul style="list-style-type: none"> <li>- Ensure water conservation is being practiced by:               <ul style="list-style-type: none"> <li>a. Minimising water use during cleaning of equipment;</li> <li>b. Undertaking regular audits of water systems;</li> <li>c. Including a discussion on water usage and conservation during environmental awareness training; and</li> <li>d. The use of grey water is encouraged.</li> </ul> </li> </ul>	Contractor / dEO / cEO in consultation with the ECO	Implement the required water conservation measures throughout on-site construction processes	During the construction phase	ECO	Monthly, and as and when required	Successful implementation of water conservation



## 5.7 Storm and wastewater management

**Impact management outcome:** Impacts to the environment caused by stormwater and wastewater discharges during construction are avoided.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Runoff from the cement/ concrete batching areas must be strictly controlled, and contaminated water must be collected, stored and either treated or disposed of off-site, at a location approved by the project manager.	Contractor	Implement measures for the control and management of runoff	During the construction phase	cEO	Weekly	No mismanagement of runoff or contaminated water due to the temporary concrete batching plant
– All spillage of oil onto concrete surfaces must be controlled by the use of an approved absorbent material and the used absorbent material disposed of at an appropriate waste disposal facility.	Contractor and cEO	Obtain approved absorbent material and make use of licensed waste disposal facilities for disposal of oil	During the Construction Phase	ECO	Monthly	Availability of approved absorbent material at the construction site and proof of disposal of oil at licensed disposal facilities
– Natural stormwater runoff not contaminated during the development and clean water can be discharged directly to watercourses and water bodies, subject to the Project Manager's approval and support by the ECO.	DPM in consultation with the ECO	Consultation between the DPM and the ECO to determine if water can be discharged directly into water bodies	During the construction phase	ECO	As and when the need arises to discharge natural stormwater runoff and clean water	Proof of consultation between the DPM and ECO and the outcomes thereof to be provided. Proof of water quality testing and the results thereof.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		(where present). The necessary water quality testing must be undertaken prior to discharge				

### 5.8 Solid and hazardous waste management

**Impact management outcome:** Waste is appropriately stored, handled and safely disposed of at a recognised waste facility.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– All measures regarding waste management must be undertaken using an integrated waste management approach.	Contractor	Develop and implement a waste management plan	During the construction phase	ECO	Monthly	Implementation of the waste management plan and proof of waste management through proof of responsible disposal
– Sufficient, covered waste collection bins (scavenger and weatherproof) must be provided.	Contractor	Provision of appropriate waste collection bins strategically placed	During the construction phase	cEO	Weekly	Appropriate waste collection bins are available throughout the site

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		throughout the site				
– A suitably positioned and clearly demarcated waste collection site must be identified and provided.	DPM and Contractor	Identify an appropriate location for the waste collection site which must be clearly demarcated through signage and temporary fencing	Design and Construction Phase	ECO	Once, prior to the commencement of construction	A waste collection site is appropriately placed and demarcated
– The waste collection site must be maintained in a clean and orderly manner.	Contractor	Regular collection of waste and maintenance of the area must be undertaken as per the waste requirements for the project during construction	During the Construction Phase	cEO	Weekly	The waste collection site is maintained and clean
– Waste must be segregated into separate bins and clearly marked for each waste type for recycling and safe disposal.	Contractor	Provide separate and marked bins for the different waste types associated with	During the Construction Phase	cEO	Weekly	Separate waste bins are available on site and waste generated is separated into the relevant bins

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		the construction phase				
– Staff must be trained in waste segregation.	cEO / dEO in consultation with the ECO	Include waste segregation as part of the environmental awareness training material.	Pre-construction Construction	ECO	Monthly, and as and when required	Environmental awareness training material requirements checklist
– Bins must be emptied regularly.	Contractor	Bins must be emptied before reaching total capacity and on a regular basis as required for the project	During the construction phase	ECO	Monthly	No mismanagement of bins.
– General waste produced onsite must be disposed of at registered waste disposal sites/ recycling company.	Contractor	Disposal of general waste at licensed waste disposal facilities must be undertaken as per the waste management plan	During the construction phase	ECO	Monthly	Disposal certificates of disposal at licensed facilities to be provided
– Hazardous waste must be disposed of at a registered waste disposal site.	Contractor	Disposal of hazardous waste at licensed waste disposal facilities	During the construction phase	ECO	Monthly	Disposal certificates of disposal at licensed facilities to be provided

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		must be undertaken as per the waste management plan				
– Certificates of safe disposal for general, hazardous, and recycled waste must be maintained.	Contractor	Obtain certificates for safe disposal of waste	During the construction phase	ECO	Monthly	Disposal certificates of disposal at licensed facilities to be provided and filed as part of the filing system

## 5.9 Protection of watercourses

**Impact management outcome:** Pollution and contamination of the watercourse environment and erosion are prevented.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– All watercourses must be protected from direct or indirect spills of pollutants such as sewage, cement, oils, fuels, chemicals, aggregate tailings, wash and contaminated water or organic material resulting from the Contractor's activities.	Contractor	Contractor to undertake activities which can cause spills of pollutants outside of watercourses	During the construction phase	cEO	Weekly	No incidents reported of spillage of pollutants into watercourses

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– In the event of a spill, prompt action must be taken to clear the polluted or affected areas.	Contractor and cEO	Develop a management plan or process for implementation should a spill take place	During the construction phase	cEO	Weekly	Feedback must be provided by the contractor in terms of how the spill was handled and photographic evidence of the feedback must be provided and kept on record
– Where possible, no development equipment must traverse any seasonal or permanent wetland.	cEO and Contractor	Ensure layout has been informed by the environmental sensitivities as determined by the basic assessment and specialist studies	Construction Phase	ECO	Once off review that the layout used is the approved one	Confirm no development equipment traverses any seasonal or permanent wetland as per the authorised layout by reviewing the as-built designs (once-off confirmation).
– Development of permanent watercourse crossing must only be undertaken where no alternative access to tower position is available.	cEO, Contractor	Ensure that permanent crossings (access roads) are provided for	During the construction phase	cEO	Weekly	Ensure that permanent crossings are developed if

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		access to the power line if no alternative crossing is available.				there is no alternative.
- There must not be any impact on the long-term morphological dynamics of watercourses.	DPM, cEO	Develop a management plan or process for implementation should a spill take place within a watercourse and ensure continuous monitoring	During the construction and operation phase	ECO, dEO	For all phases of the project life cycle (i.e. construction, operation, decommissioning)	No incidents reported of spillage of pollutants into watercourses
- Upgrading of Existing crossing points must be favoured over the creation of new crossings (including temporary access)".	DPM, cEO	Develop a management plan or process for implementation should a spill take place within a watercourse and ensure continually monitoring	During the pre-construction and construction phase	ECO, dEO	During the construction phase of the project.	Existing crossing points utilised as opposed to new ones created and no incidents reported of spillage of pollutants into watercourses

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<p>– When working in or near any watercourse, the following environmental controls and consideration must be taken:</p> <p>a) Water levels during the period of construction;</p> <p>b) Unless authorised, there should be no altering of the bed, banks, course or characteristics of a watercourse;</p> <p>c) During the execution of the works, appropriate measures to prevent pollution and contamination of the riparian environment must be implemented e.g. including ensuring that construction equipment is well maintained;</p> <p>d) Where earthwork is being undertaken in close proximity to any watercourse, slopes must be stabilised using suitable materials, i.e., sandbags or geotextile fabric, to prevent sand and rock from entering the channel; and</p> <p>e) Appropriate rehabilitation and re-vegetation measures for the watercourse banks must be implemented timeously. In this regard, the banks should be appropriately and incrementally stabilised as soon as development allows.</p>	Contractor	Activities undertaken near watercourses must be in-line with and consider the specified environmental controls	During the construction phase	ECO	Monthly, and as and when required	No degradation of the watercourses and no incidents of destruction reported



### 5.10 Vegetation clearing

**Impact management outcome:** Vegetation clearing is restricted to the authorised development footprint of the proposed infrastructure.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<b>General:</b>						
– Indigenous vegetation which does not interfere with the development must be left undisturbed.	cEO and contractor	Demarcate areas of indigenous vegetation to be avoided before clearance is undertaken	Construction and operation (i.e., for maintenance purposes)	ECO monthly, Operation and maintenance team weekly	Weekly, and as and when required	No unnecessary clearance of indigenous vegetation is undertaken
– Protected or endangered species may occur on or near the development site. Special care should be taken not to damage such species.	Contractor	Demarcate areas containing protected or endangered species to be avoided by construction activities	During the Construction Phase	ECO monthly and Operation and maintenance team weekly	Weekly, and as and when required	No clearance of protected or endangered species other than those permitted to be removed
– Search, rescue and replanting of all protected and endangered species likely to be damaged during project development must be identified by the relevant specialist and completed prior to any development or clearing.	Relevant specialist in consultation with the Contractor	Develop and implement a Plant Search and Rescue Plan	Pre-construction & Construction	cEO	Weekly, and as and when required	Implementation of the Plant Search and Rescue Plan and photographic evidence and notes of the implementation of the plan

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>Permits for removal must be obtained from the Department of Environment, Forestry and Fisheries (DEFF) prior to the cutting or clearing of the affected species, and they must be filed; and from the Department of Agriculture, Environmental Affairs, Rural Development and Land Reform for protected plants.</li> </ul>	DPM	Undertake the permitting process in order to obtain the relevant permits for the removal of protected species. Permits must be kept on file	Pre-construction	ECO	Once, prior to the commencement of the construction phase and removal of the protected species	DEFF permits on file
<ul style="list-style-type: none"> <li>The Environmental Audit Report must confirm that all identified species have been rescued and replanted and that the location of replanting is compliant with conditions of approvals.</li> </ul>	ECO	Ensure that the audit report indicates all species rescued and replanted and provides feedback in terms of compliance with the conditions of permits for replanting	During the Construction Phase and following the completion of the Construction Phase	ECO	Once off or as and when required	ECO confirmed rescued and replanted programme implemented correctly.
<ul style="list-style-type: none"> <li>Trees felled due to construction must be documented and form part of the Environmental Audit Report.</li> </ul>	ECO	Ensure that the audit report documents the details of trees felled	During the Construction Phase and following the completion of the Construction Phase	ECO	Once off or as and when required	ECO confirms documentation of trees felled

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Rivers and watercourses must be kept clear of felled trees, vegetation cuttings and debris.	Contractor	Felled trees, vegetation cuttings and debris must be disposed of at a licensed waste disposal facility	During the Construction Phase	ECO	Monthly	No felled trees, vegetation cuttings and debris are dumped in inappropriate locations and disposal certificates are available as proof of responsible disposal
– Only a registered pest control operator may apply herbicides on a commercial basis and commercial application must be carried out under the supervision of a registered pest control operator that is appropriately trained.	DPM and Contractor	A suitably qualified pest control operator must be appointed	Construction and Operation	ECO	As and when the use of herbicides is required	Only registered pest control operators must be appointed and proof of their registration must be provided
– A daily register must be kept of all relevant details of herbicide usage.	Contractor	Develop a daily register for the documentation of the details of herbicide usage	During the construction phase	ECO	Monthly	Daily register provided by the pest control operator

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>All protected species and sensitive vegetation not removed must be clearly marked and such areas fenced off in accordance to <b>Section 5.3: Access restricted areas.</b></li> </ul>	Contractor in consultation with the cEO	Spatially demarcate protected species and sensitive vegetation and implement appropriate fencing where required as per section 5.3	During the construction phase	ECO	Once, during the undertaking of the demarcation of the areas and the erection of the fencing	Demarcation and fencing is undertaken in-line with the requirements of section 5.3
<b>Servitude:</b>						
<ul style="list-style-type: none"> <li>Vegetation that does not grow high enough to cause interference with overhead transmission and distribution infrastructures, or cause a fire hazard to any plantation, must not be cut or trimmed unless it is growing in the road access area, and then only at the discretion of the Project Manager.</li> </ul>	Contractor in consultation with the DPM	Identify areas of vegetation not to be trimmed.	Construction and Operation	ECO Operation and maintenance team	Monthly	An indication of the areas where vegetation has not been trimmed or where vegetation has been removed from access roads must be provided.
<ul style="list-style-type: none"> <li>Where clearing for access purposes is essential, the maximum width to be cleared within the servitude must be in accordance to distance as agreed between the landowner and the EA holder.</li> </ul>	Contractor	Clearing for access must be undertaken as per the requirements provided by the	During the construction phase	ECO	Monthly, and as and when required	Proof must be provided that only agreed upon areas have been cleared

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		landowner and the EA holder				
– Alien invasive vegetation must be removed according to a plan (in line with relevant municipal and provincial procedures, guidelines and recommendations) and disposed of at a recognised waste disposal facility.	Contractor	Undertake removal of alien invasive vegetation in accordance with the relevant guideline relevant and ensure the vegetation is disposed of at a licensed waste disposal facility	Construction and Operation	ECO Operation and maintenance team	Monthly, and as and when required	Proof must be provided that alien invasive vegetation has been cleared in accordance to the relevant guideline and that the vegetation was disposed of at a licensed waste disposal facility
– Vegetation must be trimmed where it is likely to intrude on the minimum vegetation clearance distance (MVCD) or will intrude on this distance before the next scheduled clearance. MVCD is determined from SANS 10280.	Contractor	Develop a procedure for the trimming of vegetation in terms of the listed requirements	Construction and operation	ECO Operation and maintenance team	Monthly, and as and when required	Proof must be provided that vegetation is trimmed in accordance with the listed requirements
– Debris resulting from clearing and pruning must be disposed of at a recognised waste disposal facility, unless the landowners wish to retain the cut vegetation.	Contractor	Dispose of the debris in accordance with the waste management plan	Construction and operation	ECO Operation and maintenance team	Monthly, and as and when required	Proof must be provided that the debris has been disposed of at a licensed

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						waste disposal facility
– In the case of the development of new overhead transmission and distribution infrastructures, a one metre “trace-line” must be cut through the vegetation for stringing purposes only and no vehicle access must be cleared along the “ trace-line”. Alternative methods of stringing that limit impact to the environment must always be considered.	Contractor	Develop a procedure for the cutting of vegetation for stringing purposes	Pre-construction & Construction	ECO	Once, prior to the commencement of construction	Proof of implementation of the procedure for the cutting of vegetation for stringing purposes

### 5.11 Protection of fauna

**Impact management outcome:** Minimise disturbance to fauna and avifauna.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– No interference with livestock must occur without the landowner’s written consent and with the landowner or a person representing the landowner being present.	dEO / cEO Contractor	Develop a procedure for dealing with livestock within the affected properties	Pre-construction and during the construction phase	ECO	Once, prior to the commencement of construction and as and when required during the construction phase	Written consent provided by the landowner and proof of representation of the landowner during interference

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– The breeding sites of raptors and other wild bird species must be taken into consideration during the planning of the development programme.	dEO / cEO in consultation with the Contractor	Ensure that the planning and development programme considers breeding sites for wild bird species	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and as and when required	The planning and development programme includes the consideration of breeding sites for wild bird species
– Breeding sites must be kept intact and disturbance to breeding birds must be avoided. Special care must be taken where nestlings or fledglings are present.	dEO / cEO in consultation with the Contractor	Avoid breeding sites and ensure that special care is taken in the presence of nestlings and fledglings	During the Construction Phase Operation Phase	ECO monthly, cEO and Operation and maintenance team weekly	Weekly, and as an when required during the construction. Monthly, and as and when required during operation	Photographic record of intact breeding sites
– Nesting sites on existing parallel lines must be documented.	dEO / cEO in consultation with the ECO	Walk-downs of the existing lines located parallel to the project must be undertaken and nests and the details thereof documented	During the Construction Phase Operation Phase	ECO Operation and maintenance team	Quarterly, and as and when required	Details of walk-downs undertaken must be noted and kept on file and photographic records of nesting sites must be kept

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Special recommendations of the avian specialist must be adhered to at all times to prevent unnecessary disturbance of birds.	dEO / cEO in consultation with the Contractor	All mitigation measures recommended by the avifauna specialist must be implemented	During the Construction Phase Operation Phase	ECO Operation and maintenance team	Monthly during construction and monthly during operation	Photographic record of compliance and successful implementation of the recommended measures
– Bird guards and diverters must be installed on the new line as per the recommendations of the specialist.	dEO / cEO in consultation with the Contractor	Recommendations made by the specialist for the installation of bird guards and diverters must be adhered to and implemented as appropriate. Bird guards and diverters must be maintained	During the Construction Phase Operation Phase	ECO Operation and maintenance team	Monthly, and as and when required	Photographic record of implementation and maintenance of bird guards and diverters
– No poaching must be tolerated under any circumstances. All animal dens in close proximity to the works areas must be marked as Access restricted areas.	dEO / cEO in consultation with the Contractor	All site staff must be informed of this requirement during the Environmental Awareness Training and the consequences of not adhering	During the Construction Phase	ECO	Monthly, and as and when required	No instances of poaching is reported



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		to the requirement. These areas must be demarcated as Access Restricted Areas				
- No deliberate or intentional killing of fauna is allowed.	dEO / cEO in consultation with the Contractor	All site staff must be informed of this requirement during the Environmental Awareness Training and the consequences of not adhering to the requirement. These areas must be demarcated as Access Restricted Areas	During the Construction Phase	ECO	Monthly, and as and when required	No instances of deliberate or intentional killing is reported
- In areas where snakes are abundant, snake deterrents are to be deployed on the pylons to prevent snakes climbing up, being electrocuted and causing power outages.	dEO / cEO in consultation with the Contractor	Implement and maintain snake deterrents on pylons in areas where snakes are abundant	During the Construction Phase Operation Phase	ECO Operation and maintenance team	Once, during the construction of the pylons and as and when required. Monthly during operation	Photographic record of the implementation and maintenance of snake deterrents

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– No Threatened or Protected species (ToPs) and/or protected fauna as listed according NEMBA (Act No. 10 of 2004) and relevant provincial ordinances may be removed and/or relocated without appropriate authorisations/permits.	DPM in consultation with the dEO	Undertake a permitting process to obtain the required permits	Pre-construction	ECO	Once, prior to the commencement of construction and as and when required	Permits for removal and/relocation must be kept on file and be readily available

## 5.12 Protection of heritage resources

**Impact management outcome:** Minimise impact to heritage resources.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Identify, demarcate and prevent impact to all known sensitive heritage features on site in accordance with the No-Go procedure in Section 5.3: Access restricted areas.	DPM and a suitably qualified specialist  dEO / cEO in consultation with the Contractor and ECO	Spatially identify and demarcate areas of heritage significance as per the Heritage Impact Assessment and the Heritage Walk-through Report and as per the requirements of section 5.3	Pre-construction	ECO	Once, prior to the commencement of construction	Proof of avoidance of sensitive heritage features through details of avoidance and photographic records

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<p>– Carry out general monitoring of excavations for potential fossils, artefacts and material of heritage importance.</p>	<p>dEO (in consultation with specialists if/as required).</p>	<p>Ensure construction staff are adequately informed (via environmental awareness training) to carry out monitoring of excavations for fossils, artefacts and important heritage material</p>	<p>During the Construction Phase</p>	<p>ECO</p>	<p>Monthly, or as required</p>	<p>Environmental awareness training includes measures relating to monitoring for chance finds</p>
<p>– All work must cease immediately, if any human remains and/or other archaeological, palaeontological, and historical material are uncovered. Such material, if exposed, must be reported to the nearest museum, archaeologist/palaeontologist (or the South African Police Services), so that a systematic and professional investigation can be undertaken. Sufficient time must be allowed to remove/collect such material before development recommences.</p>	<p>dEO / cEO in consultation with the Contractor and ECO</p>	<p>Develop and implement procedures for situations where human remains, archaeological, palaeontological or historical material are uncovered</p>	<p>During the Construction Phase</p>	<p>ECO</p>	<p>As and when required</p>	<p>Proof of work ceased, and the required procedures followed in cases where material is discovered.</p>

### 5.13 Safety of the public

**Impact management outcome:** All precautions are taken to minimise the risk of injury, harm or complaints.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>Identify fire hazards, demarcate and restrict public access to these areas as well as notify the local authority of any potential threats e.g., large brush stockpiles, fuels etc.</li> </ul>	cEO in consultation with the Contractor	Develop an Emergency Preparedness, Response and Fire Management Plan specific to the project	Pre-construction Construction	cEO	Once, prior to the commencement of construction and weekly during the construction phase	Compliance with the Emergency Preparedness, Response and Fire Management Plan
<ul style="list-style-type: none"> <li>All unattended open excavations must be adequately fenced or demarcated.</li> </ul>	Contractor	Ensure that all excavations undertaken is fenced and demarcated within a reasonable timeframe and in instances where excavations will be open for long-periods of time	During the Construction Phase	cEO	Weekly	Excavations are fenced where required and photographic proof can be provided
<ul style="list-style-type: none"> <li>Adequate protective measures must be implemented to prevent unauthorised access to and climbing of partly constructed towers and protective scaffolding.</li> </ul>	Contractor	All staff must be easily identifiable, and the climbing of towers and	During the construction phase	ECO	Monthly, and as and when required	No incidents of unauthorised climbing is reported

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		scaffolding must only be undertaken by authorised personnel as managed by the Contractor				
– Ensure structures vulnerable to high winds are secured.	Contractor	Ensure that sufficient stabilisation measures are implemented to secure structures vulnerable to high winds	During the construction phase	cEO	Weekly, and as and when required	No incidents of unstable structures due to high winds is reported
– Maintain an incidents and complaints register in which all incidents or complaints involving the public are logged.	cEO	Compile and regularly update as incidents and complaints are submitted from the public and indicate the actions taken to resolve the complaint	During the construction phase	ECO	Monthly, and as and when required	The incidents and complaints register is complete and provides all the required details

## 5.14 Sanitation

**Impact management outcome:** Clean and well-maintained toilet facilities are available to all staff in an effort to minimise the risk of disease and impact to the environment.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Mobile chemical toilets are installed onsite if no other ablution facilities are available.	Contractor	Mobile chemical toilets must be placed appropriately and in areas that avoid environmental sensitivities	During the Construction Phase	cEO	Weekly	Mobile toilets are installed and avoid environmental sensitivities
– The use of ablution facilities and or mobile toilets must be used at all times and no indiscriminate use of the veld for the purposes of ablutions must be permitted under any circumstances.	Contractor in consultation with the cEO	All site staff must be informed of this requirement during the Environmental Awareness Training and the consequences of not adhering to the requirement.	Pe-construction & Construction	ECO	Monthly, and as and when required	No evidence of non-compliance identified
– Where mobile chemical toilets are required, the following must be ensured: a) Toilets are located no closer than 100 m to any watercourse or water body; b) Toilets are secured to the ground to prevent them from toppling due to wind or any other cause;	Contractor in consultation with the cEO	The installation of the toilets by the Contractor must be as per the listed requirements	During the Construction Phase	cEO	Weekly	No evidence of non-compliance identified

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>c) No spillage occurs when the toilets are cleaned or emptied and the contents are managed in accordance with the EMPr;</li> <li>d) Toilets have an external closing mechanism and are closed and secured from the outside when not in use to prevent toilet paper from being blown out;</li> <li>e) Toilets are emptied before long weekends and workers holidays, and must be locked after working hours; and</li> <li>f) Toilets are serviced regularly and the ECO must inspect toilets to ensure compliance to health standards.</li> </ul>						
<ul style="list-style-type: none"> <li>- A copy of the waste disposal certificates must be maintained.</li> </ul>	Contractor	Certificates obtained from the licensed waste disposal facility with the emptying of the toilets must be kept on file	During the Construction Phase	ECO	Monthly, and as and when required	Certificates for waste disposal from the licensed waste disposal facility available on site

### 5.15 Prevention of disease

**Impact Management outcome:** All necessary precautions linked to the spread of disease are taken.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Undertake environmentally friendly pest control in the camp area.	Contractor	Only environmentally friendly pest control must be used, when required	During the Construction Phase	ECO	As and when pest control is required for the project	Contractor to provide proof of pest control used being environmentally friendly
– Ensure that the workforce is sensitised to the effects of sexually transmitted diseases, especially HIV/ AIDS.	cEO / Contractor in consultation with the ECO	The effects of sexually transmitted diseases and HIV/ AIDS must be covered in the Environmental Awareness Training	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during construction	Environmental awareness training material requirements checklist
– The Contractor must ensure that information posters on HIV/ AIDS are displayed in the Contractor Camp area.	Contractor	Develop and place information posters on HIV/ AIDS	During the Construction Phase	cEO	Weekly	Photographic evidence of poster placement
– Information and education relating to sexually transmitted diseases to be made available to both construction workers and local community, where applicable.	cEO / Contractor in consultation with the ECO	Information and education of sexually transmitted diseases must	Pre-construction & Construction	ECO	Monthly	Environmental awareness training material requirements checklist



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		be covered in the Environmental Awareness Training.				
– Free condoms must be made available to all staff on site at central points.	Contractor	Placement of free condoms in mobile toilets and at the construction camps	During the Construction Phase	ECO	Monthly	Proof of placement of free condoms by the contractor to be provided
– Medical support must be made available.	dEO / cEO in consultation with the Contractor	Ensure that designated personnel with first aid training are available on site and that first aid kits to provide medical support is readily available	Construction and Operations	ECO	Monthly	Check the availability of first aid trained personnel and medical kits (including if these are complete in terms of supplies)
– Provide access to Voluntary HIV Testing and Counselling Services.	Contractor	Compile a HIV testing schedule and provide counselling services where required	During the Construction Phase	ECO	Quarterly, and as and when required	Voluntary testing schedules and proof of counselling (where undertaken)

### 5.16 Emergency procedures

**Impact management outcome:** Emergency procedures are in place to enable a rapid and effective response to all types of environmental emergencies.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Compile an Emergency Response Action Plan (ERAP) prior to the commencement of the proposed project.	Contractor	Develop an Emergency Preparedness, Response and Fire Management Plan specific to the project	Pre-construction	ECO	Once, prior to the commencement of construction	Emergency Preparedness, Response and Fire Management Plan compiled
– The Emergency Plan must deal with accidents, potential spillages, and fires in line with relevant legislation.	Contractor	Develop an Emergency Preparedness, Response and Fire Management Plan specific to the project which covers accidents, potential spillages and fires	Pre-construction	ECO	Once, prior to the commencement of construction	Emergency Preparedness, Response and Fire Management Plan includes required specifications
– All staff must be made aware of emergency procedures as part of environmental awareness training.	cEO / dEO in consultation with the ECO	Develop environmental awareness training material which covers	Pre-construction	ECO	Prior to the commencement of the environmental	Environmental awareness training material requirements checklist

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		the relevant emergency procedures			awareness training	
– The relevant local authority must be made aware of a fire as soon as it starts.	Contractor in consultation with the ECO	Develop and include a procedure in the Emergency Preparedness, Response and Fire Management Plan for the event of a fire and the procedure to be followed for informing the local authority	Construction	ECO	As and when a fire occurs	The local authority was informed as per the relevant procedure set out in the Emergency Preparedness, Response and Fire Management Plan
– In the event of emergency, necessary mitigation measures to contain the spill or leak must be implemented (see <b>Hazardous Substances section 5.17</b> ).	Contractor	Implement the required mitigation measures in the event of a spill or leak as per the requirements of Section 5.17.	Construction and Operations	ECO	As and when a spill or leak occurs	The mitigation measures included under Section 5.17 have been adhered to

### 5.17 Hazardous substances

**Impact management outcome:** Safe storage, handling, use and disposal of hazardous substances.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– The use and storage of hazardous substances to be minimised and non-hazardous and non-toxic alternatives substituted where possible.	cEO in consultation with the Contractor	Develop a strategy of how hazardous substances can be and should be minimised	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	Contractor to provide evidence of substances used for proof of compliance
– All hazardous substances must be stored in suitable containers as defined in the Method Statement.	Contractor	Develop a Method Statement for the storage of hazardous substances in suitable containers	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	Photographic proof that hazardous substances are stored in suitable containers as per the requirements of the relevant Method Statements
– Containers must be clearly marked to indicate contents, quantities, and safety requirements.	Contractor	Where hazardous waste is stored, these must be clearly marked indicating the	During the Construction Phase	ECO	Monthly	Photographic proof that containers are marked as per the requirements

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		required details of the contents				
– All storage areas must be bunded. The bunded area must be of sufficient capacity to contain a spill / leak from the stored containers.	Contractor	Ensure that storage areas are sufficiently bunded which are of sufficient capacity to contain a spill / leak from the stored containers	During the Construction Phase	ECO	Monthly during the Construction Phase	Photographic proof that storage areas are bunded and proof that the bund areas are of sufficient capacity to contain a spill / leak from the stored containers
– Bunded areas to be suitably lined with a SABS approved liner.	Contractor	Ensure that bunded storage areas are suitably lined	During the Construction Phase	ECO	Once, during the Construction Phase	Photographic proof that bunded storage areas are suitably lined
– An Alphabetical Hazardous Chemical Substance (HCS) control sheet must be drawn up and kept up to date on a continuous basis.	cEO / Contractor	Compile and update an Alphabetical Hazardous Chemical Substance (HCS) control sheet specific to the project	During the Construction Phase	ECO	Monthly, and as and when required	Complete and up to date control sheet provided by the Contractor

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
- All hazardous chemicals that will be used on site must have Material Safety Data Sheets (MSDS).	cEO / Contractor	Keep a record of all hazardous chemicals and the respective MSDS	During the Construction Phase	ECO	Monthly, and as and when required	Record of hazardous chemicals and the respective MSDS
- All employees working with HCS must be trained in the safe use of the substance and according to the safety data sheet.	cEO / Contractor	Provide training for personnel working with HCS	Pre-construction	ECO	Once, prior to the commencement of construction and as and when required	Record of training provided to personnel working with HCS
- Employees handling hazardous substances / materials must be aware of the potential impacts and follow appropriate safety measures. Appropriate personal protective equipment must be made available.	cEO / Contractor	Develop environmental awareness training material which covers the relevant impacts and safety measures.  Provide appropriate training and personal protective equipment for the relevant personnel handling hazardous	Pre-construction & Construction	ECO	Prior to the commencement of the environmental awareness training and monthly during the construction phase for personal protective equipment	Environmental awareness training material requirements checklist and all relevant personnel have undergone appropriate training and have access to personal protective equipment

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		substances and materials				
– The Contractor must ensure that diesel and other liquid fuel, oil and hydraulic fluid is stored in appropriate storage tanks or in bowzers.	Contractor	Appropriate storage facilities must be constructed or obtained for the storing of diesel, other liquid fuel, oil and hydraulic fluid	During the Construction Phase	ECO	Monthly, and as and when required	Storage tanks for the project are appropriate and no incidents are reported in this regard
– The tanks/ bowzers must be situated on a smooth impermeable surface (concrete) with a permanent bund. The impermeable lining must extend to the crest of the bund and the volume inside the bund must be 130% of the total capacity of all the storage tanks/ bowzers (110% statutory requirement plus an allowance for rainfall).	Contractor	Appropriate storage facilities must be constructed or obtained for tanks as per the requirements listed	During the Construction Phase	ECO	Monthly, and as and when required	Storage areas for the tanks/ bowzers for the project are appropriate and no incidents are reported in this regard
– The floor of the bund must be sloped, draining to an oil separator.	Contractor	Appropriate storage facilities must be constructed as per the requirements listed	During the Construction Phase	ECO	Once, during construction	Bunded storage areas are constructed according to the requirements

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Provision must be made for refuelling at the storage area by protecting the soil with an impermeable groundcover. Where dispensing equipment is used, a drip tray must be used to ensure small spills are contained.	Contractor	Appropriately constructed refuelling facility must be developed as per the requirements. Drip trays must be provided for use	During the Construction Phase	ECO cEO	Monthly Weekly	Soils at the refuelling facility are protected as required and drip trays are provided and used
– All empty externally dirty drums must be stored on a drip tray or within a bunded area.	Contractor	Ensure that empty dirty drums are stored appropriately as per the requirements	During the Construction Phase	ECO cEO	Monthly Weekly	Drip trays or bunded areas are used for the storage of dirty drums
– No unauthorised access into the hazardous substances storage areas must be permitted.	Contractor	Ensure through the implementation of procedures that no unauthorised access is undertaken into the storage areas	During the Construction Phase	ECO	Monthly	Proof of the implementation of the relevant procedure must be provided by the contractor
– No smoking must be allowed within the vicinity of the hazardous storage areas.	Contractor	Inform all employees of the requirement and develop	During the Construction Phase	ECO cEO	Monthly Weekly	Photographic record of the signage placed



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		and place relevant signage in the relevant areas				must be provided
– Adequate fire-fighting equipment must be made available at all hazardous storage areas.	Contractor	Hazardous storage areas must be fitted with adequate fire-fighting equipment	During the Construction Phase	ECO	Monthly	Adequate fire-fighting equipment is available and has been serviced
– Where refuelling away from the dedicated refuelling station is required, a mobile refuelling unit must be used. Appropriate ground protection such as drip trays must be used.	Contractor	Provide a mobile refuelling unit as well as suitable ground protection, where required	During the Construction Phase	ECO	Monthly, and as and when required	A mobile refuelling unit and suitable ground protection is available for use
– An appropriately sized spill kit kept onsite relevant to the scale of the activity/s involving the use of hazardous substance must be available at all times.	Contractor	Provide an appropriate spill kit for the project for the use of hazardous substances	During the Construction Phase	ECO	Monthly, and as and when required	Appropriate spill kits are available for use
– The responsible operator must have the required training to make use of the spill kit in emergency situations.	cEO and Contractor	Provide training on the use of spill kits to the relevant employees	Pre-construction	ECO	Once, prior to the commencement of construction	Proof of training to be provided by the contractor

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>- An appropriate number of spill kits must be available and must be located in all areas where activities are being undertaken.</li> </ul>	cEO and Contractor	Provide an appropriate number of spill kits in relevant areas	During the Construction Phase	ECO	Monthly	Proof of appropriate number of spill kits in appropriate areas to be provided by the contractor
<ul style="list-style-type: none"> <li>- In the event of a spill, contaminated soil must be collected in containers and stored in a central location and disposed of according to the National Environmental Management: Waste Act 59 of 2008. Refer to Section 5.7 for procedures concerning storm and wastewater management and 5.8 for solid and hazardous waste management.</li> </ul>	cEO and Contractor	Storage and disposal of contaminated soil must be in accordance with the National Environmental Management: Waste Act and sections 5.7 and 5.8 of this EMPr	During the Construction Phase	ECO	Monthly, and as and when required	<p>Proof of storage and disposal in terms of the National Environmental Management: Waste Act must be provided.</p> <p>Certificates of disposal at licensed waste disposal facilities must be provided</p>

### 5.18 Workshop, equipment maintenance and storage

**Impact management outcome:** Soil, surface water and groundwater contamination are minimised.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Where possible and practical all maintenance of vehicles and equipment must take place in the workshop area.	Contractor	Demarcate specific areas for the maintenance of vehicles and equipment	During the Construction Phase	ECO	Monthly	A dedicated area for the maintenance of vehicles and machinery is used.
– During servicing of vehicles or equipment, especially where emergency repairs are effected outside the workshop area, a suitable drip tray must be used to prevent spills onto the soil.	Contractor	Ensure that a drip tray is available for an emergency repair required	During the Construction Phase	ECO	Monthly	Contractor to provide evidence of drip tray use for emergency repairs
– Leaking equipment must be repaired immediately or be removed from site to facilitate repair.	Contractor	Ensure that where leaking equipment is identified it is repaired immediately or removed from site for repairs	During the Construction Phase	ECO	Monthly	Contractor to provide details of equipment repaired or removed from site
– Workshop areas must be monitored for oil and fuel spills.	cEO	Undertake regular inspections of the workshop areas for oil and fuel spills and	During the Construction Phase	ECO	Monthly	Register of inspection

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		keep an updated register of inspection on site				
– Appropriately sized spill kit kept onsite relevant to the scale of the activity taking place must be available.	Contractor	Provide an appropriate spill kit for the project	During the Construction Phase	ECO	Monthly, and as and when required	Appropriate spill kits are available for use
– The workshop area must have a bunded concrete slab that is sloped to facilitate runoff into a collection sump or suitable oil / water separator where maintenance work on vehicles and equipment can be performed.	Contractor	Ensure that the workshop area is sufficiently bunded in accordance with the required specification	During the Construction Phase	ECO	Once, during the Construction Phase and as and when required	Workshop area is bunded in accordance with the required specification
– Water drainage from the workshop must be contained and managed in accordance with Section 5.7: storm and wastewater management.	Contractor	Ensure that water drainage from workshop area is managed as per the requirements of section 5.7	During the Construction Phase	ECO	Monthly	Workshop drainage is managed in accordance with the requirements

## 5.19 Batching plants

**Impact management outcome:** Minimise spillages and contamination of soil, surface water and groundwater.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Concrete mixing must be carried out on an impermeable surface.	Contractor	Provide impermeable surface for the mixing of concrete	During the Construction Phase	cEO	Weekly	No concrete mixing is undertaken on open ground
– Batching plants areas must be fitted with a containment facility for the collection of cement laden water.	Contractor	Implement measures for the control and management of cement laden water	During the construction phase	cEO	Weekly	No mismanagement of laden water due to the temporary concrete batching plant
– Dirty water from the batching plant must be contained to prevent soil and groundwater contamination.	Contractor	Implement measures for the control and management of dirty water to prevent soil and groundwater contamination	During the construction phase	cEO	Weekly	No mismanagement of dirty water due to the temporary concrete batching plant and no/minimal soil and groundwater contamination
– Bagged cement must be stored in an appropriate facility and at least 10 m away from any water courses, gullies and drains.	Contractor	Demarcate and provide a storage area for	During the Construction Phase	cEO	Weekly	Photographic proof of bagged

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		bagged cement in-line with the listed requirements				cement stored within the demarcated area
– A washout facility must be provided for washing of concrete associated equipment. Water used for washing must be restricted.	Contractor	Provide a washout facility for the washing of associated equipment. Enforce limitations on water use for washing of equipment	During the Construction Phase	cEO	Weekly	No cement laden water is released into the environment. Only minimal water is used for washing
– Hardened concrete from the washout facility or concrete mixer can either be reused or disposed of at an appropriate licensed disposal facility.	Contractor	Make use of hardened concrete where possible or dispose of concrete in a suitable manner	During the Construction Phase	ECO	Monthly	Certificates of disposal of concrete at licensed waste disposal facility
– Empty cement bags must be secured with adequate binding material if these will be temporarily stored on site.	Contractor	Bind empty cement bags and temporarily store it in an appropriate area on site	During the Construction Phase	ECO	Monthly	Proof of binding of empty cement bags and storage in an appropriate area on site to be provided by the Contractor

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Sand and aggregates containing cement must be kept damp to prevent the generation of dust (Refer to Section 5.20: Dust emissions).	Contractor	Ensure that sand and aggregates are kept damp or otherwise protected from dust generation	During the Construction Phase	ECO	Monthly	Proof of dampening (or alternative dust suppression) of sand and aggregates must be provided by the Contractor
– Any excess sand, stone and cement must be removed or reused from site on completion of construction period and disposed at a registered disposal facility.	Contractor	Ensure that all excess sand, stone and cement is removed or reused	At the completion of the Construction Phase	ECO	Once, with the completion of construction	Certificates for the disposal of sand, stone and cement at licensed waste disposal facilities or proof of reuse must be provided
– Temporary fencing must be erected around batching plants in accordance with Section 5.5: Fencing and gate installation.	Contractor	Erect Temporary fencing	During the construction phase	cEO	Weekly	Temporary fencing around batching plants

## 5.20 Dust emissions

**Impact management outcome:** Dust prevention measures are applied to minimise the generation of dust.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Take all reasonable measures to minimise the generation of dust as a result of project development activities to the satisfaction of the ECO.	Contractor	Apply appropriate dust suppressant	During the Construction Phase	cEO	Weekly	Contractor to provide proof of use of appropriate dust suppressants
– Removal of vegetation must be avoided until such time as soil stripping is required, and similarly exposed surfaces must be re-vegetated or stabilised as soon as is practically possible.	Contractor	Proper planning for vegetation removal must be undertaken as well as for the associated rehabilitation	During the Construction Phase and Rehabilitation	cEO	Weekly	Plan for implementation must be provided by the Contractor
– Excavation, handling and transport of erodible materials must be avoided under high wind conditions or when a visible dust plume is present.	Contractor	Ensure that specific limitations are placed on the transport and handling of erodible materials during high wind conditions or when a visible dust plume is present	During the Construction Phase	cEO	Bi-weekly (every second week)	No complaints submitted in this regard



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– During high wind conditions, the ECO must evaluate the situation and make recommendations as to whether dust-damping measures are adequate, or whether working will cease altogether until the wind speed drops to an acceptable level.	ECO	ECO to provide adequate recommendations	During the Construction Phase	Not Applicable		
– Where possible, soil stockpiles must be located in sheltered areas where they are not exposed to the erosive effects of the wind.	Contractor	Place soil stockpiles in areas less affected by wind	During the Construction Phase	cEO and ECO	Bi-weekly (every second week) Monthly	Soil stockpiles are not exposed to wind and have not been eroded
– Where erosion of stockpiles becomes a problem, erosion control measures must be implemented at the discretion of the ECO.	Contractor in consultation with the ECO	Contractor to implement erosion control measures as recommended and agreed with the ECO	During the Construction Phase	cEO	Weekly, until erosion is no longer a problem	Recommendations made by the ECO have been implemented by the Contractor
– Vehicle speeds must not exceed 40 km/h along dust roads or 20 km/h when traversing unconsolidated and non-vegetated areas.	cEO / dEO / contractor	Inform all drivers of speed limits and place appropriate signage along the relevant roads	During the Construction Phase Operation Phase	ECO Operation and Maintenance team	Monthly	No complaints from community members are submitted
– Straw stabilisation must be applied at a rate of one bale/10 m <sup>2</sup> and harrowed into the top 100 mm of top material, for all completed earthworks.	Contractor	Ensure that straw stabilisation is undertaken as per the listed requirements	During the Construction Phase	ECO	Monthly	Photographic record of all straw stabilisation undertaken

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– For significant areas of excavation or exposed ground, dust suppression measures must be used to minimise the spread of dust.	Contractor	Appropriate dust suppressant measures are implemented	During the Construction Phase	cEO	Weekly	Photographic record of measures being implemented and the results thereof

### 5.21 Blasting

**Impact management outcome:** Impact to the environment is minimised through a safe blasting practice.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Any blasting activity must be conducted by a suitably licensed blasting contractor.	Not Applicable – no blasting proposed.					
– Notification of surrounding landowners, emergency services site personnel of blasting activity 24 hours prior to such activity taking place on Site.	Not Applicable – no blasting proposed.					

### 5.22 Noise

**Impact Management outcome:** Unnecessary noise is prevented by ensuring that noise from construction activities is mitigated.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– The Contractor must keep noise level within acceptable limits. Restrict the use of sound amplification equipment for communication and emergency only.	Contractor	Ensure that noise limits do not exceed acceptable limits and avoid the use of amplification communication	During the Construction Phase	ECO	Monthly, and as and when required	No complaints registered in this regard. No amplification equipment is used.
– All vehicles and machinery must be fitted with appropriate silencing technology and must be properly maintained.	Contractor	Provide and implement silencing technology	During the Construction Phase	ECO	Monthly, and as and when required	No complaints registered in this regard. Silencing technology is utilised.
– Any complaints received by the Contractor regarding noise must be recorded and communicated. Where possible or applicable, provide transport to and from the site on a daily basis for construction workers.	cEO	Update complaints register. Provide daily transport to and from site for employees	During the Construction Phase	ECO	Monthly, and as and when required	Complaints register provided by the cEO and proof of transportation services provided
– Develop a Code of Conduct for the construction phase in terms of behaviour of construction staff. Operating hours as determined by the environmental authorisation are adhered to during the development phase. Where not defined, it must be ensured that development activities must still meet the impact management outcome related to noise management.	cEO and Contractor in consultation with the ECO	Compile a Code of Conduct for staff. Appropriate operating hours must be identified for the project.	Pre-construction and Construction	ECO	Once, prior to the commencement of construction	No complaints registered in this regard.

### 5.23 Fire prevention

**Impact management outcome:** Prevention of uncontrollable fires.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Designate smoking areas where the fire hazard could be regarded as insignificant.	cEO	Identify and demarcate through signage designated smoking areas	Pre-construction & Construction	ECO	Monthly	Photographic record of designated smoking area
– Firefighting equipment must be available on all vehicles located on site.	cEO / dEO in consultation with the Contractor	Provide all vehicles with firefighting equipment	Construction	ECO	Monthly	All vehicles are fitted with firefighting equipment and the details thereof are provided by the cEO
– The local Fire Protection Agency (FPA) must be informed of construction activities.	cEO in consultation with the ECO	Undertake formal consultation to inform the local FPA of the associated construction activities	Pre-construction	ECO	Once, during the commencement of the Construction Phase	Proof of consultation with the FPA
– Contact numbers for the FPA and emergency services must be communicated in environmental awareness training and displayed at a central location on site.	dEO / cEO / Contractor in	Develop environmental awareness	Pre-construction & Construction	ECO	Prior to the commencement of the	Environmental awareness training material

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
	consultation with the ECO	<p>training material which covers the contact numbers for the FPA and emergency services.</p> <p>Place the contact numbers for the FPA and emergency services at a visible and central location</p>			environmental awareness training and once during the construction phase	requirements checklist and photographic record of contact numbers on display
- Two-way swop of contact details between ECO and FPA.	ECO	Consultation between the ECO and FPA to exchange contact details	Pre-construction	Not Applicable		

#### 5.24 Stockpiling and stockpile areas

**Impact management outcome:** Erosion and sedimentation as a result of stockpiling are reduced.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– All material that is excavated during the project development phase (either during piling (if required) or earthworks) must be stored appropriately on site in order to minimise impacts to watercourses, wetlands and water bodies.	Contractor	Identify and demarcate an appropriate location for the storage of excavated materials	Pre-construction & Construction	ECO	Monthly	Excavated material is not stored within sensitive environmental areas
– All stockpiled material must be maintained and kept clear of weeds and alien vegetation growth by undertaking regular weeding and control methods.	Contractor	Implement appropriate and sufficient maintenance on stockpiled material regularly	During the Construction Phase	cEO ECO	Bi-weekly (every second month) Monthly	Stockpiled material is maintained sufficiently and is clear of weeds and alien vegetation
– Topsoil stockpiles must not exceed 2 m in height.	Contractor	Enforce limitations for the height of topsoil stockpiles	During the Construction Phase	cEO ECO	Bi-weekly (every second month) Monthly	Topsoil stockpiles do not exceed 2m in height
– During periods of strong winds and heavy rain, the stockpiles must be covered with appropriate material (e.g., cloth, tarpaulin etc.).	Contractor	Appropriate material must be provided in order to cover stockpiles when required	During the Construction Phase	ECO	Monthly	Contractor to provide proof of availability of appropriate material to cover stockpiles when required
– Where possible, sandbags (or similar) must be placed at the bases of the stockpiled material in order to prevent erosion of the material.	Contractor	Sandbags must be provided in order to prevent erosion of	During the Construction Phase	ECO	Monthly	Contractor to provide proof of availability of sandbags to prevent erosion

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		stockpiled materials				of stockpiled materials

### 5.25 Finalising tower positions

**Impact management outcome:** No environmental degradation occurs as a result of the survey and pegging operations.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– No vegetation clearing must occur during survey and pegging operations.	Contractor	Implement restrictions in terms of vegetation clearing during the survey and pegging operations	Pre-construction	cEO	Weekly	Contractor to provide photographic proof that no vegetation has been cleared
– No new access roads must be developed to facilitate access for survey and pegging purposes.	Contractor	Restrict the development of new access roads for survey and pegging purposes	Pre-construction	cEO	Weekly	Contractor to provide photographic proof that no new roads have been developed
– Project manager, botanical specialist and contractor to agree on final tower positions based on survey within assessed and approved areas.	DPM, Suitably Qualified	Undertake consultation between the	Pre-construction	ECO	Once the final tower positions have been	Provision of final tower positions to the ECO

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
	Specialist and Contractor	relevant responsible people and finalise the tower positions for the power line			finalised and agreed upon	
– The surveyor is to demarcate (peg) access roads/tracks in consultation with ECO. No deviations will be allowed without the prior written consent from the ECO.	Surveyor in consultation with the ECO	Undertake consultation between the surveyor and the ECO	Pre-construction	cEO	Weekly	Consultation with the ECO regarding the distribution of pegs.

### 5.26 Excavation and Installation of foundations

**Impact management outcome:** No environmental degradation occurs as a result of excavation or installation of foundations.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– All excess spoil generated during foundation excavation must be disposed of in an appropriate manner and at a recognised disposal site, if not used for backfilling purposes.	Contractor	Use a licensed waste disposal facility for the disposal of excess spoil	During the Construction Phase	ECO	Monthly	Certificates obtained for the disposal of excess spoil at a licensed waste disposal facility
– Spoil can however be used for landscaping purposes and must be covered with a layer of 150 mm topsoil for rehabilitation purposes.	Contractor	Spoil used for landscaping must be applied	Construction and Rehabilitation	ECO	Monthly	Photographic record of spoil used for



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		as per the listed requirements				landscaping purposes as well as feedback from the contractor
– Management of equipment for excavation purposes must be undertaken in accordance with Section 5.18: Workshop equipment maintenance and storage.	Contractor	Undertake the management of equipment for excavation as per the requirements of section 5.18	During the Construction Phase	ECO	Monthly	Management of equipment is undertaken in line with the requirements of section 5.18
– Hazardous substances spills from equipment must be managed in accordance with Section 5.17: Hazardous substances.	Contractor	Undertake the management of hazardous substances spills from equipment as per the requirements of section 5.17	During the Construction Phase	ECO	Monthly	Management of hazardous substances spills from equipment is undertaken in line with the requirements of section 5.17
– Batching of cement to be undertaken in accordance with Section 5.19: Batching plants.	Contractor	Ensure correct batching of cement	During the construction phase	cEO	Weekly	Measures in place to ensure the batching of cement is done in accordance with Section 5.19: Batching plants

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Residual cement must be disposed of in accordance with Section 5.8: Solid and hazardous waste management.	Contractor	Undertake the disposal of residual cement as per the requirements of section 5.8	During the Construction Phase	ECO	Monthly	The disposal of residual cement is undertaken in line with section 5.8.

### 5.27 Assembly and erecting towers

**Impact management outcome:** No environmental degradation occurs as a result of assembly and erecting of towers.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Prior to erection, assembled towers and tower sections must be stored on elevated surfaces (suggest wooden blocks) to minimise damage to the underlying vegetation.	Contractor	Provide the necessary materials for the elevated surface, where towers are to be placed on indigenous vegetation	During the Construction Phase	cEO	Weekly	Implementation of elevated surface and photographic record thereof
– In sensitive areas, tower assembly must take place off-site or away from sensitive positions.	Contractor in consultation with the cEO and the ECO	Identify sensitive areas to be avoided by tower assembly and ensure that	Pre-construction & Construction	cEO	Weekly	Tower assembly is undertaken outside of sensitive areas

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		the areas are not infringed upon				
– The crane used for tower assembly must be operated in a manner which minimises impact to the environment.	Contractor in consultation with the cEO and the ECO	Ensure that no impact to the environment is imposed during the operation of the crane	Pre-construction & Construction	cEO	Weekly	No environmental damages incurred as a result of the crane.
– The number of crane trips to each site must be minimised.	Contractor in consultation with the cEO and the ECO	Ensure that the utilisation of the crane is maximised when on site.	Pre-construction & Construction	cEO	Weekly	Few crane trips to each site observed.
– Wheeled cranes must be utilised in preference to tracked cranes. However, Rocky terrain may require tracked cranes in the project site.	Contractor	Ensure wheeled cranes are utilised, where practical.	Pre-construction & Construction	cEO	Weekly	Wheeled cranes observed on site.
– Consideration must be given to erecting towers by helicopter or by hand where it is warranted to limit the extent of environmental impact.	Contractor	Contractor to undertake erecting of towers in an environmentally acceptable manner	During the Construction Phase	ECO	Monthly	No unacceptable environmental impacts occur with the erecting of the towers
– Access to tower positions to be undertaken in accordance with access requirements specified in <b>Section 5.4: Access Roads.</b>	Contractor	Undertake access to tower positions as per the	During the Construction Phase	ECO	Monthly	Access to tower positions are undertaken as per the

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		requirements of section 5.4				requirements of section 5.4
- Vegetation clearance to be undertaken in accordance with general vegetation clearance requirements specified in <b>Section 5.10: Vegetation clearing</b> .	Contractor	Undertake vegetation clearance as per the requirements of section 5.10	During the Construction Phase	cEO	Weekly	Vegetation clearance is undertaken as per the requirements of section 5.10
- No levelling at tower sites must be permitted unless approved by the Development Project Manager or Developer Site Supervisor.	Contractor in consultation with the DPM and DSS	Written permission for levelling at tower sites, if required, must be obtained from the DPM and DSS prior to the undertaking of any levelling activities	During the Construction Phase	ECO	Monthly, and as and when required	Written permission from the DPM and DSS provided to the Contractor
- Topsoil must be removed separately from subsoil material and stored for later use during rehabilitation of such tower sites.	Contractor	Implement appropriate measures to ensure that topsoil is removed from subsoil material	Construction and Rehabilitation	cEO	Weekly, and as and when required	Proof of appropriate measures implemented must be provided by the Contractor
- Topsoil must be stored in heaps not higher than 2m to prevent destruction of the seed bank within the topsoil.	Contractor	Implement the listed requirements for	During the Construction Phase	cEO	Weekly	Topsoil is stored as per the listed requirements

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		the storage of topsoil				
– Excavated slopes must be no greater than 1:3, but where this is unavoidable, appropriate measures must be undertaken to stabilise the slopes.	Contractor	Implement the listed requirements for the excavation of slopes	During the Construction Phase	cEO	Weekly	Excavation of slopes is undertaken as per the listed requirements
– Fly rock from blasting activity must be minimised and any pieces greater than 150 mm falling beyond the Working Area, must be collected and removed.	cEO / dEO / contractor	Ensure all pieces greater than 150 mm falling beyond the Working Area, are collected and removed and implement measures to try and minimise fly rock from blasting activity	Pre-Construction Phase	ECO/EO	During blasting activities	ECO/EO to confirm necessary measures have been undertaken to minimise fly rock from blasting activity and that no pieces greater than 150 mm are beyond the working area.
– Only existing disturbed areas are utilised as spoil areas.	Contractor in consultation with the ECO	Identify, demarcate and use existing disturbed areas for spoil areas	Pre-construction & Construction	cEO	Weekly	Only identified disturbed areas are used as spoil areas
– Drainage is provided to control groundwater exit gradient with the spill areas such that migration of fines is kept to a minimum.	Not Applicable					

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Surface water runoff is appropriately channelled through or around spoil areas.	DPM and Contractor	Design and implement appropriate surface runoff measures for spoil areas	Pre-construction & Construction	ECO	Once, during the construction of the surface runoff measures	Implementation of surface runoff measures through and/or around spoil areas
– During backfilling operations, care must be taken not to dump the topsoil at the bottom of the foundation and then put spoil on top of that.	Contractor	Develop and implement backfilling procedures which ensures that topsoil is not placed at the bottom of foundations.	Pre-construction & Construction	cEO	Weekly	Backfilling operations are undertaken as per the procedures developed
– The surface of the spoil is appropriately rehabilitated in accordance with the requirements specified in Section 5.29: Landscaping and rehabilitation.	Contractor	Rehabilitation of the surface spoil must be undertaken in accordance with the requirements of section 5.29	Rehabilitation	cEO	Weekly	Rehabilitation of the surface spoil is undertaken as per the requirements of section 5.29
– The retained topsoil must be spread evenly over areas to be rehabilitated and suitably compacted to effect re-vegetation of such areas to prevent erosion as soon as construction activities on the site is complete. Spreading of topsoil must not be undertaken, where possible, at the beginning of the dry season.	Contractor	Ensure that topsoil is spread evenly and compacted appropriately. This must be undertaken	Rehabilitation	cEO	Weekly	Proof that topsoil has been spread evenly and compacted correctly must be provided by

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		outside of the start of the dry season, where possible				the Contractor/cEO. Proof that the activities were undertaken outside of the start of the dry season (or motivation as to why this was not possible) must be provided by the Contractor

### 5.28 Stringing

**Impact management outcome:** No environmental degradation occurs as a result of stringing.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Where possible, previously disturbed areas must be used for the siting of winch and tensioner stations. In all other instances, the siting of the winch and tensioner must avoid Access restricted areas and other sensitive areas.	Contractor in consultation with the ECO	Identify and demarcate areas appropriate for the siting of winch and tensioner	Pre-construction & Construction	cEO	Weekly	Winch and tensioner stations are located outside of identified sensitive areas

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		stations which does not infringe on access restricted areas or environmentally sensitive areas				
– The winch and tensioner station must be equipped with drip trays in order to contain any fuel, hydraulic fuel or oil spills and leaks.	Contractor	Provide sufficient drip trays	During the Construction Phase	cEO	Weekly	Sufficient drip trays are available for the winch and tensioner stations and no spills occur
– Refuelling of the winch and tensioner stations must be undertaken in accordance with <b>Section 5.17: Hazardous substances.</b>	Contractor	The refuelling of winch and tensioner stations must be undertaken as per the requirements of section 5.17	During the Construction Phase	ECO	Monthly	The refuelling of winch and tensioner stations is undertaken as per the requirements of section 5.17
– In the case of the development of overhead transmission and distribution infrastructure, a one metre "trace-line" may be cut through the vegetation for stringing purposes only and no vehicle access must be cleared along "trace-lines". Vegetation clearing must be undertaken by hand, using chainsaws and handheld implements, with vegetation being cut off at	Contractor	Develop and implement procedures for implementation for vegetation clearing during stringing in line	Pre-construction & Construction	ECO and cEO weekly during stringing	Once, prior to the commencement of construction and weekly during stringing	Implementation of the procedures put in place and proof thereof from the Contractor



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
ground level. No tracked or wheeled mechanised equipment must be used.		with the specification.				
– Alternative methods of stringing which limit impact to the environment must always be considered e.g. by hand or by using a helicopter.	Contractor	Identify and implement the stringing method with the least environmental impact	During the Construction Phase	cEO	Weekly	Implementation of identified method of stringing with the least environmental impact
– Where the stringing operation crosses a public or private road or railway line, the necessary scaffolding/ protection measures must be installed to facilitate access. If, for any reason, such access has to be closed for any period(s) during development, the persons affected must be given reasonable notice, in writing.	Contractor	Identify prior to construction areas where protection measures will be required during stringing. Where access is to be restricted timeous written notice must be provided to the affected parties	Pre-construction & Construction	ECO	Monthly, and as and when required	Proof of implementation of protection measures and proof of written notice to affected parties must be provided by the Contractor
– No services (electrical distribution lines, telephone lines, roads, railways lines, pipelines fences etc.) must be damaged because of stringing operations. Where disruption to services is unavoidable, persons affected must be given reasonable notice, in writing.	Contractor in consultation with the cEO, DPM and dEO	Avoid the damaging or disturbance of existing services. Where services will be disrupted timeous notice must be	During the Construction Phase	ECO	Monthly, and as and when required	No disruption of services occurs. Where disruption occurs proof of written notice to affected parties must be

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		provided to the affected parties				provided by the Contractor
– Where stringing operations cross cultivated land, damage to crops is restricted to the minimum required to conduct stringing operations, and reasonable notice (10 work days minimum), in writing, must be provided to the landowner.	Not Applicable					
– Necessary scaffolding protection measures must be installed to prevent damage to the structures supporting certain high value agricultural areas such as vineyards, orchards, nurseries.	Not Applicable					

## 5.29 Socio-economic

**Impact management outcome:** Socio-economic development is enhanced.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Develop and implement communication strategies to facilitate public participation.	dEO / cEO	Identify and implement appropriate strategies for communication with the	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction	Communication is undertaken as per the identified strategies and no complaints

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		communities through consideration of the community needs				are submitted regarding communication
– Develop and implement a collaborative and constructive approach to conflict resolution as part of the external stakeholder engagement process.	Contractor	Development and implement a Grievance Mechanism which considers the community needs and provides procedures for conflict resolution	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	Conflict resolution is undertaken in line with the requirements of the Grievance Mechanism. No complaints on conflict resolution is submitted by the community
– Sustain continuous communication and liaison with neighbouring owners and residents.	Contractor	Development and implement a Grievance Mechanism that provides procedures for communication / liaison with neighbouring landowners and residents	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	Communication / liaison with neighbouring landowners and residents are undertaken in line with the requirements of the Grievance Mechanism. No complaints on communication with

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						neighbouring landowners and residents is submitted
– Create work and training opportunities for local stakeholders.	Contractor	Develop and implement a “locals first” policy for the provision of employment opportunities	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	The “locals first” policy is considered in terms of the employment and training opportunities
– Where feasible, no workers, with the exception of security personnel, must be permitted to stay overnight on the site. This would reduce the risk to local farmers.	Not applicable –no on-site housing is envisaged with daily commute to and from site expected of construction staff.					

### 5.30 Temporary closure of site

**Impact management outcome:** Minimise the risk of environmental impact during periods of site closure greater than five days.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Bunds must be emptied (where applicable) and need to be undertaken in accordance with the impact management actions included in <b>sections 5.17: management of hazardous substances</b> and <b>5.18 workshop, equipment maintenance and storage</b> .	Contractor	Regular emptying of the bunds must be undertaken. This must be	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Bunds are emptied as per the requirements listed under

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		undertaken as per the requirements listed in sections 5.17 and 5.18				sections 5.17 and 5.18
- Hazardous storage areas must be well ventilated.	Contractor	Install appropriate ventilation in all hazardous storage areas	During the construction phase	ECO	Prior to site closure for more than 05 days	Effective ventilation is installed in hazardous storage areas
- Fire extinguishers must be serviced and accessible. Service records to be filed and audited at last service.	Contractor / cEO	Ensure fire extinguishers are serviced, as required and are easily accessible with appropriate signage indicating location. Ensure service records are kept up to date and filed	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Signage placed indicating location of fire extinguishers and service records
- Emergency and contact details must be displayed.	Contractor / cEO	Place emergency and contact details which are readily available and easily accessible	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Photographic proof of contact details on display

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Security personnel must be briefed and have the facilities to contact or be contacted by relevant management and emergency personnel.	Contractor in consultation with the ECO	Hold a workshop with all security personnel to provide a brief of the project and security requirements. Provide facilities in order to contact management and emergency personnel	Pre-construction & construction	ECO	Prior to site closure for more than 05 days	Proof of the workshop held must be kept on file by the contractor.
– Night hazards such as reflectors, lighting, traffic signage etc. must have been checked.	Contractor	Regular checks of night hazards must be undertaken	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Proof of checks of night hazards must be provided by the contractor
– Fire hazards identified and the local authority must have been notified of any potential threats e.g., large brush stockpiles, fuels etc.	cEO / Contractor in consultation with the ECO	Identify any potential fire hazards and notify the relevant local authority	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Proof of notification of the fire hazards to the local authority must be provided by the Contractor
– Structures vulnerable to high winds must be secured.	Contractor	Ensure structures vulnerable to wind are secure prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Structures vulnerable to wind are secured prior to site closure

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
- Wind and dust mitigation must be implemented.	Contractor	Implement wind and dust mitigation prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Wind and dust mitigation is implemented prior to site closure
- Cement and materials stores must have been secured.	Contractor	Ensure cement and material stores are secured prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Cement and material stores are secured prior to site closure
- Toilets must have been emptied and secured.	Contractor	Ensure toilets are emptied and secured prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Toilets are emptied and secured prior to site closure
- Refuse bins must have been emptied and secured.	Contractor	Ensure refuse bins are emptied and secured prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	refuse bins are emptied and secured prior to site closure
- Drip trays must have been emptied and secured.	Contractor	Ensure drip trays are emptied and secured prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Drip trays are emptied and secured prior to site closure

### 5.31 Landscaping and rehabilitation

**Impact management outcome:** Areas disturbed during the development phase are returned to a state that approximates the original condition.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– All areas disturbed by construction activities must be subject to landscaping and rehabilitation; All spoil and waste must be disposed to a registered waste site and certificates of disposal provided.	Contractor	Develop and implement a rehabilitation plan for the rehabilitation of all disturbed areas.  Dispose of all spoil and waste at a licensed waste disposal facility	Pre-construction & Rehabilitation	cEO	Weekly	Rehabilitation of the disturbed areas is undertaken as per the rehabilitation plan. All certificates of waste disposal at licensed facilities are available.
– All slopes must be assessed for contouring, and to contour only when the need is identified in accordance with the Conservation of Agricultural Resources Act, No 43 of 1983.	Contractor in consultation with the ECO	Assess all slopes and determine whether contouring is required	Rehabilitation	cEO	Weekly	All slopes are assessed and contoured as required
– All slopes must be assessed for terracing, and to terrace only when the need is identified in accordance with the Conservation of Agricultural Resources Act, No 43 of 1983.	Contractor in consultation with the ECO	Assess all slopes and determine whether	Rehabilitation	cEO	Weekly	All slopes are assessed and terraced as required



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		terracing is required				
– Berms that have been created must have a slope of 1:4 and be replanted with indigenous species and grasses that approximates the original condition.	Contractor	Ensure all berms have a slope of 1:4 and is replanted with indigenous species and grasses	Rehabilitation	cEO	Weekly	All berms have a slope of 1:4 and is replanted with indigenous species and grasses
– Where new access roads have crossed cultivated farmlands, that lands must be rehabilitated by ripping which must be agreed to by the holder of the EA and the landowners.	Not applicable					
– Rehabilitation of tower sites and access roads outside of farmland.						
– Indigenous species must be used for with species and/grasses to where it compliments or approximates the original condition.	Contractor	Make use of indigenous species for rehabilitation	Rehabilitation	cEO	Weekly	Indigenous species are used for rehabilitation
– Stockpiled topsoil must be used for rehabilitation (refer to <b>Section 5.24: Stockpiling and stockpiled areas</b> ).	Contractor	Ensure stockpiled topsoil is used as per the requirements listed under section 5.24	Rehabilitation	cEO	Weekly	Stockpiled topsoil is used as per the requirements listed under section 5.24
– Stockpiled topsoil must be evenly spread so as to facilitate seeding and minimise loss of soil due to erosion.	Contractor	Ensure that topsoil is spread evenly	Rehabilitation	cEO	Weekly	Topsoil is spread evenly

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Before placing topsoil, all visible weeds from the placement area and from the topsoil must be removed.	Contractor	Remove all visible weeds from placement area and topsoil before spreading the topsoil	Rehabilitation	cEO	Weekly	No weeds are visible in the placement area or the topsoil
– Subsoil must be ripped before topsoil is placed.	Contractor	Undertake the ripping of subsoil prior to the spreading of topsoil	Rehabilitation	cEO	Weekly	Subsoil is ripped before topsoil is placed
– The rehabilitation must be timed so that rehabilitation can take place at the optimal time for vegetation establishment.	Contractor	Plan the timeframe for rehabilitation in order to undertake vegetation planting during the optimal time for vegetation establishment	Rehabilitation	ECO	At the start of rehabilitation to confirm correct timeframe	Rehabilitation is undertaken during the optimal time
– Where impacted through construction related activity, all sloped areas must be stabilised to ensure proper rehabilitation is effected and erosion is controlled.	Contractor	All disturbed slope areas must be stabilised	Rehabilitation	cEO	Weekly	Disturbed slopes are stabilised sufficiently
– Sloped areas stabilised using design structures or vegetation as specified in the design to prevent erosion of embankments. The contract design	Contractor	Stabilise slopes as per the design specifications	Pre-construction & Rehabilitation	cEO	Weekly	Slopes are stabilised as per the design specifications

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
specifications must be adhered to and implemented strictly.						
– Spoil can be used for backfilling or landscaping as long as it is covered by a minimum of 150 mm of topsoil.	Contractor	Spoil used for landscaping must be applied as per the listed requirements	Rehabilitation	cEO	Weekly	Photographic record of spoil used for landscaping purposes as well as feedback from the contractor
– Where required, re-vegetation including hydro-seeding can be enhanced using a vegetation seed mixture as described below. A mixture of seed can be used provided the mixture is carefully selected to ensure the following: a) Annual and perennial plants are chosen; b) Pioneer species are included; c) Species chosen must be indigenous to the area with the seeds used coming from the area; d) Root systems must have a binding effect on the soil; and e) The final product must not cause an ecological imbalance in the area.	Contractor in consultation with a suitably qualified specialist	Make use of a suitable vegetation seed mixture should enhancement be required	Rehabilitation	ECO	As and when required	Use of a suitable vegetation seed mixture if required

## **6 ACCESS TO THE GENERIC EMPr**

Once completed and signed, to allow the public access to the generic EMPr, the holder of the EA must make the EMPr available to the public in accordance with the requirements of regulation 26(h) of the EIA Regulations.

**PART B: SECTION 2**

**7 SITE SPECIFIC INFORMATION AND DECLARATION**

**7.1 Sub-section 1: contact details and description of the project**

7.1.1 Details of the applicant:

<b>Applicant Name</b>	<b>Energy Team (Pty) Ltd</b>
<b>Contact Person</b>	Thomas Condesse
<b>Physical Address</b>	Ground Floor, Sable Corner, 15 Bridgeway Road, Bridgeways Precinct, Century City, 7441
<b>Postal Address</b>	Ground Floor, Sable Corner, 15 Bridgeway Road, Bridgeways Precinct, Century City, 7441
<b>Telephone</b>	+33 6 22 66 59 32
<b>Fax</b>	N/A
<b>Cell</b>	+33 6 22 66 59 32
<b>Email Address</b>	Thomas.condesse@energyteam.co.za

7.1.2 Details and expertise of the EAP:

<b>EAP Name</b>	<b>Karen Jodas</b>
<b>EAP Qualifications</b>	M.Sc in Geography (Geomorphology), Rhodes University, Grahamstown, 1996
<b>Professional Affiliation/Registration</b>	South Africa Council of Natural Scientific Professions - 400106/99 Environmental Assessment Practitioners Association of South Africa – 2022/5499
<b>Physical Address</b>	First floor, Block 2 5 Woodlands Drive Office Park C/o Woodlands Drive & Western Service Road Woodmead Johannesburg 2191
<b>Telephone</b>	011 656 3237
<b>Fax</b>	086 684 0547

<b>Cell</b>	082 655 1935
<b>Email Address</b>	<a href="mailto:Karen@savannahsa.com">Karen@savannahsa.com</a>

### 7.1.3 Project Details

**Project name:** Kleinzee Solar PV Facility and Associated Grid Connection Infrastructure, Northern Cape Province

### 7.1.4 Project Description

The development of a solar photovoltaic (PV) facility with a generating capacity of up to 200MW is proposed by Energy Team (Pty) Ltd on a site located located approximately 20km west of the town of Komaggas, and 28km southeast of Kleinsee. The project is located in the Nama Khoi Local Municipality within the Namakwa District Municipality, Northern Cape. The solar PV development will be known as the Kleinzee Solar PV Facility. The Kleinzee Solar PV Facility is located within Focus Area 8 of the Renewable Energy Development Zones (REDZ), which is known as the Springbok REDZ, and within the Northern Corridor of the Strategic Transmission Corridors.

The infrastructure associated with the 200MW solar PV facility will include:

- » Solar PV array comprising PV modules and mounting structures
- » Inverters and transformers
- » Low voltage cabling between the PV modules to the inverters
- » 33kV cabling between the project components and the facility substation
- » 132kV onsite facility substation
- » 132kV power line to connect to the grid at Zonnequa Collector Substation within a 300m wide and 8.5km long corridor
- » Battery Energy Storage System (BESS)
- » Site offices and maintenance buildings, including workshop areas for maintenance and storage
- » Laydown areas
- » Site access and internal roads.

The power generated by Kleinzee Solar PV Facility will be sold to Eskom and will feed into the national electricity grid. Ultimately, Kleinzee Solar PV facility and the associated grid connection infrastructure is intended to be part of the renewable energy projects portfolio for South Africa, as contemplated in the Integrated Resources Plan (IRP) and Renewable Energy Independent Power Producer Procurement (REIPPP) Programme.

**Table 1** below provides the details of the project, including the main infrastructure components and services that will be required during the project life cycle.

**Table 1:** Details of the Kleinzee Solar PV Facility and associated infrastructure

<b>Component</b>	<b>Description / Dimensions</b>
Total extent of the Affected Properties, including the grid connection corridor, also referred to as the project site	~1115.11ha
Total extent of the Development area <sup>1</sup>	~300ha
Contracted capacity of the facility	Up to 200MW
Technology	» Monofacial or Bifacial PV panels, mounted on either fixed-tilt, or single-axis tracking systems
PV panels	» Height: ~5m from ground level (installed)
On-Site Facility Substation & Switching Substation	» On-site facility substation and switching substations hub located on Portion 4 of the Farm Zonnkewa 328. » Approximately 2ha in extent (2ha per substation)
Grid Connection	» 132kV grid connection » 33kV cabling between the project components and the facility substation » Low voltage cabling between the PV modules to the inverters. » Facility substation located within grid corridor. » A 300m wide grid connection corridor within which the grid connection infrastructure will be constructed and operated. » Corridor traverses Farm Zonnkewa 326, Portion 1 of the Farm Zonnkewa 326, Portions 2, 3 and 4 of the Farm Zonnkewa 328.
Corridor width (for grid connection assessment purposes)	» 300m wide
Power line servitude width	» Up to 32m
Corridor length	» Approximately 8.5km
Battery Energy Storage System (BESS)	» Solid state battery technology (e.g. Lithium-ion technology) as a preferred technology. » Housed in containers covering a total approximate footprint of up to 3ha within the assessed substation, BESS and O&M Building hub area.

<sup>1</sup> The area to be covered by the facility layout and infrastructure of the proposed Kleinzee Solar PV Facility.

Site access roads and internal roads	<ul style="list-style-type: none"> <li>» Existing roads will be used, wherever possible, to access the project site and development area.</li> <li>» Access via existing gravel road the DR2964 located to the North of the site - portions of this road will require upgrading to 8m width to accommodate the movement of heavy vehicles.</li> <li>» From Farm Zonkewa 326, a planned access road up to ~7.5km in length and up to 8m in width located within the 300m grid connection corridor will traverse Farm Zonkewa 326, Portion 1 of Farm Zonnekwa 326, Portions 2, 3 and 4 of Farm Zonkewa 328.</li> <li>» Access road falls within 300m corridor assessed for the grid line</li> <li>» Internal access roads up to 6m in width.</li> </ul>
Associated infrastructure hub	<ul style="list-style-type: none"> <li>» Battery Energy Storage System (BESS).</li> <li>» Site offices and maintenance buildings, including workshop areas for maintenance and storage.</li> <li>» Laydown areas.</li> <li>» On-site facility substation and switching substation</li> </ul>

#### 7.1.6 Preliminary technical specification of the overhead transmission and distribution:


- Length – up to 30m
- Tower parameters
  - Number and types of towers – Number to be confirmed based on detailed design, informed by pre-construction site surveys, geotechnical investigation, and environmental walk-throughs. Tower type will be steel self-supporting and/or stayed monopoles. Lattice structures may be utilised at specific strain- or bend-points
  - Tower spacing (mean and maximum) – Power line towers (or pylons) are an average distance of ~200m apart but can exceed 500m depending on the topography and terrain to be spanned.
  - Tower height (lowest, mean and height) – up to 41m.
  - Conductor attachment height (mean) – To be confirmed based on final tower selection, but clearance shall at all times adhere to Eskom requirements in force at time of construction. Minimum ground clearance – 6.3m or as per the Eskom requirements in force at time of construction



It should be noted that Eskom requirements for work in or near Eskom servitudes will be adhered to, and all applicable Eskom standards shall be applied.

## 7.2 Sub-section 2: Development footprint site map

This sub-section must include a map of the site sensitivity overlaid with the preliminary infrastructure layout. The sensitivity map must be prepared from the national web based environmental screening tool, when available for compulsory use at: <https://screening.environment.gov.za/screeningtool>. The sensitivity map shall identify the nature of each sensitive feature e.g. raptor nest, threatened plant species, archaeological site, etc. Sensitivity maps shall identify features both within the planned working area and any known sensitive features in the surrounding landscape. The overhead transmission and distribution profile shall be illustrated at an appropriate resolution to enable fine scale interrogation. It is recommended that <20 km of overhead transmission and distribution length is illustrated per page in A3 landscape format. Where considered appropriate, photographs of sensitive features in the context of tower positions shall be used.

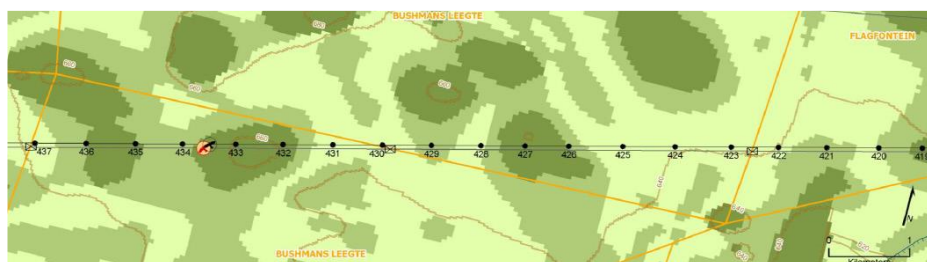

**Figure 1:** Example of an environmental sensitivity map in the context of a final overhead transmission and distribution profile.

**The national web-based environmental screening tool was utilised for this project and the project site sensitivity maps can be seen in Figures 3 to 11. The site-specific environmental sensitivity map included in the BA Report is included as Figure 2.**

### **Site sensitivity**

A combined sensitivity map for the grid connection corridor is provided below. This has been compiled based on the specialist sensitivities determined from their respective studies, and therefore aims to represent the entirety of the site and the combined sensitivities. The following environmental sensitivities were noted on site:

### **Impacts on Ecology (including flora and fauna)**

The Terrestrial Biodiversity Assessment (**Appendix D**) undertaken determined that there are no impacts associated with the Kleinzee Solar PV Facility and associated infrastructure that cannot be mitigated to an acceptable level and as such, the assessed layout was considered acceptable.

The Kleinzee PV Facility falls within the Namaqualand Stranded vegetation type, which has been impacted to a relatively limited extent by transformation to date and is classified as Least Threatened. The field assessment found that the site has a relatively low abundance of plant SCC and only *Wahlenbergia asparagoides* (VU) was observed present. There are no significant biodiversity features within the site, and it is considered relatively low sensitivity. The development footprint falls within a NPAES Priority Focus Area and identified expansion area for the Namakwa National Park, with the loss of 310 ha representing less than 0.01% of the Focus Area. Solar PV facilities do not have a large edge effect in terms of noise and disturbance, so their proximity to protected areas is not likely to represent a significant threat to biodiversity.

The development is deemed acceptable from a terrestrial ecological impact perspective, with no impacts that cannot be mitigated. It is the specialist opinion that the development should be authorised subject to mitigation and avoidance measures.

#### Impacts on Avifauna

The Avifauna Impact Assessment (**Appendix E**), which considered the results of a desktop and two-season site visit of birds on the proposed Kleinzee Solar Energy Facility site indicated a medium level of activity in terms of Passage Rates of Priority species, and medium activity of Red Data species. Low overall species richness (46 species) and medium-low reporting rates for the four species of Priority birds. National Bird Atlas data (SABAP2) suggests that six Red Data species can occur in the area, but only one was seen on this small site. Screening Tool Assessment indicated a High risk in the Animal Theme but a low risk for the Avian theme. No small, threatened larks (Vulnerable Red Lark, or Near Threatened Barlow's Lark) were recorded on site. This suggests that the avian impact will be low for the proposed PV solar farm site at Kleinsee. The power lines exporting power to the grid pose a medium risk to the birds after mitigation, given their short length and the ability for the proposed line to be aligned and staggered with the existing Gromis-Juno line.

Due to the low avian diversity, low Passage Rates, and paucity of highly threatened species on this small site no mitigation measures are required for the solar farm, but the best form of mitigation is the staggered pylon idea (Pallett et al. 2022). No fatal flaws were identified during the assessment, although it was strongly recommended that the proposed mitigation measures and monitoring protocols (e.g. post construction monitoring) be implemented during the construction and operational phase of the project.

#### Impacts on Soil and Agricultural Potential

Following the data analysis and impact assessment, the proposed Kleinzee Solar PV Facility and Associated Infrastructure is considered an acceptable development within the development area.

The soil forms present within the development area consist of the Namib soil form which are deep regic sands with depths of 1400 mm and shallow Coega soil form. There is no current agricultural land use. There is also no irrigation infrastructure, such as centre pivots or drip irrigation, present within the project area. The grazing capacity (according to DALRRD, 2018), is 45 ha/LSU, indicating that the proposed development area of 628.67 ha has forage to feed 14 head of cattle.

The total area assessed, has Low land capability and sensitivity (628.67 ha). The land capability was calculated by using 30% terrain and soil, and 40% climate capability of the area. The calculations showed that Low land capability has been assigned to soils of the Namib and Coega soil form because of the regic sand and shallow depth that has a very low water holding capacity and structure. The low land capabilities of the soils within the development area is confirmed by the absence of crop field boundaries within the Kleinzee Solar PV Facility development area.

It is the specialist's opinion that this application be considered favourably, permitting that the mitigation measures are followed to prevent soil erosion and soil pollution and to minimise impacts on the veld quality of the farm portions that will be affected. The project infrastructure should also remain within the proposed project area that will be fenced off.

## **Impacts on Heritage Resources (archaeological and paleontological)**

The overall archaeological sensitivity of the Namaqualand with regard to the preservation of Early, Middle and Later Stone Age archaeology as well as Khoe and San heritage, early colonial settlement and the Namaqualand Copper Mining landscape is regarded as very high. The field assessment conducted for this project has demonstrated that the specific area proposed for development has low sensitivity for impacts to significant heritage resources. Trace fossils are ubiquitous and important palaeoenvironmental indicators.

The significance rating is low for fossil potential as a consequence of the low probability of finding fossils in the terrestrial deposits. Further observations in the surrounding area (John Pether) indicate that the deposits are altered by pedogenic processes involving decalcification and the precipitation of pedocrete. Fossil shells are not preserved, and fossil bone is very sparse. Given the low palaeontological potential, it is improbable that fossil bones will be encountered, and no impact is anticipated.

No impact to significant palaeontological heritage is therefore anticipated. However, it is recommended that the attached Chance Fossil Finds Procedure is implemented during the course of construction activities. The field assessment conducted for this project has demonstrated that the specific area proposed for development has low sensitivity for impacts to significant archaeological heritage. One structure of significance is known to be located in close proximity to the proposed development and it is recommended that this site be protected by the implementation of a no-go buffer area.

There is no objection to the proposed development of the Kleinzee Solar PV Facility in terms of impacts to heritage resources on condition that:

- » The recommendations in the VIA must be implemented
- » The attached Chance Fossil Finds Procedure (Appendix 3) is implemented during the course of construction activities.
- » Should any buried archaeological resources or burials be uncovered during the course of development activities, work must cease in the vicinity of these finds. The South African Heritage Resources Agency (SAHRA) must be contacted immediately in order to determine an appropriate way forward.

### **Visual Impacts**


The significance of the visual impacts for the Kleinzee Solar PV Facility and its associated Grid Connection Infrastructure is expected to range from moderate to low due to the undeveloped landscape and remote location of the project infrastructure. Mitigation measures have been proposed to reduce the significance of the anticipated visual impacts, but they are considered to be good practice and should be implemented and maintained throughout the construction, operation and decommissioning phases of the proposed facility. If mitigation is undertaken as recommended, it is concluded that the significance of most of the anticipated visual impacts will remain at or be managed to acceptable levels, allowing the Solar PV facility and associated grid connection infrastructure to be authorised.

### **Social Impacts**

The findings of this SIA indicate that if mitigation measures are implemented, negative impacts can be lowered to acceptable levels. This will ensure that the proposed development of the


200MW Solar PV facility and associated infrastructure will have social benefits that outweigh the negative impacts. It is anticipated that during the construction and operational phase of the proposed project, various employment opportunities and local business opportunities will be created, benefitting the socio-economic development of the local community. Therefore, the development of the Kleinzee Solar PV facility and Grid Connection is acceptable from a social perspective.

»

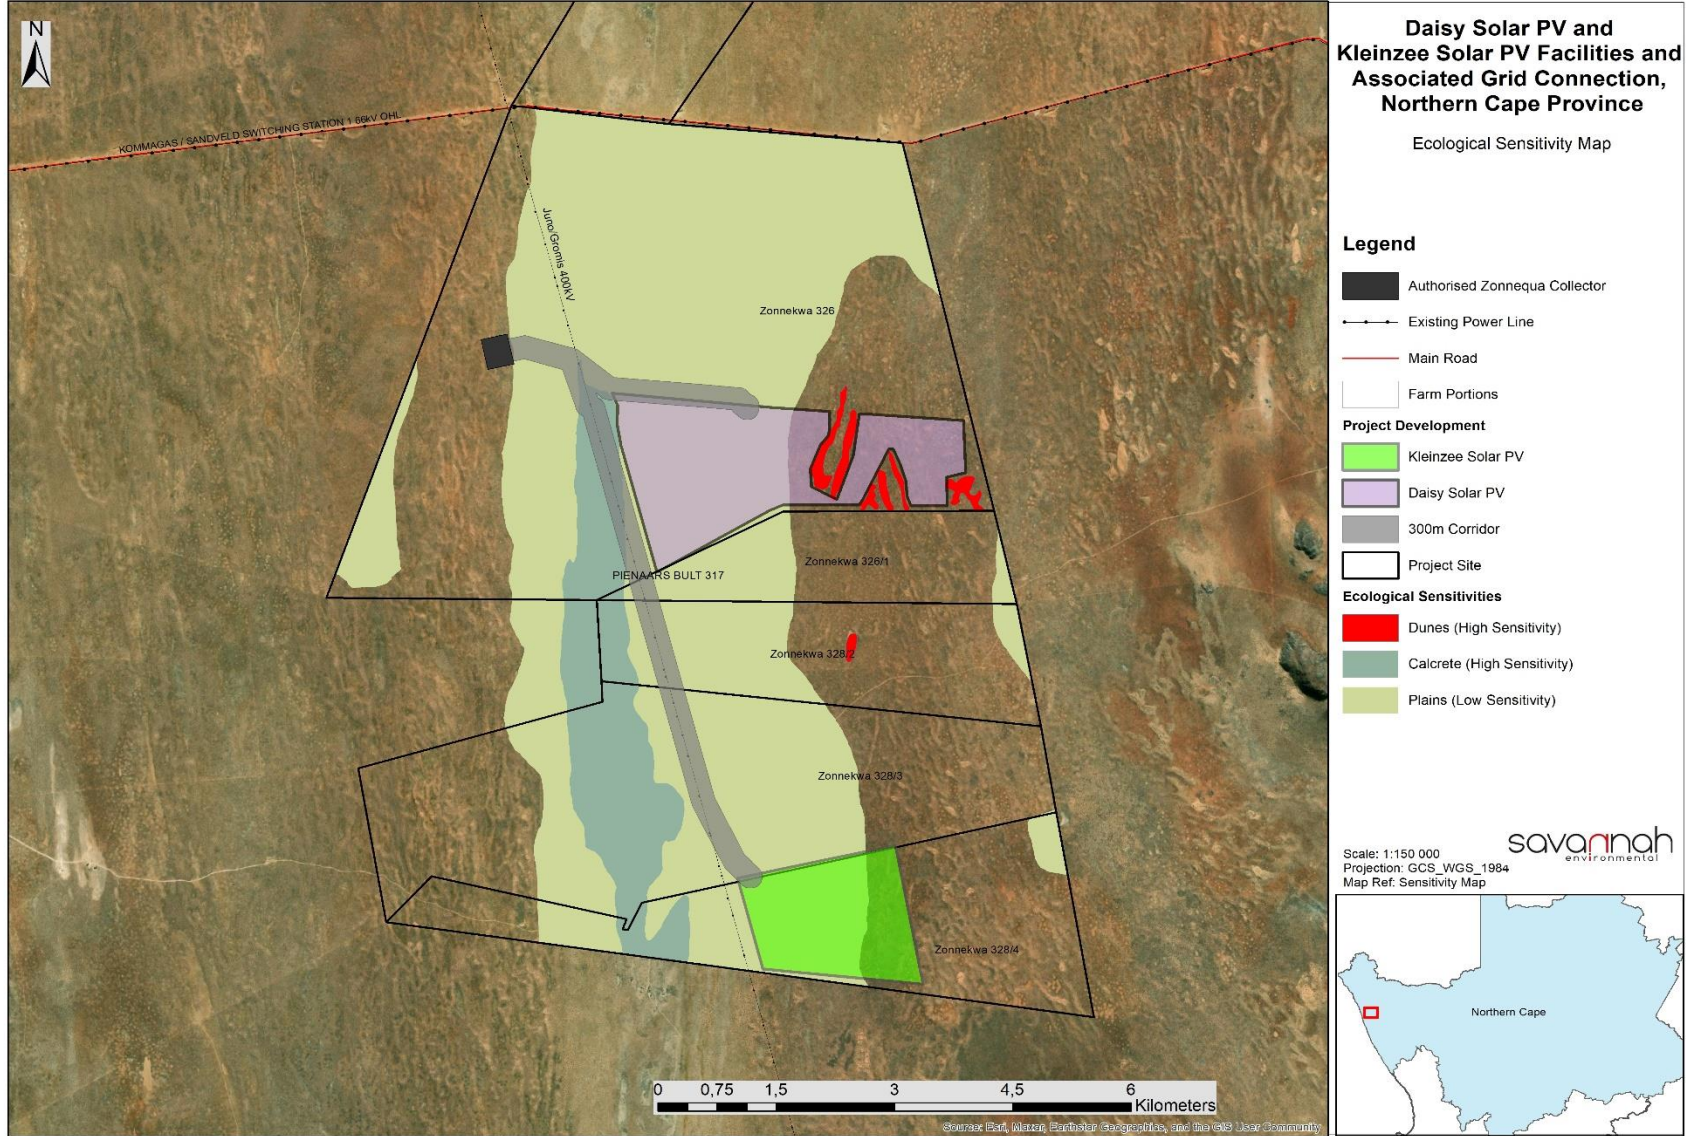


**Figure 2:** Environmental sensitivity map showing the grid connection corridor.



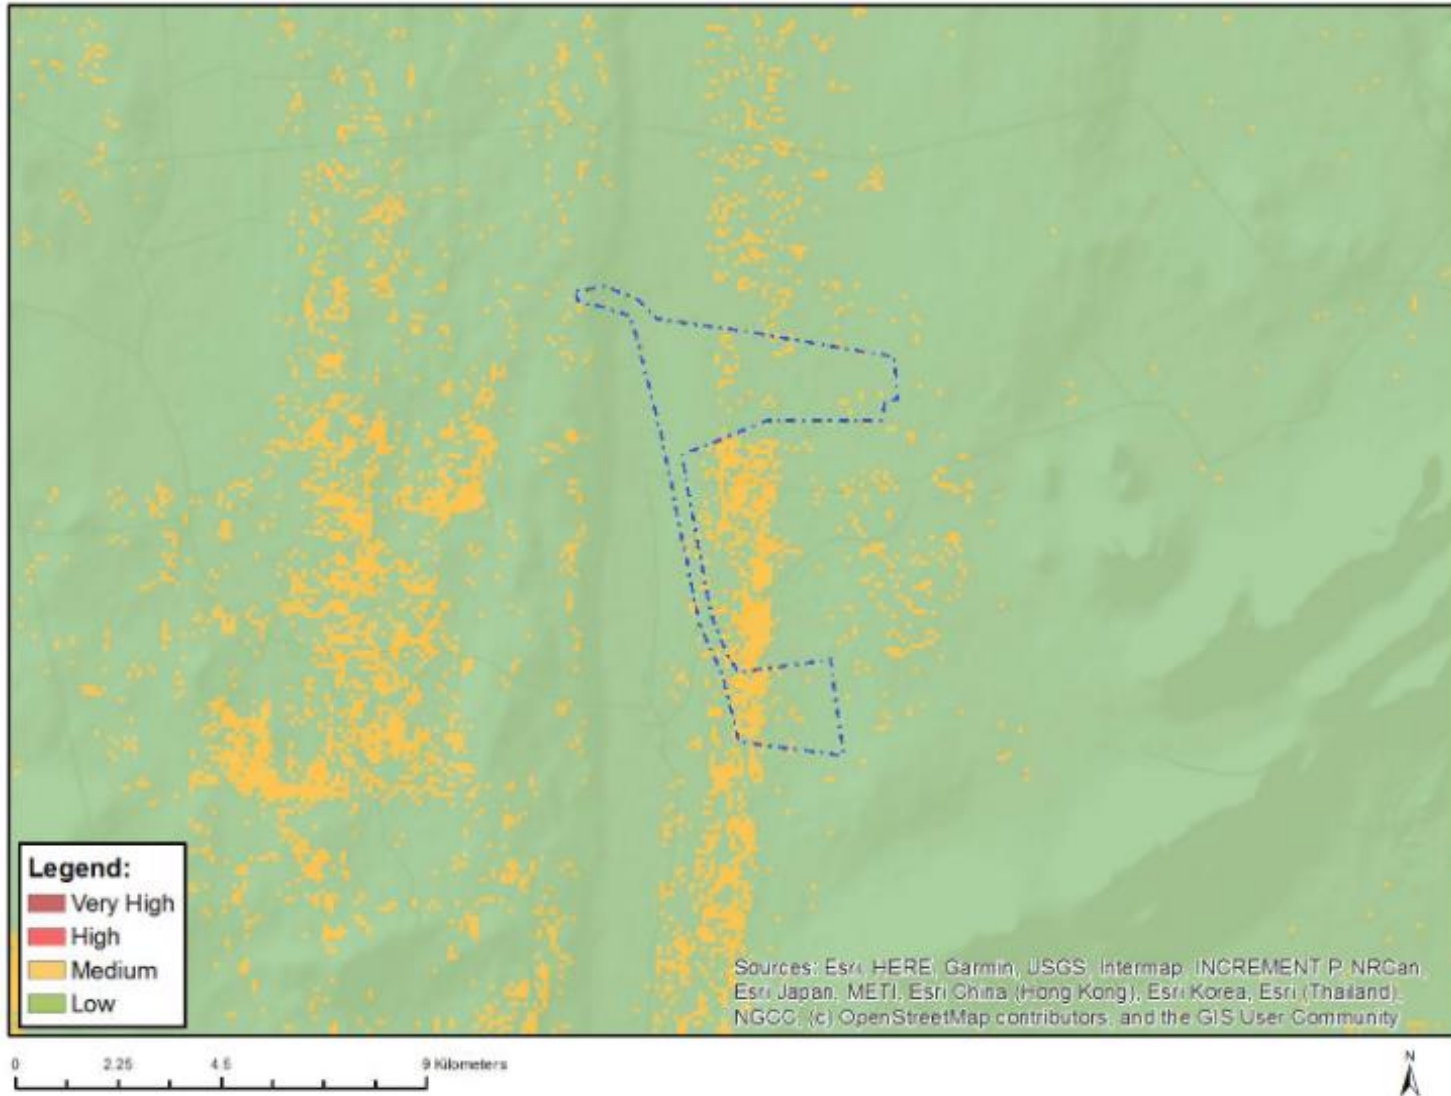


**Figure 3:** Map of relative agriculture theme sensitivity

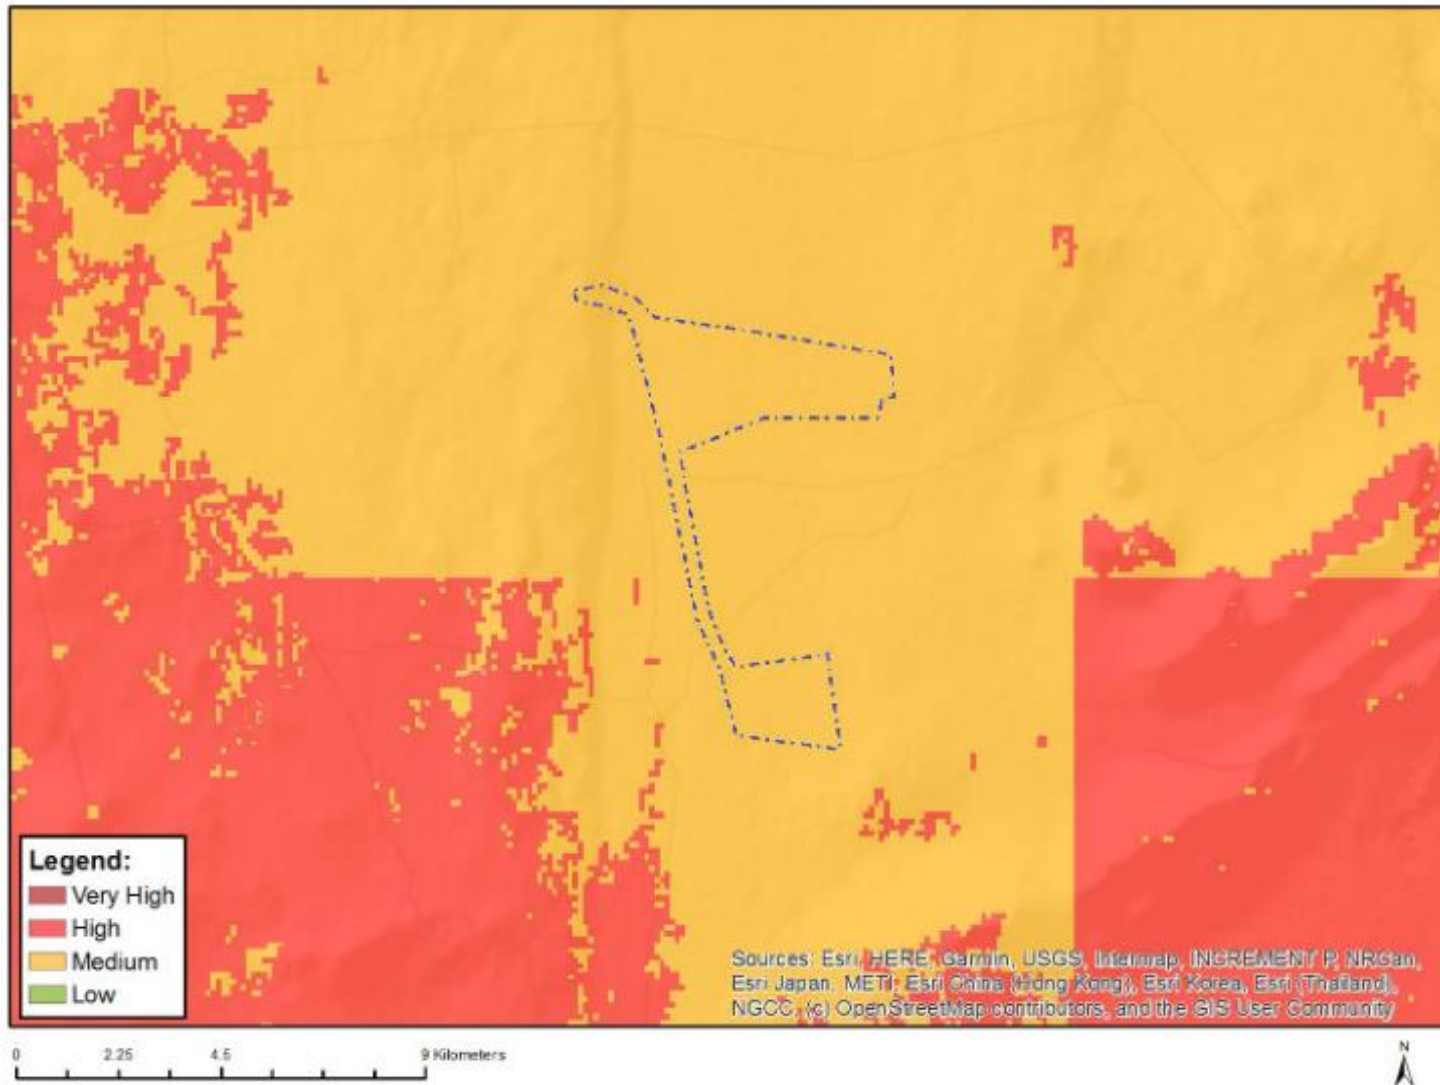

**Figure 4:** Map of relative animal species theme sensitivity




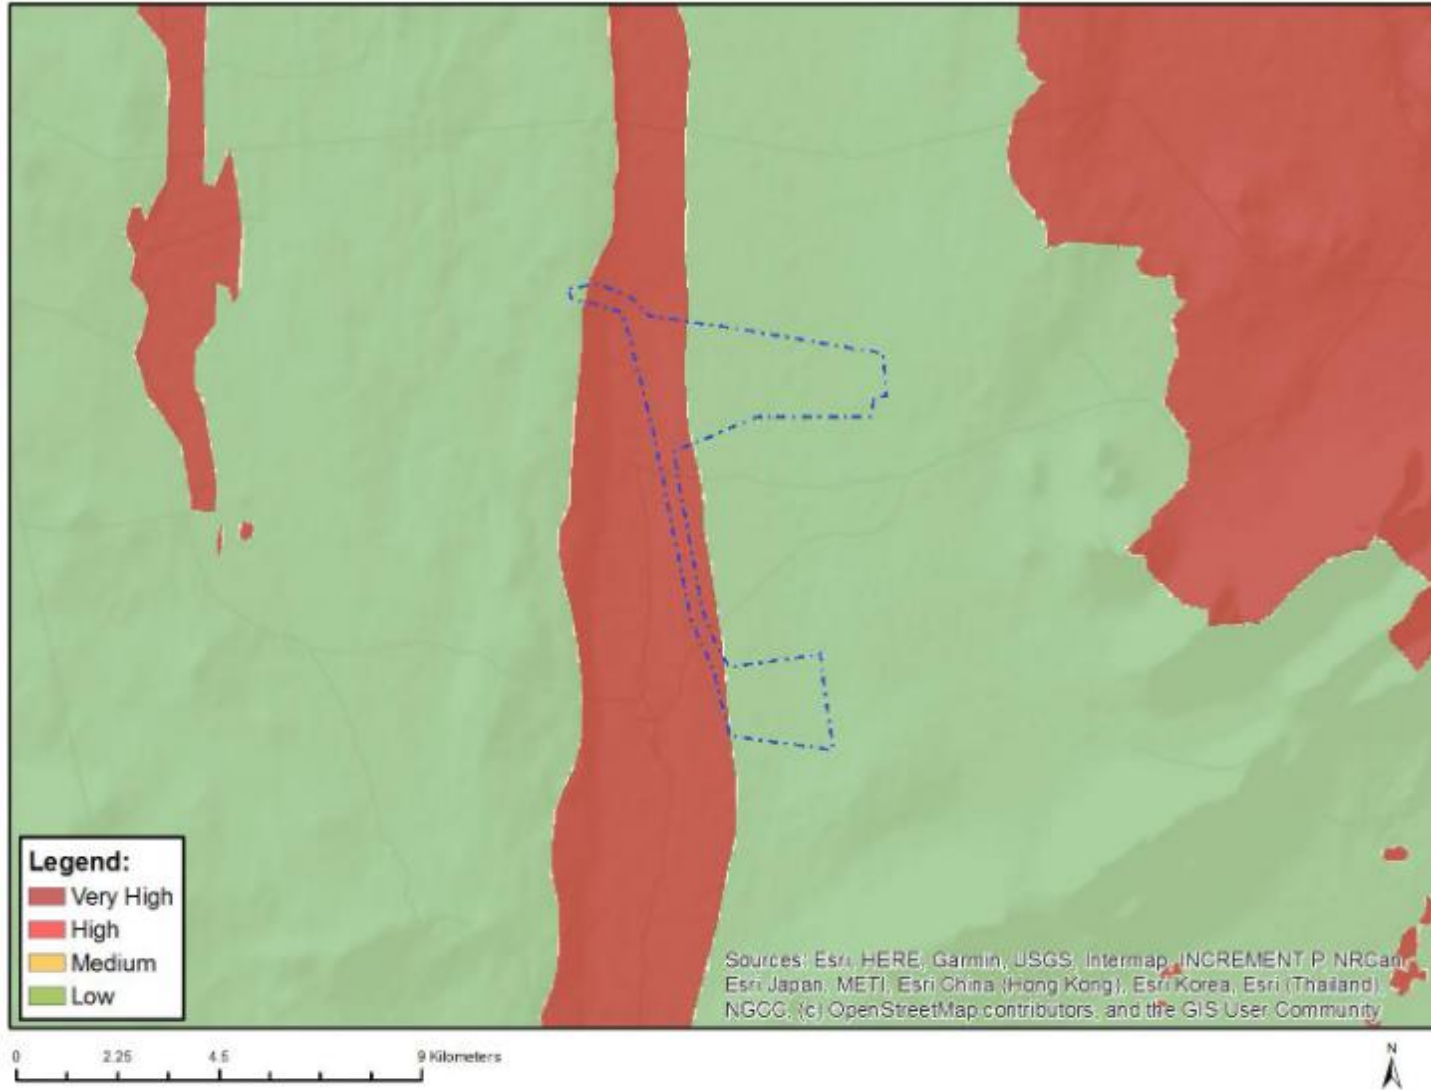


**Figure 5:** Map of relative aquatic biodiversity theme sensitivity




**Figure 6:** Map of relative archaeological and cultural heritage theme sensitivity

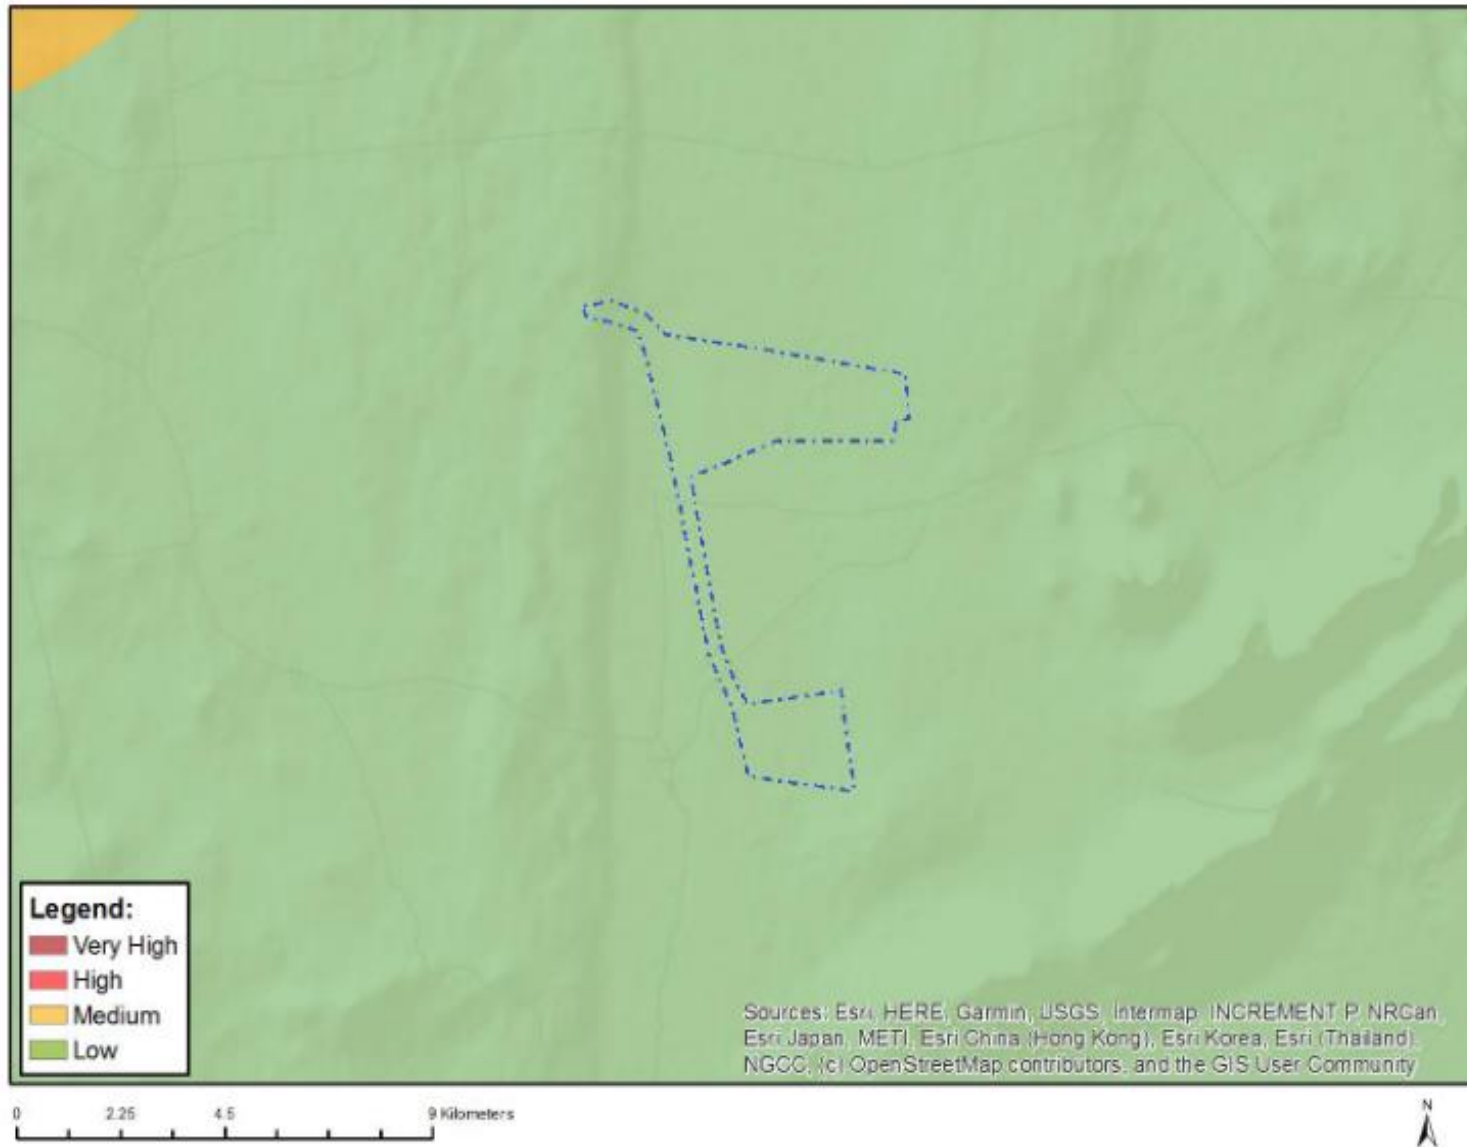


**Figure 7:** Map of relative civil aviation theme sensitivity

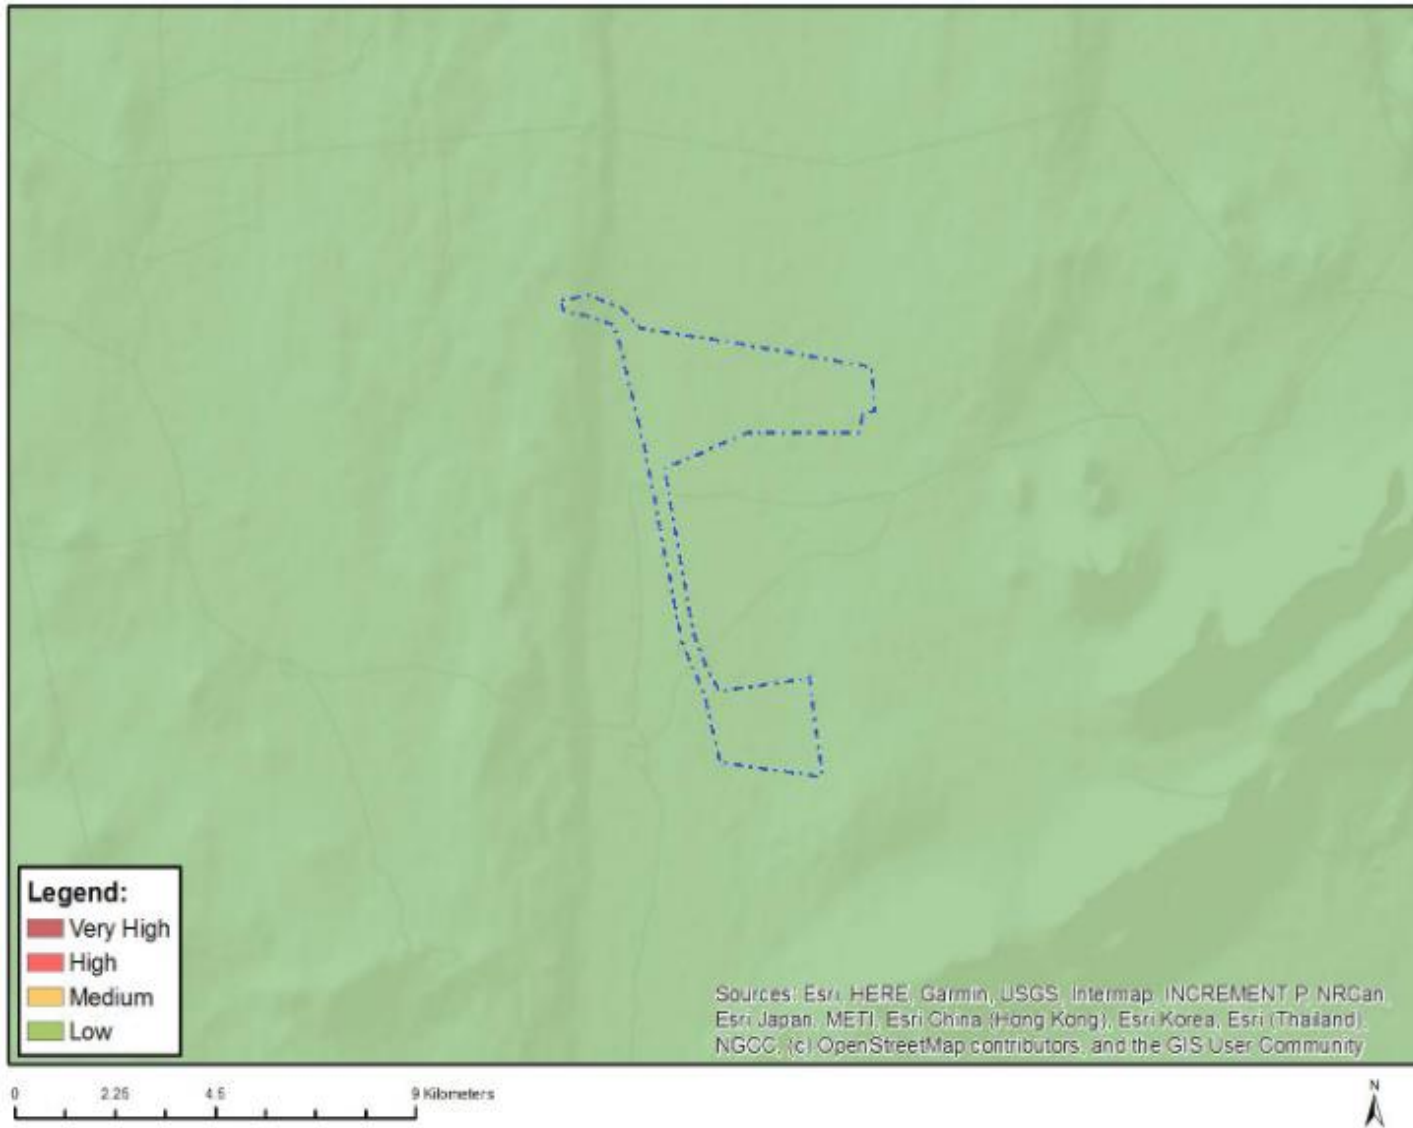


**Figure 8:** Map of relative defence theme sensitivity

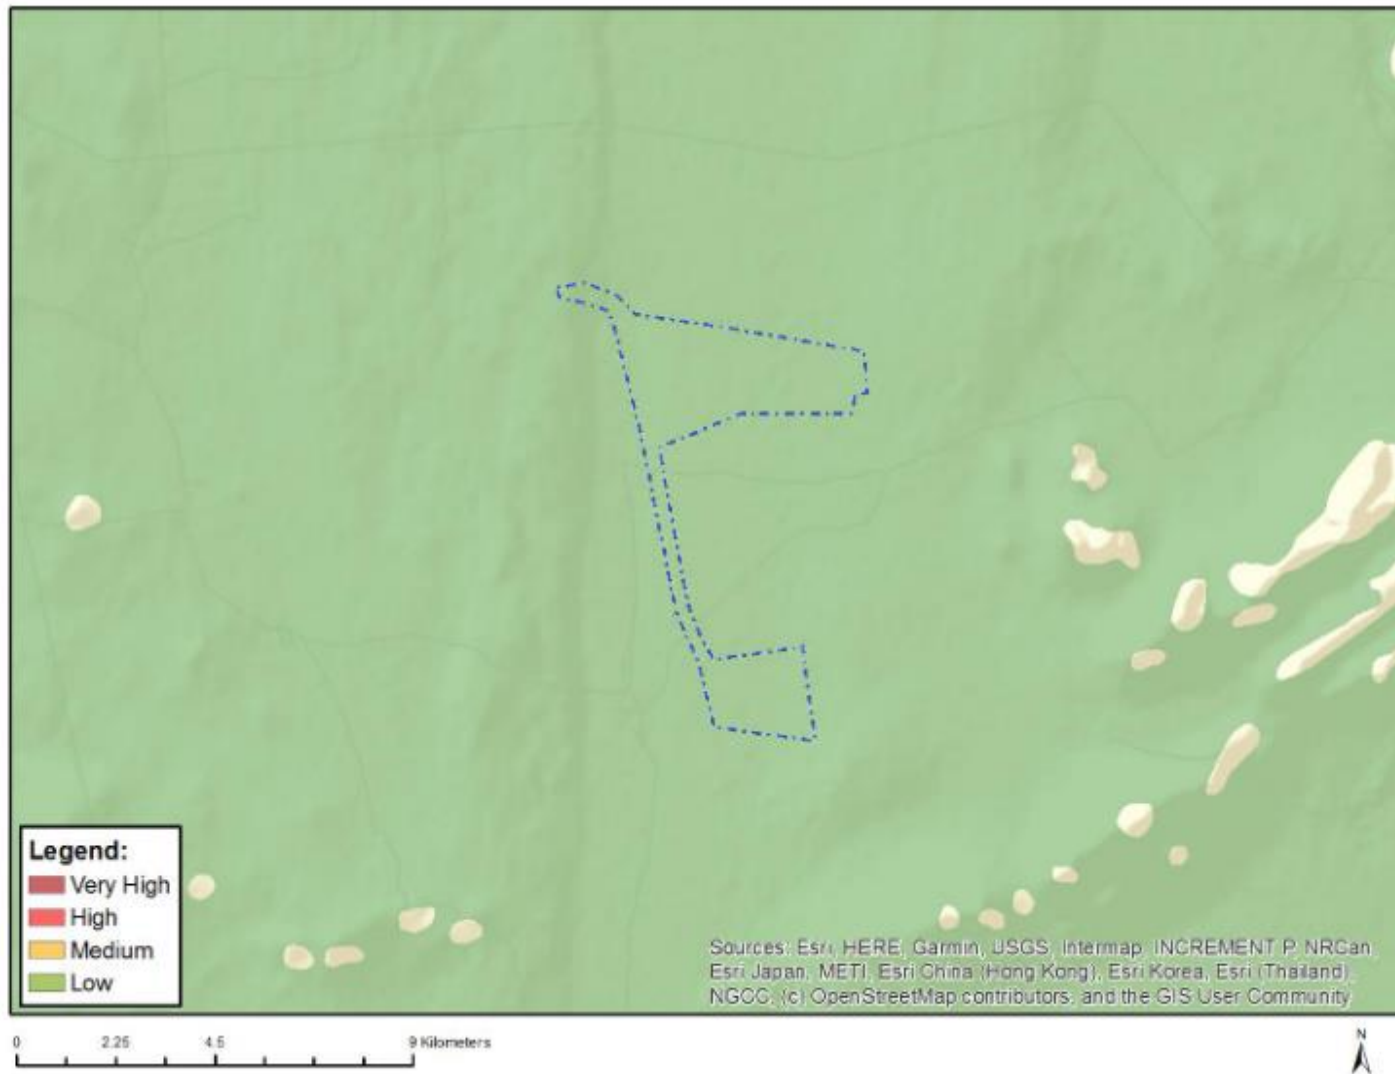

**Figure 9:** Map of relative palaeontological theme sensitivity

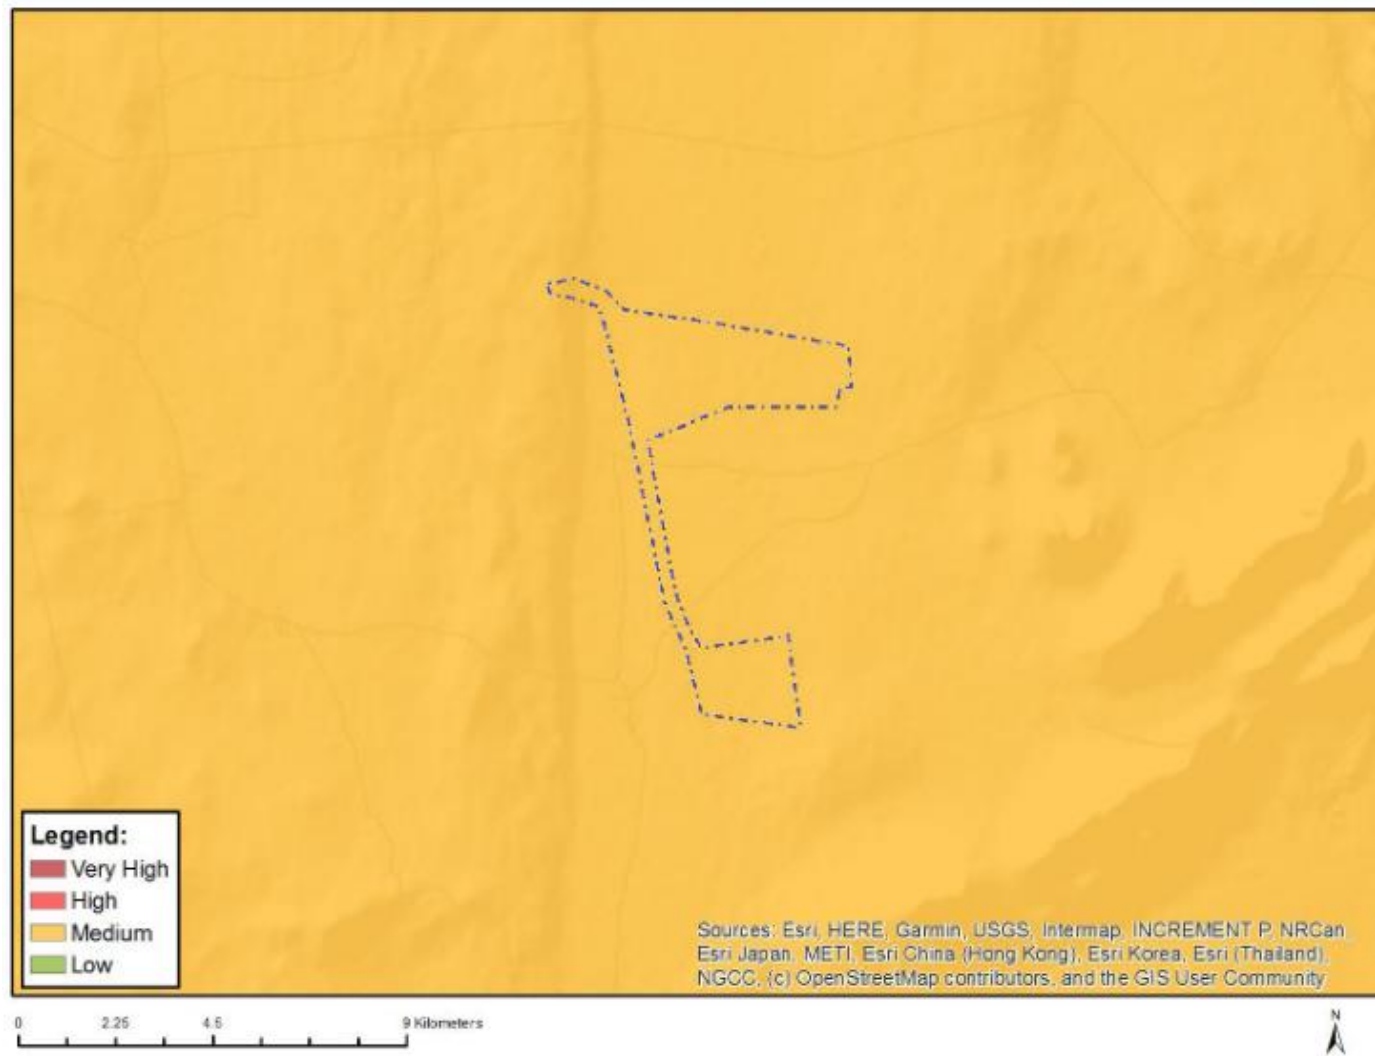

**Figure 10:** Map of relative plant species theme sensitivity

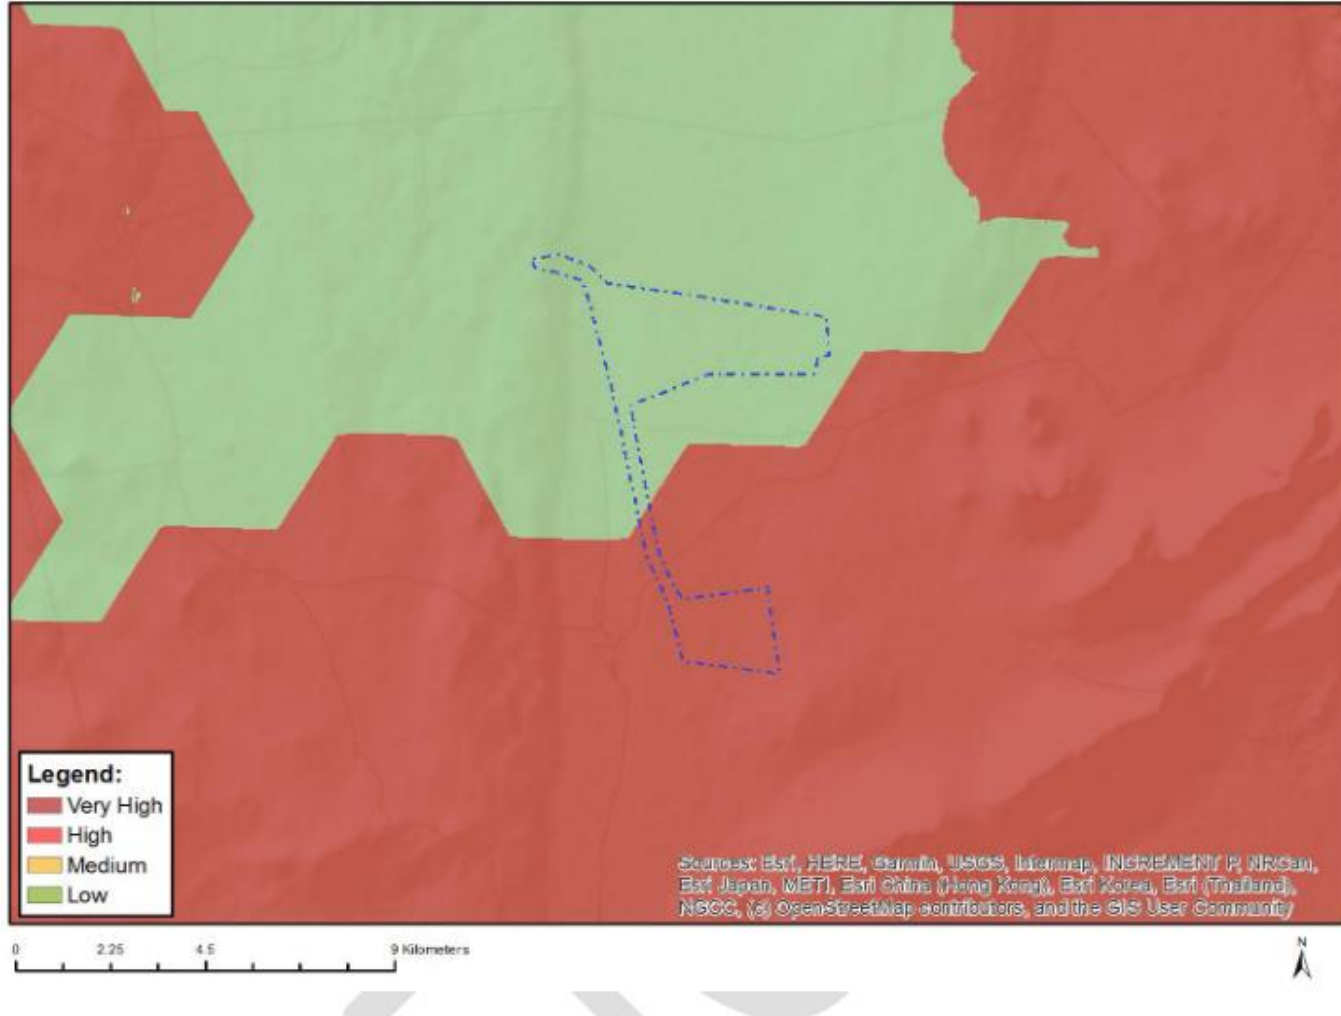

**Figure 11:** Map of relative terrestrial biodiversity theme

### 7.3 Sub-section 3: Declaration

The proponent/applicant or holder of the EA affirms that he/she will abide and comply with the prescribed impact management outcomes and impact management actions as stipulated in part B: section 1 of the generic EMPr and have the understanding that the impact management outcomes and impact management actions are legally binding. The proponent/applicant or holder of the EA affirms that he/she will provide written notice to the CA 14 days prior to the date on which the activity will commence of commencement of construction to facilitate compliance inspections.

Signature Proponent/applicant/ holder of EA

Date: xx

-----  
**This declaration will be signed by the proponent/applicant/holder of the EA once the contractor is appointed and has provided inputs to this Generic EMPr as per the requirements of this template.**

**The contractor would be required to develop the following site-specific plans in accordance with the specialist recommendation contained in Section C of this EMPr:**

- » **Alien Plant Management Plan**
- » **Rehabilitation Plan**
- » **Solid Waste Management Plan**
- » **Waste Management Plan**
- » **Stormwater Management Plan**

### 7.4 Sub-section 4: amendments to site specific information (Part B; section 2)

Should the EA be transferred to a new holder, Part B: Section 2 must be completed by the new holder and submitted with the application for an amendment of the EA in terms of Regulations 29 or 31 of the EIA Regulations, whichever applies. The information submitted for an amendment to an environmental authorisation will be considered to be incomplete should a signed copy of Part B: Section 2 not be submitted. Once approved, Part B: Section 2 forms part of the EMPr for the development and the EMPr becomes legally binding to the new EA holder.

## PART C

### 8 SITE SPECIFIC ENVIRONMENTAL ATTRIBUTES

If any specific environmental sensitivities/attributes are present on the site which require more specific impact management outcomes and impact management actions, not included in the pre-approved generic EMPr template, to manage impacts, those impact management outcomes and actions must be included in this section. These specific management controls must be referenced spatially and must include impact management outcomes and impact



management actions. The management controls including impact management outcomes and impact management actions must be presented in the format of the pre-approved generic EMPr template. This applies only to additional impact management outcomes and impact management actions that are necessary.

If Part C is applicable to the development as authorised in the EA, it is required to be submitted to the CA together with the BAR or EIAR, for consideration of, and decision on, the application for EA. The information in this section must be prepared by an EAP and the name and expertise of the EAP, including the curriculum vitae are to be included. Once approved, Part C forms part of the EMPr for the site and is legally binding.

This section will **not be required** should the site contain no specific environmental sensitivities or attributes.

## **CONSTRUCTION AND DECOMMISSIONING OUTCOMES AND ACTIONS**

### **7.1 Ecology (Fauna and Flora)**

**Impact management outcome:** Direct loss and/or fragmentation of indigenous natural vegetation is minimised

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Restrict impact to development footprint only and limit disturbance creeping into surrounding areas.	Contractor	Place a barricade around the development footprint to indicate that no disturbance is allowed beyond that point	During the construction phase	ECO	Monthly	No evidence of disturbance beyond the development footprint
– As far as possible, locate infrastructure within areas that have been previously disturbed or in areas with lower sensitivity scores. Avoid sensitive features and habitats when locating infrastructure.	Design Engineer and Contractor	Develop a layout that avoids areas of high sensitivity  Provide layout to the contractor and demarcate areas of high sensitivity	Prior to construction and during the construction phase	ECO	Monthly	Infrastructure avoids areas of high sensitivity
– Compile a Rehabilitation Plan.	Contractor, cEO	Make contractor aware of the requirement for a rehabilitation plan for the site	During the construction phase	ECO	Monthly	Rehabilitation Plan available on request

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Compile an Alien Plant Management Plan, including monitoring, to ensure minimal impacts on surrounding areas.	Contractor, CEO	Make contractor aware of the requirement for an alien plant management plan for the site	During the construction phase	ECO	Monthly	Alien Plant Management Plan available on request
– Where possible, access roads should be located along existing farm and district roads.	Design Engineer and Contractor	Develop a layout with access roads that are in alignment with existing farm and district roads and provide layout to the contractor	Prior to construction and during the construction phase	ECO	Monthly	Access roads are established along existing farm and district roads.
– Footprints of infrastructure, laydown areas, construction sites, roads and substation sites should be clearly demarcated.	Contractor	Make contractor aware of the requirement to demarcate the infrastructure footprint	During the construction phase	ECO	Monthly	Barricade evident around infrastructure footprints
– No additional clearing of vegetation should take place without a proper assessment of the environmental impacts and authorization from relevant authorities, unless for maintenance purposes, in which case all reasonable steps should be taken to limit damage to natural areas	Contractor	Place a barricade around the development footprint to indicate that no disturbance is allowed beyond that point	During the construction phase	ECO	Monthly	No vegetation clearing observed beyond the barricaded development footprint
– Limit clearing of natural habitat designated as sensitive, especially rocky outcrops, cliffs, and riparian habitats, where possible.	Contractor, CEO	Install signage at locations of sensitive features that states that no	During the construction phase	ECO	Monthly	No clearing of natural habitat designated as

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
		disturbance is allowed				sensitive is observed on site
– No driving of vehicles off-road outside of construction areas. Personnel and vehicles should be restricted to access / internal roads and no off-road driving should occur.	Contractor	Install signage stating that no driving of vehicle off-road outside of construction areas is permitted and also include this in toolbox talks and induction training material	Duration of construction phase	ECO	Monthly	No evidence of vehicles driving in the veld outside the demarcated roads
– Access to sensitive areas should be limited during construction.	cEO and Contractor	Include topic the avoidance of sensitive features in toolbox talks	Duration of construction phase	ECO	Monthly	Avoidance of sensitive areas included in toolbox talks
– Compile a Solid Waste Management Plan, including monitoring, to ensure minimal impacts on surrounding areas.	Contractor, cEO	Make contractor aware of the requirement for a Waste management Plan for the site	During the construction phase	ECO	Monthly	Solid Waste Management Plan available on request

**Impact management outcome:** Direct mortality of fauna

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
<p>– A detailed pre-construction walk-through survey will be required during a favourable season to locate any individuals of protected plants, as well as for any populations of threatened plant species. This survey must cover the footprint of all approved infrastructure, including internal service roads and footprints of tower structures (final infrastructure layout). The best season is early to late Summer, but dependent on recent rainfall and vegetation growth.</p>	Developer, Specialist	Appoint specialist prior to construction to undertake a detailed walk-through survey of the footprint areas	Prior to construction	ECO	Once at the commencement of construction	Walk-through report produced and kept on file during construction
<p>– Where significant populations of SCC are found, shift infrastructure to avoid direct impacts.</p>	Design Engineer	Use the results of the detailed walk-through survey to design the facility layout and ensure that the layout avoids areas of significant populations of species of conservation concern	Prior to construction	ECO	Monthly	No infrastructure established in areas where significant populations of species of conservation concern are found
<p>– For any plants that are transplanted, annual monitoring should take place to assess survival. This should be undertaken for a period of three years after translocation and be undertaken by a qualified botanist. The monitoring programme must be designed prior to translocation of plants and should include control sites (areas not disturbed by the project) to evaluate mortality relative to wild populations.</p>	cEO, Contractor	Prepare plan for the monitoring of transplanted plants	Prior to construction	ECO	As and when required	Plan for the monitoring of transplanted plants available upon request and results of monitoring are available on site

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– No collecting or poaching of any plant species must be permitted on site. Report any illegal collection to conservation authorities.	cEO, Contractor	Requirement for induction of all staff prior to entry, in particular about the collection of plant species	During the construction phase	ECO	Monthly	No evidence of collection of plant species, and induction roster of all staff completed, maintained and available on site
– Loss of protected species of conservation concern must be report to the conservation authorities.	cEO, Contractor	Include this condition within the contractor's pack and within the site induction material	During the construction phase	ECO	Monthly	Condition include in the site induction material and contractor's pack
– Personnel must be educated about protection status of species, including distinguishing features, to be able to identify protected species.	cEO	Develop environmental awareness training material which covers the protection status of species, including distinguishing features	During the construction phase	ECO	M Prior to the commencement of the environmental awareness training	Protection status of species, including distinguishing features included in induction material
– Implement strict access control for the site.	DSS, dEO	Demarcate the project site and place a security guard and register at the main gate	Duration of the project	ECO	Monthly	Security guard placed on site and no reports of unauthorised entry
– The location of all transplanted rescued plants must be recorded, along with the identity of the plant.	Contractor, cEO	Ensure that the locations of transplanted	During the construction phase	ECO	Monthly	Record of transplanted rescued plants

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
		rescued plants are recorded along with the identify of the plant and kept on file				available on site (includes location and identify of plants)

**Impact management outcome:** Establishment and spread of declared weeds and alien invader plants is minimised

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Undertake regular monitoring to detect alien invasions early so that they can be controlled.	Contractor, cEO	Prepare alien management plan for implementation for the duration of the construction phase	During the construction phase	ECO	Monthly	Alien Plant Management Plan available on request

**Impact management outcome:** Runoff and erosion are reduced

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
<ul style="list-style-type: none"> <li>– Compile and implement a stormwater management plan.</li> </ul>	Contractor, cEO	Make contractor aware of the requirement for a stormwater management plan for the site	During the construction phase	ECO	Monthly	Alien Plant Management Plan available on request
<ul style="list-style-type: none"> <li>– Speed limits should be set for all roads on site, as well as access roads to the site. These limits should not exceed 40 km/h, but may be set lower, depending on local circumstances. Strict enforcement of speed limits should occur – install speed control measures, such as speed humps, if necessary.</li> </ul>	Contractor, cEO	Install speed signature throughout site, include speed limit into induction and ensure all staff entering site is aware of the requirement to implement speed limits. Institute verbal and written warnings for violations and appropriate fines for repeat contraventions. Written log of fines and warning issued kept on site	During the construction phase	ECO	Monthly	Minimal instances of speeding as observed on site during audits and as evidenced in the written log of warnings and fines issued for contraventions



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Maintain adequate buffer zones around hydrological features so that these do not become degraded from runoff and erosion	Design Engineer and Contractor	Ensure layout has been informed by the environmental sensitivities as determined by the environmental impact assessment and specialist studies	Prior to construction and during construction	ECO	Once off review that the layout used is the approved one, and monthly thereafter	Hydrological features clearly demarcated  No evidence of construction activities taking place within the 'no-go' areas during audit

**Impact management outcome:** Minimal to no impacts to fauna species

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Pre-construction walk-through, undertaken in the correct season, in front of construction must be undertaken to move any individual animals, such as tortoises, prior to construction.	Developer, Specialist	Appoint specialist prior to construction to undertake a detailed walk-through survey of the footprint areas	Prior to construction	ECO	Once at the commencement of construction	Walk-through report produced and kept on file during construction
– Personnel on site should undergo environmental induction training, including the need to abide by speed limits, the increased risk of collisions with wild animals on roads in rural areas.	cEO, Contractor	Include topic on speed limits and collision with wild animals in induction material	During the construction phase	ECO	Monthly	Topic on speed limits and collision with wild animals included

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
						induction material
<ul style="list-style-type: none"> <li>Proper waste management must be implemented, ensuring no toxic or dangerous substances are accessible to wildlife. This should also apply to stockpiles of new and used materials to ensure that they do not become a hazard.</li> </ul>	Contractor	Compile a waste management plan for implementation during the construction phase	During the construction phase	ECO	Monthly	Waste management plan available on site and waste is being managed in accordance with the plan
<ul style="list-style-type: none"> <li>No collecting, hunting or poaching of any animal species should take place. Report any mortality of protected species to conservation authorities.</li> </ul>	cEO	Requirement for induction of all staff prior to entry, in particular about the collection, hunting or harvesting of and animals	Duration of the project	ECO	Monthly	No evidence of fauna mortality, and induction roster of all staff completed, maintained and available on site
<ul style="list-style-type: none"> <li>Appropriate lighting should be installed to minimize impacts on nocturnal animals, as per visual specialist assessment.</li> </ul>	Developer, Contractor	Include lighting specifications in the contractor's pack	Prior to construction and during construction	ECO	Monthly	Lighting specifications include in contractor's pack  Appropriate lighting utilised on site

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
- Construction activities should not be undertaken at night.	Developer, Contractor	Include working hours in contractor's pack	Prior to construction and during construction	ECO	Monthly	No evidence of construction activities being undertaken at night

**Impact management outcome:** Minimised impacts on surface water quality and runoff, erosion and sedimentation are reduced

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
- The contractors used for the construction phase should have spill kits available onsite prior to construction to ensure that any fuel, oil or hazardous substance spills are cleaned-up and discarded correctly	Developer	Make contractors aware of the requirement for a spill kit on site	Construction phase	ECO	Monthly	Visual observation of spills kits
- During construction activities, all rubble generated must be kept in a skip (or similar) and removed from the site to a licensed facility.	Contractor	Provision of appropriate skips which are strategically placed throughout the site	During the construction phase	ECO	Weekly	Appropriate skips are available throughout the site  Disposal certificates of disposal at licensed facilities to be provided

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		Disposal of general waste at licensed waste disposal facilities must be undertaken as per the waste management plan				
– All chemicals and toxicants to be used for the construction must be stored in a bunded area.	Contractor	Ensure that storage areas are impermeable and are sufficiently bunded, and have sumps and roofing	During the Construction Phase	ECO	Monthly	Photographic proof that storage areas are impermeable, and have bunds, sumps and roofing
– All machinery and equipment should be inspected regularly for faults and possible leaks, these should be serviced off-site at designed areas.	Contractor, cEO	Make contractors aware of the requirement for regular inspection of their machinery and equipment	Prior to construction and during construction	ECO	Monthly	Inspection checklists available on request
– Adequate sanitary facilities and ablutions on the servitude must be provided for all personnel throughout the project area. Use of these facilities must be enforced	Contractor	Ablution facilities must be provided and must be placed	During the Construction Phase	ECO	Weekly	Ablution facilities are installed and avoid environmental sensitivities

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
(these facilities must be kept clean so that they are a desired alternative to the surrounding vegetation).		appropriately and in areas which avoid environmental sensitivities				
– All contractors and employees should undergo induction which is to include a component of environmental awareness. The induction is to include aspects such as the need to avoid littering, the reporting and cleaning of spills and leaks and general good “housekeeping”.	cEO and Contractor	Prepare induction material which includes environmental awareness	Pre-construction and Construction	ECO	Monthly	Register of attendance available on request
– During construction activities, all rubble generated must be kept in a skip (or similar) and the removed from the site to a licensed facility.	Contractor, cEO	Develop and implement a waste management plan for the site.	Pre-construction and Construction	ECO	Monthly	Waste managed in accordance with the waste management plan for the site.
– All removed soil and material stockpiles must be protected from erosion, stored on flat areas where run-off will be minimised, and be surrounded by bunds.	Contractor	Prepare a method statement for the handling of soil	During the construction phase	ECO	Monthly	Method statement available on file at the site
– No dumping of material on site may take place.	Contractor	Toolbox talks must include topics on the handling of waste material	During the construction pahse	ECO	Monthly	No dumping of material observed on site  Register of attendance of toolbox talks on the handling of waste

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						material available on site
– All waste generated on site during construction must be adequately managed. Separation and recycling of different waste materials should be supported.	Contractor, cEO	Develop and implement a waste management plan for the site.	Pre-construction and Construction	ECO	Monthly	Waste managed in accordance with the waste management plan for the site.
– Landscape and re-vegetate all unnecessarily denuded areas as soon as possible.	Contractor	Develop and implement a rehabilitation plan for the rehabilitation of all disturbed areas.	Pre-construction & Rehabilitation	ECO	Weekly	Rehabilitation of the disturbed areas is undertaken as per the rehabilitation plan.

## 7.2 Avifauna

**Impact management outcome:** Displacement of priority species due to disturbance associated with construction of the Pixley Park PV plants and associated infrastructure

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Construction activity should be restricted to the immediate footprint of the infrastructure.	cEO, Contractor	Visual inspection of the construction activities to observe whether they remain within the defined footprint area  Demarcate project footprint	Duration of construction phase	ECO	Monthly	No evidence of construction activity outside the immediate footprint of the infrastructure
– Access to the remainder of the site should be strictly controlled to prevent unnecessary disturbance of priority species.	cEO, Contractor	Demarcate sensitive areas to restrict access to these areas	Duration of construction phase	ECO	Monthly	Sensitive areas appropriately demarcated and fenced off for the duration of the construction phase
– Conduct a pre-construction inspection (avifaunal walk-through) of the final central collector substation layout and power line alignment to identify priority species that may be breeding within the substation area and to record the status of the eagle nests on the existing transmission power lines. If a nest is occupied, the avifaunal specialist must consult with the contractor to find ways of minimising the potential disturbance to the breeding pair of eagles during the construction period. This could include measures such as delaying some of the activities until after the breeding season.	DPM	Appoint a qualified avifauna specialist to conduct a pre-construction walk-through of the final central collector substation layout	Pre-construction	ECO	Once off at the commencement of construction	Walk-through report available on file

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Measures to control noise and dust should be applied according to current best practice in the industry	Contractor	Ensure that measures to control noise and dust are applied throughout construction	During the construction phase	ECO	Monthly	No noise or dust complaints reported
– Maximum use should be made of existing access roads and the construction of new roads should be kept to a minimum.	Contractor	Existing access routes to be used must be specified and the development of new roads must be avoided as far as possible	Construction	cEO	Weekly	Implementation of the approved layout
– Vegetation clearance should be limited to what is absolutely necessary.	cEO and contractor	Demarcate areas of indigenous vegetation to be avoided before clearance is undertaken	During the construction phase	ECO	Weekly, and as and when required	No unnecessary clearance of indigenous vegetation is undertaken
– The recommendations of the ecological and botanical specialist studies must be strictly implemented, especially as far as limitation of the construction footprint is concerned.	CEO, Contractor	Implement the recommendation of the specialist of the ecological and botanical reports.	During the construction phase	ECO	Monthly	Evidence of implementation through pictures

**Impact management outcome:** During construction: Displacement of priority species due to habitat transformation associated with construction of the Pixley Park PV plants and associated infrastructure.



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– A 200m solar panel free buffer zone must be implemented around dams, wetlands, and drainage lines.	Contractor	Demarcate areas to avoid the sites	During the construction phase	ECO	Monthly	No go zone around the nests. Pictures of the sites. No construction or disturbance to the sites.
– Maximum used should be made of existing access roads and the construction of new roads should be kept to a minimum.	cEO, Contractor	Use the existing access roads to the site in the area.	Construction phase	ECO	Monthly	Use the existing access roads.
– The mitigation measures proposed by the biodiversity and vegetation specialists must be strictly implemented.	cEO, Contractor	Implement proposed mitigation measures from the specialist reports	Construction phase	ECO	Monthly	Evidence of implementation through pictures

### 7.3 Land Use, Soils and Agricultural Potential

**Impact management outcome:** Minimise loss of land capability

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Prevent any spills from occurring. Machines must be parked within hard park areas and must be checked daily for fluid leaks.	Contractor cEO	Vehicle and equipment storage areas must have	During the construction phase	ECO	Monthly	Vehicle and equipment storage areas have hard

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		hard surfaces and must be appropriately bunded.				surfaces and are appropriately bunded.  No spills recorded in the site incident register.
– Proper invasive plant control must be undertaken quarterly.	Contractor cEO	Ensure that invasive plant control is undertaken on an ongoing basis (at least quarterly).	During the construction phase	ECO	As and when required	Photographic proof of invasive plant control being undertaken on site.
– All excess soil (soil that are stripped and stockpiled to make way for foundations) must be stored, continuously managed / maintained to be used for rehabilitation of eroded areas.	Contractor cEO	Development a procedure for the removal, handling, and storage of soil and ensure implementation of this procedure during the construction phase.	During the construction phase	ECO	Monthly	Copy of procedure for the removal, handling, and storage of soil provided during the review.  Visual observation of appropriate soil storage and handling practices on site.
– Rip all compacted areas outside of the developed areas that have been compacted.	Contractor cEO	Ensure that ripping is undertaken on all compacted areas outside of the development areas.	Following completion of the construction phase.	ECO	Monthly	Visual observation of ripping being undertaken on compacted areas outside the development areas.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Ripping must be done by means of a commercial ripper that has at least two rows of tines.	Contractor Developer	Utilise a commercial ripper with at least two rows of tines for ripping purposes.	During the construction phase	ECO	As and when required	Ripping undertaken using a commercial ripper with at least two rows of tines.
– Ripping must take place between 1 and 3 days after seeding and following a rainfall event (seeding must therefore be carried out directly after a rainfall event).	Contractor cEO	Ensure that ripping is undertaken between 1 and 3 days after seeding and following a rainfall event.	During the construction phase	ECO	As and when required	Visual observation of ripping being undertaken between 1 and 3 days after seeding and following a rainfall event.

#### 7.4 Heritage

**Impact management outcome:** Impacts on archaeological and palaeontological heritage resources are reduced

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Should any significant archaeological resources be uncovered during the course of the construction phase, work must cease in the area of the find and SAHRA must be contacted regarding an appropriate way forward.	Contractor, cEO, Specialist (if required)	If any evidence of unrecorded archaeological resources or possible burials is observed during the course of construction activities, all work must cease immediately within	Duration of Construction Phase	ECO, cEO	Ongoing (cEO), Monthly (ECO)	Evidence of communication with SAHRA where any evidence of unrecorded archaeological resources or possible burials is found

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		the vicinity of the find and the find be reported to the SAHRA.				
<p>– The Chance Fossil Finds Procedure must be implemented for the duration of construction activities:</p> <ul style="list-style-type: none"> <li>○ Once alerted to fossil occurrence(s): alert site foreman, stop work in area immediately (N.B. safety first!), safeguard site with security tape / fence / sand bags if necessary.</li> <li>○ Record key data while fossil remains are still in situ: <ul style="list-style-type: none"> <li>* Accurate geographic location – describe and mark on site map / 1: 50 000 map / satellite image / aerial photo.</li> <li>* Context – describe position of fossils within stratigraphy (rock layering), depth below surface.</li> <li>* Photograph fossil(s) in situ with scale, from different angles, including images showing context (e.g. rock layering).</li> </ul> </li> <li>○ If feasible to leave fossils in situ: <ul style="list-style-type: none"> <li>* Alert Heritage Resources Agency and project palaeontologist (if any) who will advise on any necessary mitigation.</li> <li>* Ensure fossil site remains safeguarded until clearance is given by the Heritage Resources Agency for work to resume.</li> </ul> </li> <li>○ If not feasible to leave fossils in situ (emergency procedure only):</li> </ul>	Developer, Contractor	The chance fossil finds procedure must be include in the contractor's pack	During the construction phase	ECO	Monthly	Chance fossil finds procedure is included in the contractor's pack and evidence of implementation of the procedure is observed

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul style="list-style-type: none"> <li>* Carefully remove fossils, as far as possible still enclosed within the original sedimentary matrix (e.g. entire block of fossiliferous rock).</li> <li>* Photograph fossils against a plain, level background, with scale.</li> <li>* Carefully wrap fossils in several layers of newspaper / tissue paper / plastic bags.</li> <li>* Safeguard fossils together with locality and collection data (including collector and date) in a box in a safe place for examination by a palaeontologist.</li> <li>* Alert Heritage Resources Agency and project palaeontologist (if any) who will advise on any necessary mitigation.</li> </ul> <ul style="list-style-type: none"> <li>o If required by Heritage Resources Agency, ensure that a suitably-qualified specialist palaeontologist is appointed as soon as possible by the developer.</li> </ul> <p>Implement any further mitigation measures proposed by the palaeontologist and Heritage Resources Agency.</p>						

## 7.5 Visual

**Impact management outcome:** Visual impact of construction activities on sensitive visual receptors, and the potential impact on the sense of place is reduced.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
- Retain and maintain natural vegetation immediately adjacent to the development footprint.	Project proponent/ design consultant  Contractor  cEO	Visual inspection of the layout to ensure that vegetation immediately adjacent to the development footprint will not be disturbed  Ensure that natural vegetation immediately adjacent to the development footprint/servitude is retained and maintained.	Prior to construction and during construction	ECO	Ongoing throughout construction	Onsite evidence that natural vegetation immediately adjacent to the development footprint/servitude is retained and maintained.
- Ensure that vegetation is not unnecessarily removed during the construction phase.	Contractor  cEO	Visual inspection of the project site to ensure that no unnecessary vegetation clearance is being undertaken.  Include this mitigation in the contractor's environmental awareness training.	During construction	ECO	Daily, during the vegetation clearance phase and monthly thereafter	Onsite evidence that not unnecessary vegetation clearance is being undertaken.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<p>– Plan the placement of laydown areas and temporary construction equipment camps in order to minimise vegetation clearing (i.e., in already disturbed areas) wherever possible.</p>	<p>Project proponent/ design consultant</p> <p>Contractor</p> <p>cEO</p>	<p>Ensure that temporary construction infrastructure in the final layout is placed within already disturbed areas, where possible.</p> <p>Ensure that temporary construction infrastructure is established within already disturbed areas, where possible, during the construction phase.</p>	<p>Prior to construction and during construction</p>	<p>ECO</p>	<p>Once-off review of the final layout prior to construction and as and when required during the construction phase</p>	<p>Photographic proof that temporary construction infrastructure is placed in already disturbed areas, where possible.</p> <p>Final layout shows placement of temporary construction infrastructure within already disturbed areas.</p>
<p>– Restrict the activities and movement of construction workers and vehicles to the immediate construction site and existing access roads.</p>	<p>Contractor</p>	<p>Demarcate construction site to restrict movement within the construction site and immediate area. Inform the contractors, through inclusion of this condition in the environmental</p>	<p>Duration of the construction phase</p>	<p>ECO</p>	<p>Monthly</p>	<p>Reduced duration of the construction phase. Copy of construction programme provided during audit</p>

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		awareness training and contractor's packs, that movement should be restricted to existing access roads.				
– Ensure that rubble, litter, and disused construction materials are appropriately stored (if not removed daily) and then disposed regularly at licensed waste facilities.	Contractor	Waste to be appropriately stored in designated areas.  Disposal of waste at licensed waste disposal facilities must be undertaken as per the waste management plan	Duration of the construction phase	ECO	Monthly	Appropriate storage of waste in designated areas.  Disposal certificates of disposal at licensed facilities to be provided
– Reduce and control construction dust using approved dust suppression techniques as and when required (i.e. whenever dust becomes apparent).	Contractor	Apply appropriate dust suppression techniques.	Duration of the construction phase	ECO	Weekly	Contractor to provide proof of use of appropriate dust suppression technique. Photographic evidence that dust suppression is being undertaken on site



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
- Restrict construction activities to daylight hours whenever possible in order to reduce lighting impacts.	Developer Contractor cEO	Ensure that working hours are clearly communicated to construction workers and that the working hours are restricted to daylight hours and are adhered to.	Duration of the construction phase	ECO	Daily	Limited construction activities taking place at night.
- Rehabilitate all disturbed areas immediately after the completion of construction works.	Contractor cEO	Ensure that disturbed areas are rehabilitated immediately after completion of construction works and that this is communicated to the contractor.  Develop and implement a rehabilitation plan for the site.	Following completion of construction	ECO	As and when required	Visual observation that disturbed areas are rehabilitated immediately after the completion of construction works.

## 7.6 Socio-Economic

**Impact management outcome:** Enhanced socio-economic development and reduction in potential negative social impacts.

Impact Management Actions	Implementation	Monitoring
---------------------------	----------------	------------

	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<p>– Where reasonable and practical, the proponent should appoint local contractors and implement a 'locals first' policy, especially for semi and low-skilled job categories. However, due to the low skills levels in the area, the majority of skilled posts are likely to be filled by people from outside the area.</p>	Developer	Develop and implement a "locals first" policy for the provision of employment opportunities	Prior to construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	The "locals first" policy is considered in terms of the employment and training opportunities
<p>– Where feasible, efforts should be made to employ local contractors that are compliant with Broad Based Black Economic Empowerment (BBBEE) criteria.</p>	Developer	Develop and implement a "locals first" policy for the provision of employment opportunities that states that first preference will be given to contractors that are compliant with BBBEE criteria	Prior to construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	The "locals first" policy is considered in terms of the employment and gives first preference to contractors that are compliant with BBBEE criteria
<p>– Before the construction phase commences the proponent should meet with representatives from the ELM to establish the existence of a skills database for the area. If such a database exists it should be made available to the contractors appointed for the construction phase.</p>	Developer	Identify and implement appropriate strategies for communication with representatives from the MLM	Prior to construction	ECO	Once, prior to the commencement of construction and monthly during the construction	Communication is undertaken as per the identified strategies and evidence of the meeting with the MLM (meeting minutes) is provided during the audit
<p>– The local authorities, community representatives, and organisations on the interested and affected party database should be informed of the final decision</p>	Developer	Identify and implement appropriate	Prior to construction	ECO	Once, prior to the commencement of construction	Evidence indicating that interested and

regarding the project and the potential job opportunities for locals and the employment procedures that the proponent intends following for the construction phase of the project.		strategies to communicate the availability of job opportunities to interested and affected parties and ensure that all interested and affected parties are aware of the job opportunities associated with the project			and monthly during the construction	affected parties were informed of the job opportunities is provided during the audit
- Where feasible, training and skills development programmes for locals should be initiated prior to the initiation of the construction phase.	Developer	Develop and implement a "locals first" policy for the provision of employment opportunities	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	The "locals first" policy is considered in terms of the employment and training opportunities
- The recruitment selection process should seek to promote gender equality and the employment of women wherever possible.	Developer	Develop and implement a "locals first" policy for the provision of employment opportunities and ensure that the policy promotes gender equality and women empowerment	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	The "locals first" policy, which promotes gender equality and women empowerment is considered in terms of the employment
- The proponent should liaise with the ELM with regards the establishment of a database of local companies, specifically BBBEE companies, which qualify as potential service providers (e.g., construction	Developer	Establish communication channels with the ULM	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly	Documentary evidence indicating liaison between the

companies, catering companies, waste collection companies, security companies etc.) prior to the commencement of the tender process for construction contractors. These companies should be notified of the tender process and invited to bid for project-related work.					during the construction phase	developer and the ULM
– Where possible, the proponent should make it a requirement for contractors to implement a 'locals first' policy for construction jobs, specifically for semi and low-skilled job categories.	Developer	Develop and implement a "locals first" policy for the provision of employment opportunities	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	The "locals first" policy is considered in terms of the employment
– Ongoing consultation with stakeholders must be undertaken throughout the construction phase.	Developer	Establish communication channels with stakeholders and implement a grievance mechanism	During the construction phase	ECO	Monthly	Documentary evidence indicating liaison between the developer and stakeholders
– The proponent and the contractor(s) should develop a code of conduct for the construction phase. The code should identify which types of behaviour and activities are not acceptable. Construction workers in breach of the code should be dismissed. All dismissals must comply with the South African labour legislation.	Developer, in consultation with the Monitoring Forum	Develop and implement code of conduction for the construction phase	Prior to construction and during the construction phase	ECO	Monthly	Code of conduct evident during audit
– The proponent and the contractor should implement an HIV/AIDS awareness programme for all construction workers at the outset of the construction phase.	cEO / Contractor in consultation with the ECO	The effects of sexually transmitted diseases and HIV/AIDS must be covered in the Environmental Awareness Training	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during construction	Environmental awareness training material requirements checklist

- The contractor should provide transport for workers to and from the site on a daily basis. This will enable the contractor to effectively manage and monitor the movement of construction workers on and off the site.	cEO	Provide daily transport to and from site for employees	During the Construction Phase	ECO	Monthly, and as and when required	Proof of transportation services provided
- The contractor must ensure that all construction workers from outside the area are transported back to their place of residence within 2 days for their contract coming to an end.	cEO	Provide transport from site to employees within 2 days of their contract coming to an end	Towards the end of the construction phase	ECO	As and when required, towards the end of the construction phase	Proof of transportation services provided
- It is recommended that no construction workers, with the exception of security personnel, should be permitted to stay over-night on the site.	Not Applicable - no on-site housing is envisaged with daily commute to and from site expected of construction staff.					
- The proponent should enter into an agreement with the local farmers in the area whereby damages to farm property etc. during the construction phase will be compensated for. The agreement should be signed before the construction phase commences.	DPM Contractor	Develop agreements for compensation for the damage of farm property etc. with the affected landowners. Ensure that agreements are approved and signed	Pre-construction	dEO ECO	Once, prior to construction	Availability of approved and signed agreements
- Traffic movement and construction related activities should be contained within clearly designated areas.	Contractor, cEO	Ensure that traffic and activities are contained within designated areas	During the construction phase	ECO	Weekly	Traffic and activities are contained within designated areas
- Strict traffic speed limits must be enforced on the farm.	cEO / dEO / Contractor	Inform all drivers of speed limits and place appropriate signage along the relevant roads	During the construction and operation phase	ECO Operation and Maintenance team	Monthly	No complaints regarding speeding on site are received

<p>– All farm gates must be closed after passing through.</p>	<p>DSS and Contractor</p>	<p>Ensure farm gates are closed after passing through as required through the implementation of a formalised process</p>	<p>During the construction phase</p>	<p>cEO</p>	<p>Weekly and as and when required</p>	<p>Farm gates are closed after passing through and no complaints from landowners are received.</p>
<p>– Contractors appointed by the proponent should provide daily transport for low and semi-skilled workers to and from the site. This would reduce the potential risk of trespassing on the remainder of the farm and adjacent properties.</p>	<p>cEO</p>	<p>Provide daily transport to and from site for employees</p>	<p>During the construction phase</p>	<p>ECO</p>	<p>Monthly, and as and when required</p>	<p>Proof of transportation services provided during audit</p>
<p>– The proponent should hold contractors liable for compensating farmers and communities in full for any stock losses and/or damage to farm infrastructure that can be linked to construction workers. This should be contained in the Code of Conduct to be signed between the proponent, the contractors' and neighbouring landowners. The agreement should also cover loses and costs associated with fires caused by construction workers or construction related activities (see below).</p>	<p>DPM Contractor</p>	<p>Develop agreements with the contractors regarding their liability for compensating farmers and communities in full for any stock losses and/or damage to farm infrastructure that can be linked to construction workers. Ensure that agreements are approved and signed</p>	<p>Pre-construction</p>	<p>dEO ECO</p>	<p>Once, prior to construction</p>	<p>Availability of approved and signed agreement</p>
<p>– The Environmental Management Plan (EMP) must outline procedures for managing and storing waste on site, specifically plastic waste that poses a threat to livestock if ingested.</p>	<p>cEO</p>	<p>Ensure that the EMP contains measures for managing and storing waste on site</p>	<p>Pre-construction and during the construction and operation phase</p>	<p>dEO, ECO, cEO</p>	<p>Once, at the onset of the construction phase, and again on the onset of</p>	<p>Measures for managing and storing waste included in the EMP and the</p>

					the operation phase	implementation thereof observed during audit
– Contractors appointed by the proponent must ensure that all workers are informed at the outset of the construction phase of the conditions contained on the Code of Conduct, specifically consequences of stock theft and trespassing on adjacent farms.	cEO and Contractor in consultation with the ECO	Compile a Code of Conduct for staff. Ensure that the conditions of the Code of Conduct are communicated staff at the outset of construction	Pre-construction	ECO	Once, prior to the commencement of construction	No complaints registered in this regard
– Contractors appointed by the proponent must ensure that construction workers who are found guilty of stealing livestock and/or damaging farm infrastructure are dismissed and charged. This should be contained in the Code of Conduct. All dismissals must be in accordance with South African labour legislation.	Developer	Compile a Code of Conduct for staff. Ensure that any dismissals are done in accordance with South African labour legislation	During the construction phase	ECO	As and when necessary	No complaints from dismissed staff  Code of Conduct observed during audit
– No construction workers, with the exception of security personnel, should be permitted to stay over-night on the site.	Not Applicable - no on-site housing is envisaged with daily commute to and from site expected of construction staff.					
– Contractor should ensure that open fires on the site for cooking or heating are not allowed except in designated areas.	ECO / cEO / dEO	Hold environmental awareness training workshops. Training material should include the fact that open fires for cooking or heating are prohibited, in designated areas	Pre-construction construction and operations	ECO dEO	Monthly and as and when required	Attendance register and training minutes / notes for the record
– Smoking on site should be confined to designated areas.		Erect signage indicating designated	Construction and operations	ECO dEO cEO	Monthly, and as and when required	Photographic evidence of signage

		smoking areas, and ensure that smoking is only confined to these areas				indicating designated smoking areas
<p>– Contractor to ensure that construction related activities that pose a potential fire risk, such as welding, are effectively managed and are confined to areas where the risk of fires has been reduced. Measures to reduce the risk of fires include avoiding working in high wind conditions when the risk of fires is greater. In this regard special care should be taken during the high risk dry, windy winter months.</p>	dEO / cEO / Contractor	<p>Ensure that construction related activities that pose a potential fire risk, such as welding, are effectively managed and are confined to areas where the risk of fires has been reduced</p> <p>Develop environmental awareness training material which covers conditions under which work should not be undertaken to reduce the risk of fires</p>	Pre-construction, construction and operations	ECO	Prior to the commencement of the environmental awareness training, once during the construction phase and once during the operation phase	<p>No fire outbreaks occurred</p> <p>Environmental awareness training material observed</p>
<p>– Contractor should provide adequate fire-fighting equipment on-site, including a fire fighting vehicle.</p>	Contractor	The site must be fitted with adequate fire-fighting equipment	During the Construction Phase	ECO	Monthly	Adequate fire-fighting equipment is available and has been serviced



- Contractor to provide fire-fighting training to selected construction staff.	cEO and Contractor	Provide training on the use of fire-fighting equipment to the relevant employees	Pre-construction	ECO	Once, prior to the commencement of construction	Proof of training to be provided by the contractor
- As per the conditions of the Code of Conduct, in the event of a fire being caused by construction workers and or construction activities, the appointed contractors must compensate farmers for any damage caused to their farms. The contractor should also compensate the fire-fighting costs borne by farmers and local authorities.	DPM Contractor	Develop agreements with the contractors regarding their liability for damage as a result of fires caused by construction workers and or construction activities. Ensure that agreements are approved and signed	Pre-construction	dEO ECO	Once, prior to construction	Availability of approved and signed agreement
- Dust suppression measures must be implemented on un-surfaced roads, such as wetting on a regular basis and ensuring that vehicles used to transport sand and building materials are fitted with tarpaulins or covers.	Contractor	Appropriate dust suppression measures are implemented	During the construction phase	cEO, ECO	Weekly	Photographic record of measures being implemented and the results thereof
- All vehicles must be road-worthy, and drivers must be qualified and made aware of the potential road safety issues and need for strict speed limits.	cEO / dEO / Contractor	Regular inspection of vehicles  Inform all drivers of speed limits and place appropriate signage along the relevant roads	During construction and operations	ECO  Operation and Maintenance team	Monthly	No complaints from community members are submitted  Vehicle inspection checklists available

– An Environmental Control Officer (ECO) should be appointed to monitor the construction phase. The Environmental Control Officer (ECO) should conduct regular inspections (daily or weekly) of affected farms to ensure farm gates are closed and damage to fences is addressed timeously.	Developer	Ensure that an ECO is appointed prior to the commencement of construction activities	Pre-construction	cEO	Once, prior to construction	Appointment letter provided for review
– Ongoing communication with landowners and road users during the construction period.	dEO / cEO	Identify and implement appropriate strategies for communication with landowners and road users	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction	Communication is undertaken as per the identified strategies and no complaints are submitted regarding communication
– Establishment of a Grievance Mechanism that provides local farmers and other road users with an effective and efficient mechanism to address issues related to construction related impacts, including damage to local gravel farm roads.	Contractor	Development and implement a Grievance Mechanism which provides procedures for communication / liaison with neighbouring landowners and residents	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	Communication / liaison with neighbouring landowners and residents are undertaken in line with the requirements of the Grievance Mechanism. No complaints on communication with neighbouring landowners and residents is submitted
– Repair of all affected road portions at the end of construction period where required.	dEO / cEO	Record the conditions of private roads to be	During the construction	ECO	Prior to the use of private roads and	Photographic record and proof of the

		used (prior to use) and get into an agreement with the landowner on requirement for repairing of the affected roads portions at the end of the construction period	phase and post-construction		after completion of construction	road conditions pre-construction  Agreement between the developer and landowner
- Implementation of a road maintenance programme throughout the construction phase to ensure that the affected roads are maintained in a good condition and repaired once the construction phase is completed.	Contractor	Develop and implement a road maintenance programme that provides procedures on how affected roads can be maintained in good condition	Pre-construction & Construction	ECO	Once, prior to the commencement of construction and monthly during the construction phase	Road maintenance programme available on file and no bad road conditions resulting from the construction activities are observed

## OPERATIONAL PHASE OUTCOMES AND ACTIONS

### 7.7 Ecology (Fauna and Flora)

**Impact management outcome:** Direct loss and/or fragmentation of indigenous natural vegetation is minimised

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Restrict impact to development footprint only and limit disturbance creeping into surrounding areas.	Operator	Place a barricade around the development footprint to indicate that no disturbance is allowed beyond that point	During the operational phase	dEO	Monthly	No evidence of disturbance beyond the development footprint
– Protect sensitive features and habitats during operation activities.	Design Engineer and Operator	Develop a facility layout that avoids areas of high sensitivity  Provide layout to the operator and demarcate areas of high sensitivity	Prior to and during the operational phase	dEO	Monthly	Infrastructure avoids areas of high sensitivity
– Compile a rehabilitation plan	Operator, cEO	Make operator aware of the requirement for a rehabilitation plan for the site	During the operational phase	dEO	Monthly	Rehabilitation Plan available on request
– Implement Alien Plant Management Plan, including monitoring, to ensure minimal impacts on surrounding areas.	Operator, cEO	Make operator aware of the requirement for an alien plant management plan for the site	During the operational phase	dEO	Monthly	Alien Plant Management Plan available on request
– No additional clearing of vegetation should take place during the operation phase without a proper assessment of the environmental impacts and authorization from	Operator	Place a barricade around the development footprint to indicate	During the operational phase	dEO	Monthly	No vegetation clearing observed beyond the

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
relevant authorities, unless for maintenance purposes, in which case all reasonable steps should be taken to limit damage to natural areas		that no disturbance is allowed beyond that point				barricaded development footprint

**Impact management outcome:** Establishment and spread of declared weeds and alien invader plants is minimised

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Undertake regular monitoring to detect alien invasions early so that they can be controlled.	Operator	Prepare alien management plan for implementation for the duration of the operational phase	During the operational phase	dEO	Monthly	Alien Plant Management Plan available on request

**Impact management outcome:** Runoff and erosion are reduced

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Compile and implement a stormwater management plan.	Operator	Make operator aware of the requirement for a stormwater management plan for the site	During the operational phase	dEO	Monthly	Stormwater Management Plan available on request
– Speed limits should be set for all roads on site, as well as access roads to the site. These limits should not exceed 40 km/h, but may be set lower, depending on local circumstances. Strict enforcement of speed limits should occur – install speed control measures, such as speed humps, if necessary.	Operator	Install speed signature throughout site, include speed limit into induction and ensure all staff entering site is aware of the requirement to implement speed limits. Institute verbal and written warnings for violations and appropriate fines for repeat contraventions. Written log of fines and warning issued kept on site	During the operational phase	dEO	Monthly	Minimal instances of speeding as observed on site during audits and as evidenced in the written log of warnings and fines issued for contraventions

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Maintain adequate buffer zones around hydrological features so that these do not become degraded from runoff and erosion	Design Engineer and Operator	Ensure layout has been informed by the environmental sensitivities as determined by the environmental impact assessment and specialist studies	Prior to and during the operational phase	dEO	Once off review that the layout used is the approved one, and monthly thereafter	Hydrological features clearly demarcated  No evidence of construction activities taking place within the 'no-go' areas during audit
– Surface runoff and erosion must be properly controlled during the operational phase, and any issues addressed as quickly as possible.	Contractor	Implement measures for the control and management of runoff	During the operation phase	dEO	Monthly	No mismanagement of runoff

**Impact management outcome:** Minimal to no impacts to fauna species

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– No dogs or other pets should be allowed on site, except those confined to landowners' dwellings.	Operator, cEO	Include topic on 'no dogs allowed on site' in induction training material	During the operational phase	dEO	Monthly	Topic on 'no dogs allowed on site' included in induction training material

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Timeframe	Evidence of compliance
– Personnel on site should undergo environmental induction training, including the need to abide by speed limits, the increased risk of collisions with wild animals on roads in rural areas.	cEO, Operator	Include topic on speed limits and collision with wild animals in induction material	During the operational phase	dEO	Monthly	Topic on speed limits and collision with wild animals included in induction material
– Proper waste management must be implemented, ensuring no toxic or dangerous substances are accessible to wildlife. This should also apply to stockpiles of new and used materials to ensure that they do not become a hazard.	Operator	Compile a waste management plan for implementation during the operational phase	During the operational phase	dEO	Monthly	Waste management plan available on site and waste is being managed in accordance with the plan
– No collecting, hunting or poaching of any animal species should take place. Report any mortality of protected species to conservation authorities.	cEO, Operator	Requirement for induction of all staff prior to entry, in particular about the collection, hunting or harvesting of and animals	Duration of the project	dEO	Monthly	No evidence of fauna mortality, and induction roster of all staff completed, maintained and available on site

## 7.8 Avifauna

**Impact management outcome:** Mortality of priority species due to collision and electrocution with the 132kV power line is reduced.



Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<p>– The avifaunal specialist must conduct a walk-through prior to implementation to demarcate sections of power line that need to be marked with Eskom approved bird flight diverters. The bird flight diverters should be installed on the full span length on the earthwire (according to Eskom guidelines - five metres apart). Light and dark colour devices must be alternated to provide contrast against both dark and light backgrounds respectively. These devices must be installed as soon as the conductors are strung.</p>	Developer, Specialist	Appoint specialist prior to construction to undertake a detailed walk-through survey prior to implementation to demarcate sections of power line that need to be marked with Eskom approved bird flight diverters.	Pre-operation	dEO	Once at the commencement of the operational phase	Walk-through report produced and kept on file  Bird flight diverters appropriately placed along the power line
<p>– Construction of the power line must be undertaken using an approved bird friendly pole/tower design in accordance with the Distribution Technical Bulletin relating to bird friendly structures. The avifaunal specialist must sign off on the final design.</p>	Developer and Design Engineer and Operator	Investigate bird friendly pole/tower designs and ensure that the towers ultimately constructed are bird friendly	Pre-operation and during the operational phase	dEO	Once off at the commencement of the operational phase	Bird friendly towers are utilised

## 7.9 Land Use, Soils and Agricultural Potential

**Impact management outcome:** Minimise loss of land capability

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Prevent any spills from occurring. Machines must be parked within hard park areas and must be checked daily for fluid leaks.	Operator	Vehicle and equipment storage areas must have hard surfaces and must be appropriately bunded.	During the operational phase	dEO	Monthly	Vehicle and equipment storage areas have hard surfaces and are appropriately bunded.  No spills recorded in the site incident register.
– Proper invasive plant control must be undertaken quarterly.	Operator	Ensure that invasive plant control is undertaken on an ongoing basis (at least quarterly).	During the operational phase	dEO	As and when required	Photographic proof of invasive plant control being undertaken on site.
– Rip all compacted areas outside of the developed areas that have been compacted.	Operator	Ensure that ripping is undertaken on all compacted areas outside of the development areas.	During the operational phase	dEO	Monthly	Visual observation of ripping being undertaken on compacted areas outside the development areas.
– Ripping must be done by means of a commercial ripper that has at least two rows of tines.	Operator Developer	Utilise a commercial ripper with at least two rows of tines for ripping purposes.	During the operational phase	dEO	As and when required	Ripping undertaken using a commercial ripper with at least two rows of tines.
– Ripping must take place between 1 and 3 days after seeding and following a rainfall event (seeding must therefore be carried out directly after a rainfall event).	Operator cEO	Ensure that ripping is undertaken between 1 and 3 days after seeding	During the operational phase	dEO	As and when required	Visual observation of ripping being undertaken between 1 and 3 days after seeding

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		and following a rainfall event.				and following a rainfall event.

### 7.10 Visual

**Impact management outcome:** Visual impact on observers travelling along the roads and residents at homesteads in close proximity to the grid connection infrastructure is reduced

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Maintain the general appearance of the infrastructure.	Operator	Ensure regular maintenance of the infrastructure area is undertaken so that the appearance of the infrastructure is maintained	During the operation phase	dEO	Monthly	General appearance of the infrastructure is maintained

### 7.11 Socio-Economic

**Impact management outcome:** Enhanced socio-economic development and reduction in potential negative social impacts.

Impact Management Actions	Implementation	Monitoring

	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Implement training and skills development programs for members from the local community.	Developer	Develop and implement a "locals first" policy for the provision of employment and training opportunities	During the operation phase	dEO	Once prior to the commencement of operation and monthly during the operation phase	The "locals first" policy is considered in terms of the employment and training opportunities
– Maximise opportunities for local content and procurement.	Developer	Develop and implement a "locals first" policy in the procurement process	During the operation phase	dEO	Once prior to the commencement of operation and monthly during the operation phase	The "locals first" policy is considered in terms of procuring goods and services
– Maximise the number of employment opportunities for local community members.	Developer	Develop and implement a "locals first" policy in the procurement process	During the operation phase	dEO	Once prior to the commencement of operation and monthly during the operation phase	The "locals first" policy is considered in terms of procuring goods and services
– Where reasonable and practical, the proponent should appoint local contractors and implement a 'locals first' policy, especially for semi and low-skilled job categories. However, due to the low skills levels in the area, the majority of skilled posts are likely to be filled by people from outside the area.	Developer	Develop and implement a "locals first" policy for the provision of employment opportunities	During the operational phase	dEO	Once, prior to the commencement of the operational phase and monthly during the operational phase	The "locals first" policy is considered in terms of the employment and training opportunities
– Where feasible, efforts should be made to employ local contactors that are compliant with Broad Based Black Economic Empowerment (BBBEE) criteria.	Developer	Develop and implement a "locals first" policy for the provision of employment opportunities that states that first	During the operational phase	dEO	Once, prior to the commencement of operations and monthly during the operational phase	The "locals first" policy is considered in terms of the employment and gives first preference to

		preference will be given to contractors that are compliant with BBBEE criteria				contractors that are compliant with BBBEE criteria
– Before the construction phase commences the proponent should meet with representatives from the MLM to establish the existence of a skills database for the area. If such as database exists it should be made available to the contractors appointed for the construction phase.	Developer	Identify and implement appropriate strategies for communication with representatives from the MLM	During the operational phase	dEO	Once, prior to the commencement of operations and monthly during the operational phase	Communication is undertaken as per the identified strategies and evidence of the meeting with the MLM (meeting minutes) is provided during the audit
– The local authorities, community representatives, and organisations on the interested and affected party database should be informed of the final decision regarding the project and the potential job opportunities for locals and the employment procedures that the proponent intends following for the construction phase of the project.	Developer	Identify and implement appropriate strategies to communicate the availability of job opportunities to interested and affected parties and ensure that all interested and affected parties are aware of the job opportunities associated with the project	During the operational phase	dEO	Once, prior to the commencement of operations and monthly during the operational phase	Evidence indicating that interested and affected parties were informed of the job opportunities is provided during the audit
– Where feasible, training and skills development programmes for locals should be initiated prior to the initiation of the construction phase.	Developer	Develop and implement a "locals first" policy	Pre-operations & during the	dEO	Once, prior to the commencement of operations and	The "locals first" policy is considered in

		for the provision of employment opportunities	operational phase		monthly during the operational phase	terms of the employment and training opportunities
– The recruitment selection process should seek to promote gender equality and the employment of women wherever possible.	Developer	Develop and implement a “locals first” policy for the provision of employment opportunities and ensure that the policy promotes gender equality and women empowerment	Pre-operations & during the operational phase	dEO	Once, prior to the commencement of operations and monthly during the operational phase	The “locals first” policy, which promotes gender equality and women empowerment is considered in terms of the employment
– The proponent should liaise with the ULM with regards the establishment of a database of local companies, specifically BBBEE companies, which qualify as potential service providers (e.g., construction companies, catering companies, waste collection companies, security companies etc.) prior to the commencement of the tender process for construction contractors. These companies should be notified of the tender process and invited to bid for project-related work.	Developer	Establish communication channels with the ULM	Pre-operations & during the operational phase	dEO	Once, prior to the commencement of operations and monthly during the operational phase	Documentary evidence indicating liaison between the developer and the ULM
– Implement agreements with affected landowners.	DPM	Develop agreements for compensation of landowners for use of their properties. Ensure that agreements are approved and signed	During the operational phase	dEO	Once, prior to commencement of operations	Availability of approved and signed agreements

**Impact management outcome:** Potential risk to safety to farming operations and livestock associated with the presence of maintenance workers on the site is reduced.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
– Affected property owners should be notified in advance of the timing and duration of maintenance activities.	Developer and Operator	Ensure that affected property owners are notified of maintenance activities in advance	During the operational phase	dEO	As and when necessary	Proof of notification of maintenance activities to the affected property owners is available on site
– Maintenance teams must ensure that all farm gates must be closed after passing through.	Operator	Ensure farm gates are closed after passing through as required through the implementation of a formalised process	During the operational phase	dEO	As and when required	Farm gates are closed after passing through and no complaints from landowners are received
– Property owners should be compensated for damage to farm property and or loss of livestock or game associated maintenance related activities.	DPM Contractor	Develop agreements for compensation for the damage of farm property etc. with the affected landowners. Ensure that agreements are approved and signed	Pre-operation	dEO	Once, at the commencement of the operational phase	Availability of approved and signed agreements

<p>– Movement of traffic and maintenance related activities should be strictly contained within designated areas associated with transmission lines and substations.</p>	<p>Developer, Operator</p>	<p>Develop and implement code for the operational and maintenance phase to control the movement of maintenance staff on site</p>	<p>Prior to operations and during the operational phase</p>	<p>dEO</p>	<p>Monthly</p>	<p>Code of conduct evident during audit  No movement of traffic and maintenance related activities outside designated areas</p>
<p>– Strict traffic speed limits must be enforced on the farm.</p>	<p>Operator</p>	<p>Install speed signature throughout site, include speed limit into induction and ensure all staff entering site is aware of the requirement to implement speed limits. Institute verbal and written warnings for violations and appropriate fines for repeat contraventions. Written log of fines and warning issued kept on site</p>	<p>During the operational phase</p>	<p>dEO</p>	<p>Monthly</p>	<p>Minimal instances of speeding as observed on site during audits and as evidenced in the written log of warnings and fines issued for contraventions</p>
<p>– No maintenance workers should be allowed to stay overnight on the affected properties.</p>	<p>Not applicable – the development of new accommodation is not proposed. Employees will be accommodated in the nearby towns such as De Aar and transported to and from site daily.</p>					



## APPENDIX 1: METHOD STATEMENTS

To be prepared by the contractor prior to commencement of the activity. The method statements are **not required** to be submitted to the CA.

APPENDIX 2: CV OF THE EAP

