
# Red Sands PV2, Northern Cape Province

Environmental Management Programme for the 132kV on-site substation associated with the Red Sands PV1 Facility

April 2022

GENERIC ENVIRONMENTAL MANAGEMENT PROGRAMME (EMPr) FOR THE DEVELOPMENT AND EXPANSION OF SUBSTATION INFRASTRUCTURE FOR THE TRANSMISSION AND DISTRIBUTION OF ELECTRICITY



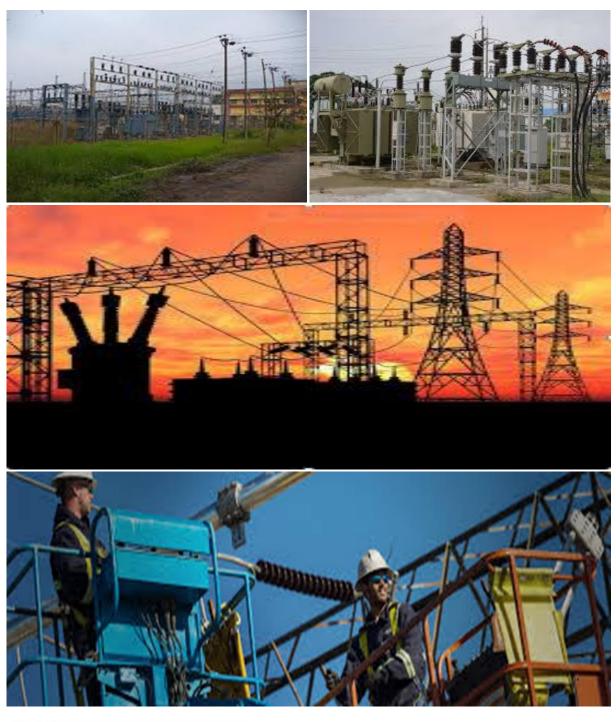

environmental affairs

Department: Environmental Affairs REPUBLIC OF SOUTH AFRICA

# TABLE OF CONTENTS

INTRC	DUC	TION	1			
1.	Bac	kground	1			
2.	Purp	Purpose1				
3.	Obj	Objective1				
4.	Sco	ре	1			
5.	Stru	cture of this document	2			
6.	Cor	mpletion of part B: section 1: the pre-approved generic EMPr template	4			
7. mc		endments of the impact management outcomes and impact ement actions	4			
8. an		cuments to be submitted as part of part B: section 2 site specific informatio claration				
(a)	А	mendments to Part B: Section 2 – site specific information and declaration	5			
PART	A–G	ENERAL INFORMATION	2			
1.	DEF	INITIONS	2			
2.	AC	RONYMS and ABBREVIATIONS	3			
3. PR		.es and responsibilities for environmental management amme (empr) implementation	4			
4.	EΝV	IRONMENTAL DOCUMENTATION REPORTING AND COMPLIANCE	.0			
Z	1.1	Document control/Filing system1	.0			
Z	1.2	Documentation to be available1	.0			
Z	1.3	Weekly Environmental Checklist1	.0			
Z	1.4	Environmental site meetings1	.1			
Z	1.5	Required Method Statements1	.1			
Z	1.6	Environmental Incident Log (Diary)1	.2			
Z	1.7	Non-compliance1	.2			
Z	1.8	Corrective action records1	.3			
Z	1.9	Photographic record1	.3			
Z	4.10	Complaints register1	.4			
Z	4.11	Claims for damages1	.4			
Z	4.12	Interactions with affected parties1	.4			
Z	4.13	Environmental audits1	.5			
Z	1.14	Final environmental audits1	.5			
PART	B: SEC	CTION 1: Pre-approved generic EMPr template1	6			

	5.	IMPA	CT MANAGEMENT OUTCOMES AND IMPACT MANAGEMENT ACTIONS	16
		5.1	Environmental awareness training	17
		5.2	Site Establishment development	20
		5.3	Access restricted areas	22
		5.4	Access roads	23
		5.5	Fencing and Gate installation	26
		5.6	Water Supply Management	31
		5.7	Storm and waste water management	32
		5.8	Solid and hazardous waste management	34
		5.9	Protection of watercourses and estuaries	37
		5.10	Vegetation clearing	40
		5.11	Protection of fauna	44
		5.12	Protection of heritage resources	48
		5.13	Safety of the public	49
		5.14	Sanitation	51
		5.15	Prevention of disease	53
		5.16	Emergency procedures	56
		5.17	Hazardous substances	58
		5.18	Workshop, equipment maintenance and storage	65
		5.19	Batching plants	67
		5.20	Dust emissions	70
		5.21	Blasting	73
		5.22	Noise	74
		5.23	Fire prevention	75
		5.24	Stockpiling and stockpile areas	77
		5.25	Civil works	79
		5.26	Excavation of foundation, cable trenching and drainage systems	81
	5.27	Installation of foundations, cable trenching and drainage systems	83	
	5.28 Insula	Installation of equipment (circuit breakers, current Transformers, Isolat ators, surge arresters, voltage transformers, earth switches)		
		5.30	Cabling and Stringing	87
		5.31 syste	Testing and Commissioning (all equipment testing, earthing system, m integration)	89
		5.32	Socio-economic	89

	5.33	Temporary closure of site
	5.34	Dismantling of old equipment95
	5.35	Landscaping and rehabilitation97
6	AC	CESS TO THE GENERIC EMPr101
PAR	T B: SEC	CTION 2
7	SITE	SPECIFIC INFORMATION AND DECLARATION
	7.1	Sub-section 1: contact details and description of the project
	7.2	Sub-section 2: Development footprint site map
	7.3	Sub-section 3: Declaration
	7.4	Sub-section 4: amendments to site specific information (Part B; section 2) 115
PAR	T C	
8	SITE	SPECIFIC ENVIRONMENTAL ATTRIBUTES
APP	ENDIX	133 EXAMPLE 133

# List of tables

Table 1: Guide to roles and responsibilities for implementation of an EMPr ......4

# INTRODUCTION

#### 1. Background

The National Environmental Management Act, 1998 (Act No. 107 of 1998) (NEMA) requires that an environmental management programme (EMPr) be submitted where an environmental impact assessment (EIA) has been identified as the environmental instrument to be utilised as the basis for a decision on an application for environmental authorisation (EA). The content of an EMPr must either contain the information set out in Appendix 4 of the Environmental Impact Assessment Regulations, 2014, as amended (EIA Regulations) or must be a generic EMPr relevant to an application as identified and gazetted by the Minister in a government notice. Once the Minister has identified, through a government notice that a generic EMPr is relevant to an application for EA, that generic EMPr must be applied by all parties involved in the EA process, including but not limited to the applicant and the competent authority (CA).

#### 2. Purpose

This document constitutes a generic EMPr relevant to applications for the development or expansion of substation infrastructure for the transmission and distribution of electricity, and all listed and specified activities necessary for the realisation of such infrastructure.

#### 3. Objective

The objective of this generic EMPr is to prescribe and pre-approve generally accepted impact management outcomes and impact management actions, which can commonly and repeatedly be used for the avoidance, management and mitigation of impacts and risks associated with the development or expansion of substation infrastructure for the transmission and distribution of electricity. The use of a generic EMPr is intended to reduce the need to prepare and review individual EMPrs for applications of a similar nature.

#### 4. Scope

The scope of this generic EMPr applies to the development or expansion of substation infrastructure for the transmission and distribution of electricity requiring EA in terms of NEMA. This generic EMPr applies to activities requiring EA, mainly activity 11 and 47 of the Environmental Impact Assessment Regulations Listing Notice 1 of 2014, as amended, and activity 9 of the Environmental Impact Assessment Regulations Listing Notice 2 of 2014, as amended, and all associated listed or specified activities necessary for the realization of such infrastructure.

# 5. Structure of this document

Part	Section	Heading	Content
A		Provides general guidance and information and is <b>not</b> <b>legally binding</b>	Definitions, acronyms, roles & responsibilities and documentation and reporting.
В	1	Pre-approved generic EMPr template	Contains generally accepted impact management outcomes and impact management actions required for the avoidance, management and mitigation of impacts and risks associated with the development or expansion of substation infrastructure for the transmission and distribution of electricity, which are presented in the form of a template that has been pre- approved.
			The template in this section is to be completed by the contractor, with each completed page signed and dated by the holder of the EA prior to commencement of the activity.
			Where an impact management outcome is not relevant, the words "not applicable" can be inserted in the template under the "responsible persons" column.
			Once completed and signed, the template represents the EMPr for the activity approved by the CA and is legally binding. The template <b>is</b> <b>not required</b> to be submitted to the CA as once the generic EMPr is gazetted for implementation, it has been approved by the CA.
			To allow interested and affected parties access to the pre-approved EMPr template for consideration through the decision-making process, the EAP on behalf of the applicant /proponent must make the hard copy of this EMPr available at a public location and where the applicant has a website, the EMPr should also be made available on such publicly accessible website.
	2	Site specific information	Contains preliminary infrastructure layout and a declaration that the applicant/holder of the EA

This document is structured in three parts with an Appendix as indicated in the table below:

Part	Section	Heading	Content
			will comply with the pre-approved generic EMPr template contained in <u>Part B: Section 1</u> , and understands that the impact management outcomes and impact management actions are <b>legally binding</b> . The preliminary infrastructure layout must be finalized to inform the final EMPr that is to be submitted with the basic assessment report (BAR) or environmental impact assessment report (EIAR), ensuring that all impact management outcomes and impact management actions have been either pre- approved or approved in terms of <u>Part C</u> . This section <b>must be</b> submitted to the CA together with the final BAR or EIAR. The information submitted to the CA will be considered to be incomplete should a signed copy of <u>Part B: section 2</u> not be submitted. Once approved, this Section forms part of the EMPr for
С		Site specific sensitivities/ attributes	the development and is legally binding. If any specific environmental sensitivities/ attributes are present on the site which require site specific impact management outcomes and impact management actions, not included in the pre-approved generic EMPr, to manage impacts, these specific impact management outcomes and impact management actions must be included in this section. These specific environmental attributes must be referenced spatially and impact management outcomes and impact management actions must be provided. These specific impact management outcomes and impact management actions must be presented in the format of the pre- approved EMPr template (Part B: section 1)
			This section will not be required should the site contain no specific environmental sensitivities or attributes. However, if <u>Part C</u> is applicable to the site, it <b>is required</b> to be submitted together with the BAR or EIAR, for consideration of, and decision on, the application for EA. The information in this section must be prepared by an EAP and must contain his/her name and expertise including a curriculum vitae. Once

Part	Section	Heading	Content
			approved, Part C forms part of the EMPr for the site and is legally binding.
			This section applies only <b>to additional</b> impact management outcomes and impact management actions that are necessary for the avoidance, management and mitigation of impacts and risks associated with the specific development or expansion and which are not already included in <u>Part B: section 1</u> .
Appendix 1			Contains the method statements to be prepared prior to commencement of the activity. The method statements are <b>not required</b> to be submitted to the competent authority.

# 6. Completion of part B: section 1: the pre-approved generic EMPr template

The template is to be completed prior to commencement of the activity, by providing the following information for each environmental impact management action:

- For implementation
  - a 'responsible person',
  - a method for implementation,
  - a timeframe for implementation
- For monitoring
  - a responsible person
  - frequency
  - evidence of compliance.

The completed template must be signed and dated by the holder of the EA prior to commencement of the activity. The method statements prepared and agreed to by the holder of the EA must be appended to the template as <u>Appendix 1</u>. Each method statement must be signed and dated on each page by the holder of the EA. This template once signed and dated is legally binding. The holder of the EA will remain responsible for its implementation.

#### 7. Amendments of the impact management outcomes and impact management actions

Once the activity has commenced, a holder of an EA may make amendments to the impact management outcomes and impact management actions in the following manner:

- Amendment of the impact management outcomes: in line with the process contemplated in Regulation 37 of the EIA Regulations; and
- Amendment of the impact management actions: in line with the process contemplated in Regulation 36 of the EIA Regulations.

# 8. Documents to be submitted as part of part B: section 2 site specific information and declaration

<u>Part B: Section 2</u> has three distinct sub-sections. The first and third sub-sections are in a template format. Sub-section two requires a map to be produced.

<u>Sub-section 1</u> contains the project name, the applicant's name and contact details, the site information, which includes coordinates of the property or farm in which the proposed substation infrastructure is proposed as well as the 21-digit Surveyor General code of each cadastral land parcel and, where available, the farm name.

<u>Sub-section 2</u> is to be prepared by an EAP and must contain his/her name and expertise including a curriculum vitae. This sub-section must include a map of the site sensitivity overlaid with the preliminary infrastructure layout using the national web based environmental screening tool, when available for compulsory use at: <u>https://screening.environment.gov.za/screeningtool.</u> The sensitivity map shall identify the nature of each sensitive feature e.g. threatened plant species, archaeological site, etc. Sensitivity maps shall identify features both within the planned working area and any known sensitive features and within 50 m from the development footprint.

<u>Sub-section 3</u> is the declaration that the applicant (s)/proponent (s) or holder of the EA in the case of a change of ownership must complete which confirms that the applicant/EA holder will comply with the pre-approved 'generic EMPr' template in <u>Section 1</u> and understands that the impact management outcomes and impact management actions are legally binding.

# (a) Amendments to Part B: Section 2 – site specific information and declaration

Should the EA be transferred, <u>Part B: Section 2</u> must be completed by the new applicant/proponent and submitted with the application for an amendment of the EA in terms of regulations 29 or 31 of the EIA Regulations, whichever applies. The information submitted as part of such an application for an amendment to an EA will be considered to be incomplete should a signed copy of <u>Part B: Section 2</u> not be submitted. Once approved, <u>Part B: Section 2</u> forms part of the EMPr for the development and the EMPr becomes legally binding to the new EA holder.

# PART A – GENERAL INFORMATION

# 1. **DEFINITIONS**

In this EMPr any word or expression to which a meaning has been assigned in the NEMA or EIA Regulations has that meaning, and unless the context requires otherwise –

"clearing" means the clearing and removal of vegetation, whether partially or in whole, including trees and shrubs, as specified;

"construction camp" is the area designated for key construction infrastructure and services, including but not limited to offices, overnight vehicle parking areas, stores, the workshop, stockpile and lay down areas, hazardous storage areas (including fuels), the batching plant (if one is located at the construction camp), designated access routes, equipment cleaning areas and the placement of staff accommodation, cooking and ablution facilities, waste and wastewater management;

"**contractor**" - The Contractor has overall responsibility for ensuring that all work, activities, and actions linked to the delivery of the contract, are in line with the Environmental Management Programme and that Method Statements are implemented as described.

"hazardous substance" is a substance governed by the Hazardous Substances Act, 1973 (Act No. 15 of 1973) as well as the Hazardous Chemical and Substances Regulations, 1995;

"method statement" means a written submission by the Contractor to the Project Manager in response to this EMPr or a request by the Project Manager and ECO. The method statement must set out the equipment, materials, labour and method(s) the Contractor proposes using to carry out an activity identified by the Project Manager when requesting the Method Statement. This must be done in such detail that the Project Manager and ECO is able to assess whether the Contractor's proposal is in accordance with this specification and/or will produce results in accordance with this specification;

The method statement must cover as a minimum applicable details with regard to:

- (i) Construction procedures;
- (ii) Plant, materials and equipment to be used;
- (iii) Transporting the equipment to and from site;
- (iv) How the plant/ material/ equipment will be moved while on site;
- (v) How and where the plant/ material/ equipment will be stored;
- (vi) The containment (or action to be taken if containment is not possible) of leaks or spills of any liquid or material that may occur;
- (vii) Timing and location of activities;
- (viii) Compliance/ non-compliance; and
- (ix) Any other information deemed necessary by the Project Manager.

"slope" means the inclination of a surface expressed as one unit of rise or fall for so many horizontal units;

"**solid waste**" means all solid waste, including construction debris, hazardous waste, excess cement/ concrete, wrapping materials, timber, cans, drums, wire, nails, food and domestic waste (e.g. plastic packets and wrappers);

**"spoil"** means excavated material which is unsuitable for use as material in the construction works or is material which is surplus to the requirements of the construction works;

**"topsoil"** means a varying depth (up to 300 mm) of the soil profile irrespective of the fertility, appearance, structure, agricultural potential, fertility and composition of the soil;

"works" means the works to be executed in terms of the Contract

# 2. ACRONYMS and ABBREVIATIONS

<b>C</b> A	Compositoret Authority
CA	Competent Authority
cEO	Contractors Environmental Officer
dEO	Developer Environmental Officer
DPM	Developer Project Manager
DSS	Developer Site Supervisor
EAR	Environmental Audit Report
ECA	Environmental Conservation Act No. 73 of 1989
ECO	Environmental Control Officer
EA	Environmental Authorisation
EIA	Environmental Impact Assessment
ERAP	Emergency Response Action Plan
EMPr	Environmental Management Programme
	Report
EAP	Environmental Assessment Practitioner
FPA	Fire Protection Agency
HCS	Hazardous chemical Substance
NEMA	National Environmental Management Act, 1998 (Act No. 107 of 1998)
NEMBA	National Environmental Management: Biodiversity Act ,2004 (Act No. 10 of 2004)
NEMWA	National Environmental Management: Waste Act, 2008 (Act No. 59 of 2008)
MSDS	Material Safety Data Sheet
RI&AP's	Registered Interested and affected parties

# 3. ROLES AND RESPONSIBILITIES FOR ENVIRONMENTAL MANAGEMENT PROGRAMME (EMPr) IMPLEMENTATION

The effective implementation of this generic EMPr is dependent on established and clear roles, responsibilities and reporting lines within an institutional framework. This section of the EMPr gives guidance to the various environmental roles and reporting lines, however, project specific requirements will ultimately determine the need for the appointment of specific person(s) to undertake specific roles and or responsibilities. As such, it must be noted that in the event that no specific person, for example, an environmental control officer (ECO) is appointed, the holder of the EA remains responsible for ensuring that the duties indicated in this document for action by the ECO are undertaken.

Responsible Person(s)	Role and Responsibilities
Developer's Project Manager (DPM)	Role         The Project Developer is accountable for ensuring compliance with the EMPr and any conditions of approval from the competent authority (CA). Where required, an environmental control officer (ECO) must be contracted by the Project Developer to objectively monitor the implementation of the EMPr according to relevant environmental legislation, and the conditions of the environmental authorisation (EA). The Project Developer is further responsible for providing and giving mandate to enable the ECO to perform responsibilities, and he must ensure that the ECO is integrated as part of the project team while remaining independent.         Responsibilities
	<ul> <li>Be fully conversant with the conditions of the EA;</li> <li>Ensure that all stipulations within the EMPr are communicated and adhered to by the Developer and its Contractor(s);</li> <li>Issuing of site instructions to the Contractor for corrective actions required;</li> <li>Monitor the implementation of the EMPr throughout the project by means of site inspections and meetings. Overall management of the project and EMPr implementation; and</li> <li>Ensure that periodic environmental performance audits are undertaken on the project implementation.</li> </ul>

**Table 1:** Guide to roles and responsibilities for implementation of an EMPr

Responsible Person(s)	Role and Responsibilities
Developer Site Supervisor (DSS)	Role The DSS reports directly to the DPM, oversees site works, liaises with the contractor(s) and the ECO. The DSS is responsible for the day to day implementation of the EMPr and for ensuring the compliance of all contractors with the conditions and requirements stipulated in the EMPr.
	<ul> <li><u>Responsibilities</u></li> <li>Ensure that all contractors identify a contractor's Environmental Officer (cEO);</li> <li>Must be fully conversant with the conditions of the EA. Oversees site works, liaison with Contractor, DPM and ECO;</li> </ul>
	<ul> <li>Must ensure that all landowners have the relevant contact details of the site staff, ECO and cEO;</li> <li>Issuing of site instructions to the Contractor for corrective actions required;</li> <li>Will issue all non-compliances to contractors; and</li> <li>Ratify the Monthly Environmental Report.</li> </ul>
Environmental Control Officer (ECO)	Role The ECO should have appropriate training and experience in the implementation of environmental management specifications. The primary role of the ECO is to act as an independent quality controller and monitoring agent regarding all environmental concerns and associated environmental impacts. In this respect, the ECO is to conduct periodic site inspections, attend regular site meetings, pre-empt problems and suggest mitigation and be available to advise on incidental issues that arise. The ECO is also required to conduct compliance audits, verifying the monitoring reports submitted by the cEO. The ECO provides feedback to the DSS and Project Manager regarding all environmental matters. The Contractor, cEO and dEO are answerable to the Environmental Control Officer for non-compliance with the Performance Specifications as set out in the EA and EMPr.
	The ECO provides feedback to the DSS and Project Manager, who in turn reports back to the Contractor and potential and Registered Interested &Affected Parties' (RI&AP's), as required. Issues of non-compliance raised by the ECO must be taken up by the Project Manager, and resolved with the Contractor as per the conditions of his contract. Decisions regarding environmental procedures, specifications and requirements which have a cost implication (i.e. those that are deemed to be a variation, not allowed for in the

Responsible Person(s)	Role and Responsibilities
	Performance Specification) must be endorsed by the Project Manager. The ECO must also, as specified by the EA, report to the relevant CA as and when required.
	<ul> <li><u>Responsibilities</u></li> <li>The responsibilities of the ECO will include the following: <ul> <li>Be aware of the findings and conclusions of all EA related to the development;</li> <li>Be familiar with the recommendations and mitigation measures of this EMPr;</li> <li>Be conversant with relevant environmental legislation, policies and procedures, and ensure compliance with them;</li> <li>Undertake regular and comprehensive site inspections / audits of the construction site according to the generic EMPr and applicable licenses in order to monitor compliance as required;</li> <li>Educate the construction team about the management measures contained in the EMPr and</li> </ul> </li> </ul>
	<ul> <li>environmental licenses;</li> <li>Compilation and administration of an environmental monitoring plan to ensure that the environmental management measures are implemented and are effective;</li> <li>Monitoring the performance of the Contractors and ensuring compliance with the EMPr and associated Method Statements;</li> <li>In consultation with the Developer Site Supervisor order the removal of person(s) and/or equipment which are in contravention of the specifications of the EMPr and/or environmental licenses;</li> <li>Liaison between the DPM, Contractors, authorities and other lead stakeholders on all environmental environmental environmental</li> </ul>
	<ul> <li>concerns;</li> <li>Compile a regular environmental audit report highlighting any non-compliance issues as well as satisfactory or exceptional compliance with the EMPr;</li> <li>Validating the regular site inspection reports, which are to be prepared by the contractor Environmental Officer (cEO);</li> <li>Checking the cEO's record of environmental incidents (spills, impacts, legal transgressions etc.) as well as corrective and preventive actions taken;</li> <li>Checking the cEO's public complaints register in which all complaints are recorded, as well as action taken;</li> </ul>

Responsible Person(s)	Role and Responsibilities
	<ul> <li>Assisting in the resolution of conflicts;</li> <li>Facilitate training for all personnel on the site – this may range from carrying out the training, to reviewing the training programmes of the Contractor;</li> <li>In case of non-compliances, the ECO must first communicate this to the Senior Site Supervisor, who has the power to ensure this matter is addressed. Should no action or insufficient action be taken, the ECO may report this matter to the authorities as non-compliance;</li> <li>Maintenance, update and review of the EMPr; and</li> <li>Communication of all modifications to the EMPr to the relevant stakeholders.</li> </ul>
developer Environmental Officer (dEO)	Role         The dEOs will report to the Project Manager and are responsible for implementation of the EMPr, environmental monitoring and reporting, providing environmental input to the Project Manager and Contractor's Manager, liaising with contractors and the landowners as well as a range of environmental coordination responsibilities.
	<ul> <li>Responsibilities</li> <li>Be fully conversant with the EMPr;</li> <li>Be familiar with the recommendations and mitigation measures of this EMPr, and implement these measures;</li> <li>Ensure that all stipulations within the EMPr are communicated and adhered to by the Employees, Contractor(s);</li> <li>Confine the development site to the demarcated area;</li> <li>Conduct environmental internal audits with regards to EMPr and authorisation compliance (on cEO);</li> <li>Assist the contractors in addressing environmental challenges on site;</li> <li>Assist in incident management:</li> <li>Reporting environmental incidents to developer and ensuring that corrective action is taken, and lessons learnt shared;</li> <li>Assist the contractor in investigating environmental incidents and compile investigation reports;</li> <li>Follow-up on pre-warnings, defects, non-conformance reports;</li> </ul>

Responsible Person(s)	Role and Responsibilities
	<ul> <li>Measure and communicate environmental performance to the Contractor;</li> <li>Conduct environmental awareness training on site together with ECO and cEO;</li> <li>Ensure that the necessary legal permits and / or licenses are in place and up to date; and</li> <li>Acting as Developer's Environmental Representative on site and work together with the ECO and contractor.</li> </ul>
Contractor	Role         The Contractor appoints the cEO and has overall responsibility for ensuring that all work, activities, and actions linked to the delivery of the contract are in line with the EMPr and that Method Statements are implemented as described. External contractors must ensure compliance with this EMPr while performing the onsite activities as per their contract with the Project Developer. The contractors are required, where specified, to provide Method Statements setting out in detail how the impact management actions contained in the EMPr will be implemented during the development or expansion of substation infrastructure for the transmission and distribution of electricity activities.         Responsibilities       -       project delivery and quality control for the development services as per appointment;
	<ul> <li>employ a suitably qualified person to monitor and report to the Project Developer's appointed person on the daily activities on-site during the construction period;</li> <li>ensure that safe, environmentally acceptable working methods and practices are implemented and that equipment is properly operated and maintained, to facilitate proper access and enable any operation to be carried out safely;</li> <li>attend on site meeting(s) prior to the commencement of activities to confirm the procedure and designated activity zones; and</li> <li>ensure that contractors' staff repair, at their own cost, any environmental damage as a result of a contravention of the specifications contained in EMPr, to the satisfaction of the ECO.</li> </ul>

Responsible Person(s)	Role and Responsibilities
contractor Environmental Officer (cEO)	Role Each Contractor affected by the EMPr should appoint a cEO, who is responsible for the on-site implementation of the EMPr (or relevant sections of the EMPr). The Contractor's representative can be the site agent; site engineer; a dedicated environmental officer; or an independent consultant. The Contractor must ensure that the Contractor's Representative is suitably qualified to perform the necessary tasks and is appointed at a level such that she/he can interact effectively with other site Contractors, labourers, the Environmental Control Officer and the public. As a minimum the cEO shall meet the following criteria:
	<ul> <li><u>Responsibilities</u></li> <li>Be on site throughout the duration of the project and be dedicated to the project;</li> <li>Ensure all their staff are aware of the environmental requirements, conditions and constraints with respect to all of their activities on site;</li> <li>Implementing the environmental conditions, guidelines and requirements as stipulated within the EA, EMPr and Method Statements;</li> <li>Attend the Environmental Site Meeting;</li> <li>Undertaking corrective actions where non-compliances are registered within the stipulated timeframes;</li> <li>Report back formally on the completion of corrective actions;</li> <li>Assist the ECO in maintaining all the site documentation;</li> <li>Prepare the site inspection reports and corrective action reports for submission to the ECO;</li> <li>Assist the ECO with the preparing of the monthly report; and</li> <li>Where more than one Contractor is undertaking work on site, each company appointed as a Contractor will appoint a cEO representing that company.</li> </ul>

# 4. ENVIRONMENTAL DOCUMENTATION REPORTING AND COMPLIANCE

To ensure accountable and demonstrated implementation of the EMPr, a number of reporting systems, documentation controls and compliance mechanisms must be in place for all substation infrastructure projects as a minimum requirement.

4.1 Document control/Filing system

The holder of the EA is solely responsible for the upkeep and management of the EMPr file. As a minimum, all documentation detailed below will be stored in the EMPr file. A hard copy of all documentation shall be filed, while an electronic copy may be kept where relevant. A duplicate file will be maintained in the office of the DSS (where applicable). This duplicate file must remain current and up-to-date. The filing system must be updated and relevant documents added as required. The EMPr file must be made available at all times on request by the CA or other relevant authorities. The EMPr file will form part of any environmental audits undertaken as prescribed in the EIA Regulations.

4.2 Documentation to be available

At the outset of the project the following preliminary list of documents shall be placed in the filing system and be accessible at all times:

- Full copy of the signed EA from the CA in terms of NEMA, granting approval for the development or expansion;
- Copy of the generic and site specific EMPr as well as any amendments thereof;
- Copy of declaration of implementing generic EMPr and subsequent approval of site specific EMPr and amendments thereof;
- All method statements;
- Completed environmental checklists;
- Minutes and attendance register of environmental site meetings;
- An up-to-date environmental incident log;
- A copy of all instructions or directives issued;
- A copy of all corrective actions signed off. The corrective actions must be filed in such a way that a clear reference is made to the non-compliance record; and
- Complaints register.

#### 4.3 Weekly Environmental Checklist

The ECOs are required to complete a Weekly Environmental Checklist, the format of which is to be agreed prior to commencement of the activity. The ECOs are required to sign and date the checklist, retain a copy in the EMPr file and submit a copy of the completed checklist to the DSS on a weekly basis.

The checklists will form the basis for the Monthly Environmental Reports. Copies of all completed checklists will be attached as Annexures to the Environmental Audit Report as required in terms of the EIA Regulations.

#### 4.4 Environmental site meetings

Minutes of the environmental site meetings shall be kept. The minutes must include an attendance register and will be attached to the Monthly Report that is distributed to attendees. Each set of minutes must clearly record "Matters for Attention" that will be reviewed at the next meeting.

4.5 Required Method Statements

The method statement will be done in such detail that the ECOs are enabled to assess whether the contractor's proposal is in accordance with the EMPr.

The method statement must cover applicable details with regard to:

- development procedures;
- materials and equipment to be used;
- getting the equipment to and from site;
- how the equipment/ material will be moved while on site;
- how and where material will be stored;
- the containment (or action to be taken if containment is not possible) of leaks or spills of any liquid or material that may occur;
- timing and location of activities;
- compliance/ non-compliance with the EMPr; and
- any other information deemed necessary by the ECOs.

Unless indicated otherwise by the Project Manager, the Contractor shall provide the following method statements to the Project Manager no less than 14 days prior to the commencement date of the activity:

- Site establishment Camps, Lay-down or storage areas, satellite camps, infrastructure;
- Batch plants;
- Workshop or plant servicing;
- Handling, transport and storage of Hazardous Chemical Substance's;
- Vegetation management Protected, clearing, aliens, felling;
- Access management Roads, gates, crossings etc.;
- Fire plan;
- Waste management transport, storage, segregation, classification, disposal (all waste streams);
- Social interaction complaints management, compensation claims, access to properties etc.;
- Water use (source, abstraction and disposal), access and all related information, crossings and mitigation;
- Emergency preparedness Spills, training, other environmental emergencies;
- Dust and noise management methodologies;
- Fauna interaction and risk management only if the risk was identified wildlife interaction especially on game farms; and
- Heritage and palaeontology management.

The ECOs shall monitor and ensure that the contractors perform in accordance with these method statements. Completed and agreed method statements between the holder of the EA and the contractor shall be captured in Appendix 1.

4.6 Environmental Incident Log (Diary)

The ECOs are required to maintain an up-to-date and current Environmental Incident Log (environmental diary). The Environmental Incident Log is a means to record all environmental incidents and/or all non-compliance notice would not be issued. An environmental incident is defined as:

- Any deviation from the listed impact management actions (listed in this EMPr) that may be addressed immediately by the ECOs. (For example a contractor's staff member littering or a drip tray that has not been emptied);
- Any environmental impact resulting from an action or activity by a contractor in contravention of the environmental stipulations and guidelines listed in the EMPr which as a single event would have a minor impact but which if cumulative and continuous would have a significant effect (for example no toilet paper available in the ablutions for an afternoon); and
- General environmental information such as road kills or injured wildlife.

The ECOs are to record all environmental incidents in the Environmental Incident Log. All incidents regardless of severity must be reported to the Developer. The Log is to be kept in the EMPr file and at a minimum the following will be recorded for each environmental incident:

- The date and time of the incident;
- Description of the incident;
- The name of the Contractor responsible;
- The incident must be listed as significant or minor;
- If the incident is listed as significant, a non-compliance notice must be issued, and recorded in the log;
- Remedial or corrective action taken to mitigate the incident; and
- Record of repeat minor offences by the same contractor or staff member.

The Environmental Incident Log will be captured in the Environmental Audit Report (EAR).

4.7 Non-compliance

A non-compliance notice will be issued to the responsible contractor by the ECOs via the DSS or Project Manager. The non-compliance notice will be issued in writing; a copy filed in the EMPr file and will at a minimum include the following:

- Time and date of the non-compliance;
- Name of the contractor responsible;
- Nature and description of the non-compliance;
- Recommended / required corrective action; and
- Date by which the corrective action to be completed.

The contractors shall act immediately when a notice of non-compliance is received and correct whatever is the cause for the issuing of the notice. Complaints received regarding

activities on the development site pertaining to the environment shall be recorded in a dedicated register and the response noted with the date and action taken. The ECO should be made aware of any complaints. Any non-compliance with the agreed procedures of the EMPr is a transgression of the various statutes and laws that define the manner by which the environment is managed. Failure to redress the cause shall be reported to the relevant CA for them to deal with the transgression, as it deems fit. The contractor is deemed not to have complied with the EMPr if, inter alia, There is a deviation from the environmental conditions, impact management outcomes and impact management actions activities, as approved in generic and site specific EMPr as relevant as set out in the EMPr, which deviation has, or may cause, an environmental impact.

4.8 Corrective action records

For each non-compliance notice issued, a documented corrective action must be recorded. On receiving a non-compliance notice from the DSS, the contractor's cEO will ensure that the corrective actions required take place within the stipulated timeframe. On completion of the corrective action the cEO is to issue a Corrective Action Report in writing to the ECOs. If satisfied that the corrective action has been completed, the ECOs are to sign-off on the Corrective Action Report, and attach the report to the non-compliance notice in the EMPr file. A corrective action is considered complete once the report has signed off by the ECOs.

#### 4.9 Photographic record

A digital photographic record will be kept. The photographic record will be used to show before, during and post rehabilitation evidence of the project as well used in cases of damages claims if they arise. Each image must be dated and a brief description note attached.

The Contractor shall:

1. Allow the ECOs access to take photographs of all areas, activities and actions.

The ECOs shall keep an electronic database of photographic records which will include:

- 1. Pictures of all areas designated as work areas, camp areas, development sites and storage areas taken before these areas are set up;
- 2. All bunding and fencing;
- 3. Road conditions and road verges;
- 4. Condition of all farm fences;
- 5. Topsoil storage areas;
- 6. All areas to be cordoned off during construction;
- 7. Waste management sites;
- 8. Ablution facilities (inside and out);
- 9. Any non-conformances deemed to be "significant";
- 10. All completed corrective actions for non-compliances;
- 11. All required signage;
- 12. Photographic recordings of incidents;
- 13. All areas before, during and post rehabilitation; and
- 14. Include relevant photographs in the Final Environmental Audit Report.

# 4.10 Complaints register

The ECOs shall keep a current and up-to-date complaints register. The complaints register is to be a record of all complaints received from communities, stakeholders and individuals. The Complaints Record shall:

- 1. Record the name and contact details of the complainant;
- 2. Record the time and date of the complaint;
- 3. Contain a detailed description of the complaint;
- 4. Where relevant and appropriate, contain photographic evidence of the complaint or damage (ECOs to take relevant photographs); and
- 5. Contain a copy of the ECOs written response to each complaint received and keep a record of any further correspondence with the complainant. The ECO's written response will include a description of any corrective action to be taken and must be signed by the Contractor, ECO and affected party. Where a damage claim is issued by the complainant, the ECOs shall respond as described in (section 4.11) below.
- 4.11 Claims for damages

In the event that a Claim for Damages is submitted by a community, landowner or individual, the ECOs shall:

- 1. Record the full detail of the complaint as described in (section 4.10) above;
- 2. The DPM will evaluate the claim and associated damage and submit the evaluation to the Senior Site Representative for approval;
- 3. Following consideration by the DPM, the claim is to be resolved and settled immediately, or the reason for not accepting the claim communicated in writing to the claimant. Should the claimant not accept this, the ECO shall, in writing report the incident to the Developer's negotiator and legal department; and
- 4. A formal record of the response by the ECOs to the claimant as well as the rectification of the method of making payments not amount will be recorded in the EMPr file.
- 4.12 Interactions with affected parties

Open, transparent and good relations with affected landowners, communities and regional staff are an essential aspect to the successful management and mitigation of environmental impacts.

The ECOs shall:

- 1. Ensure that all queries, complaints and claims are dealt within an agreed timeframe;
- 2. Ensure that any or all agreements are documented, signed by all parties and a record of the agreement kept in the EMPr file;
- 3. Ensure that a complaints telephone numbers are made available to all landowners and affected parties; and
- 4. Ensure that contact with affected parties is courteous at all times;

#### 4.13 Environmental audits

Internal environmental audits of the activity and implementation of the EMPr must be undertaken. The findings and outcomes included in the EMPr file and submitted to the CA at intervals as indicated in the EA.

The ECOs must prepare a monthly EAR. The report will be tabled as the key point on the agenda of the Environmental Site Meeting. The Report is submitted for acceptance at the meeting and the final report will be circulated to the Project Manager and filed in the EMPr file. At a frequency determined by the EA, the ECOs shall submit the monthly reports to the CA. At a minimum the monthly report is to cover the following:

- Weekly Environmental Checklists;
- Deviations and non-compliances with the checklists;
- Non-compliances issued;
- Completed and reported corrective actions;
- Environmental Monitoring;
- General environmental findings and actions; and
- Minutes of the Bi-monthly Environmental Site Meetings.

#### 4.14 Final environmental audits

On final completion of the rehabilitation and/or requirements of the EA a final EAR is to be prepared and submitted to the CA. The EAR must comply with Appendix 7 of the EIA Regulations.

# PART B: SECTION 1: Pre-approved generic EMPr template

#### 5. IMPACT MANAGEMENT OUTCOMES AND IMPACT MANAGEMENT ACTIONS

This section provides a pre-approved generic EMPr template with aspects that are common to the development of substation infrastructure for the transmission and distribution of electricity. There is a list of aspects identified for the development or expansion of substation infrastructure for the transmission and distribution of electricity, and for each aspect a set of prescribed impact management outcomes and associated impact management actions have been identified. Holders of EAs are responsible to ensure the implementation of these outcomes and actions for all projects as a minimum requirement, in order to mitigate the impact of such aspects identified for the development or expansion of substation infrastructure for the transmission and distribution of electricity.

The template provided below is to be completed by providing the information under each heading for each environmental impact management action.

The completed template must be signed and dated on each page by both the contractor and the holder of the EA prior to commencement of the activity. The method statements prepared and agreed to by the holder of the EA must be appended to the template as Appendix 1. Each method statement must also be duly signed and dated on each page by the contactor and the holder of the EA. This template, once signed and dated, is legally binding. The holder of the EA will remain responsible for its implementation.

# 5.1 Environmental awareness training

Impact management outcome: All onsite staff are aware and understands the individual responsibilities in terms of this EMPr.

Impact Management Actions	Implementation	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>All staff must receive environmental awareness training prior to commencement of the activities;</li> </ul>	ECO / cEO / dEO	Hold environmental awareness training workshops	Pre-construction Construction and Operations	ECO dEO	Monthly and as and when required	Attendance register and training minutes / notes for the record
<ul> <li>The Contractor must allow for sufficient sessions to train all personnel with no more than 20 personnel attending each course;</li> </ul>	Contractor	Scheduling of sufficient sessions through consultation with the ECO / cEO / dEO	Pre-construction Construction	ECO dEO	Monthly and as and when required	Attendance register and training minutes / notes for the record
<ul> <li>Refresher environmental awareness training is available as and when required;</li> </ul>	cEO / dEO in consultation with the ECO	Hold refresher environmental awareness training workshops	During the construction phase	ECO dEO	Monthly and as and when required	Attendance register and training minutes / notes for the record
<ul> <li>All staff are aware of the conditions and controls linked to the EA and within the EMPr and made aware of their individual roles and responsibilities in achieving compliance with the EA and EMPr;</li> </ul>	cEO / dEO	Hold training workshops and ensure that the EA and EMPr is readily available	During the construction phase	ECO dEO	Monthly and as and when required	Attendance register and training minutes / notes for the record

<ul> <li>The Contractor must erect and maintain information posters at key locations on site, and the posters must include the following information as a minimum:</li> <li>a) Safety notifications; and</li> <li>b) No littering.</li> </ul>	Contractor	Develop and place appropriate posters at key locations	Pre-construction Construction	ECO dEO cEO	Monthly	Photographic record
<ul> <li>Environmental awareness training must include as a minimum the following: <ul> <li>a) Description of significant environmental impacts, actual or potential, related to their work activities;</li> <li>b) Mitigation measures to be implemented when carrying out specific activities;</li> <li>c) Emergency preparedness and response procedures;</li> <li>d) Emergency procedures;</li> <li>e) Procedures to be followed when working near or within sensitive areas;</li> <li>f) Wastewater management procedures;</li> <li>g) Water usage and conservation;</li> <li>h) Solid waste management procedures;</li> <li>i) Sanitation procedures;</li> <li>j) Fire prevention; and</li> <li>k) Disease prevention.</li> </ul> </li> </ul>	cEO / dEO in consultation with the ECO	Develop environmental awareness training material which covers the minimum requirements	Pre-construction Construction	ECO dEO	Prior to the commence ment of the environmen tal awareness training	Environment al awareness training material requirements checklist
<ul> <li>A record of all environmental awareness training courses undertaken as part of the EMPr must be available;</li> </ul>	ECO / cEO / dEO	Filing system including all proof of training (i.e. attendance register and training minutes / notes for the record)	During the construction phase	ECO dEO	Monthly	Completed and up to date filing system with proof of training
<ul> <li>Educate workers on the dangers of open and/or unattended fires;</li> </ul>	cEO / dEO in consultation with the ECO	Develop environmental awareness training	Pre-construction Construction	ECO dEO	Prior to the commence ment of the	Environment al awareness training

		material which				environmen	material
		covers the				tal	requirements
		dangers of open				awareness	checklist
		and/or				training	
		unattended fire				0	
- A staff attendance register of all staff to have received	ECO / cEO /	Filing system	During	the	ECO	Monthly	Completed
environmental awareness training must be available.	dEO	including all proof	construction		dEO		and up to
		of training (i.e.	phase				date filing
		attendance					system
		register)					inclusive of all
							attendance
							registers
- Course material must be available and presented in	ECO / cEO /	Develop	During	the	ECO	Monthly	Environment
appropriate languages that all staff can understand.	dEO	environmental	construction		dEO		al awareness
		awareness training	phase				training
		material in the					material
		required					requirements
		languages.					checklist and
		Training material					the training
		must by readily					register which
		available to all					must indicate
		staff					the language
							of the training

# 5.2 Site Establishment development

**Impact management outcome:** Impacts on the environment are minimised during site establishment and the development footprint are kept to demarcated development area.

Impact Management Actions	Implementatio	on		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
A method statement must be provided by the contractor prior to any onsite activity that includes the layout of the construction camp in the form of a plan showing the location of key infrastructure and services (where applicable), including but not limited to offices, overnight vehicle parking areas, stores, the workshop, stockpile and lay down areas, hazardous materials storage areas (including fuels), the batching plant (if one is located at the construction camp), designated access routes, equipment cleaning areas and the placement of staff accommodation, cooking and ablution facilities, waste and wastewater management;	Contractor	Development of an appropriate method statement	Pre-construction	ECO dEO	Once, prior to constructio n	the method statement which complies with the minimum requirements listed
<ul> <li>Location of camps must be within approved area to ensure that the site does not impact on sensitive areas identified in the environmental assessment or site walk through;</li> </ul>	DPM	Place construction camps outside of sensitive areas identified in the Basic Assessment Report	Pre-construction Construction	ECO dEO	Once, prior to constructio n	Availability of a layout and sensitivity map indicating avoidance of sensitive areas
<ul> <li>Sites must be located where possible on previously disturbed areas;</li> </ul>	DPM	Place site outside of sensitive areas and within previously disturbed areas	Pre-construction	ECO dEO	Once, prior to constructio n	Availability of a layout and sensitivity map indicating

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		identified in the BA				avoidance of
		Report				sensitive
						areas and
						placement
						within
						disturbed
						areas
- The camp must be fenced in accordance with Section	DPM	Design and	Pre-construction &	ECO	Once, prior	The camp is
5.5: Fencing and gate installation; and		implementation of	Construction	dEO	to	fenced in
		fencing as per the			constructio	accordance
		requirements of			n and once	with Section
		Section 5.5 of this			during the	5.5 of this
		EMPr			constructio	EMPr
					n of the	
	ļ				fencing	
- The use of existing accommodation for contractor staff,	DPM	Identify existing	Pre-construction &	ECO	Once, prior	Contractor
where possible, is encouraged.		accommodation	Construction	dEO	to	staff are
		for contactor staff			constructio	accommoda
					n	ted in existing
						accomodati
						on

# 5.3 Access restricted areas

Impact management outcome: Access to restricted areas prevented.

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Identification of access restricted areas is to be informed by the environmental assessment, site walk through and any additional areas identified during development;</li> <li>Erect, demarcate and maintain a temporary barrier with clear signage around the perimeter of any access restricted area, colour coding could be used if</li> </ul>	dEO / cEO in consultation with the ECO dEO / cEO in consultation with the ECO	Spatially demarcate access restricted areas informed by the BA Report Erect appropriate temporary barriers around access	Pre-construction At the commencement and for the	ECO	Once, prior to constructio n Monthly	Access restricted areas are identified and provided in a spatial format Access restricted areas are
appropriate; and		restricted areas	duration of the construction phase			closed-off through temporary barriers and barriers are maintained to a sufficient standard
<ul> <li>Unauthorised access and development related activity inside access restricted areas is prohibited.</li> </ul>	Contractor / dEO / cEO	Erect appropriate temporary barriers around access restricted areas and provide clear signage of restricted status	During the construction phase	ECO	Monthly, and as and when required	Photographic evidence and notes of compliance that no unauthorised access or

Impact Management Actions	Implementation			Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
						activities has
						taken place
						within the
						access
						restricted
						areas

#### 5.4 Access roads

**Impact management outcome:** Minimise impact to the environment through the planned and restricted movement of vehicles on site.

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>An access agreement must be formalised and signed by the DPM, Contractor and landowner before commencing with the activities;</li> </ul>	DPM Contractor	Develop access agreements with the affected landowners. Ensure that agreements are approved and signed	Pre-construction	dEO ECO	Once, prior to constructio n	Availability of approved and signed negotiations
<ul> <li>All private roads used for access to the servitude must be maintained and upon completion of the works, be left in at least the original condition</li> </ul>	Contractor	Undertake maintenance activities on private roads used for construction as	During the construction phase	ceo / eco	Weekly	Photographic record of the pre- construction condition

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		degradation takes place				and degradation of roads, and records of the implementati on and effectiveness of maintenance activities
<ul> <li>All contractors must be made aware of all these access routes.</li> </ul>	dEO / cEO	Develop a map illustrating all access routes associated with the project and present and provide the map to all contractors	Pre-construction Construction	ECO	Once, prior to constructio n	Access routes map readily available
<ul> <li>Any access route deviation from that in the written agreement must be closed and re-vegetated immediately, at the contractor's expense;</li> </ul>	Contractor	All access routes developed that are not in-line with the access route agreements must be closed and re- habilitated to the pre-disturbance state	Construction and Rehabilitation	CEO ECO	Bi-weekly (every two weeks)	Photographic record of the closure of access roads and re- vegetation
<ul> <li>Maximum use of both existing servitudes and existing roads must be made to minimize further disturbance through the development of new roads;</li> </ul>	Contractor (and Eskom maintenance	Existing access routes to be used must be specified	Construction and operation	cEO Operation and	Weekly	Implementati on of the

Impact Management Actions	Implementation	n		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
	staff where	and the		maintenance		approved
	relevant to	development of		team		layout
	operation)	new roads must be				
		avoided as far as				
		possible				
- In circumstances where private roads must be used, the	dEO / cEO	Record the	During the	ECO	Prior to the	Photographic
condition of the said roads must be recorded in		conditions of	construction		use of	record and
accordance with section 4.9: photographic record; prior		private roads to be	phase		private	proof of the
to use and the condition thereof agreed by the		used (prior to use)			roads	road
landowner, the DPM, and the contractor;		as per the				conditions
		requirements of				agreed upon
		section 4.9 and				with the
		agree on the				relevant
		required condition				parties
		of the roads with the landowner,				
		DPM and				
		contractor				
- Access roads in flattish areas must follow fence lines and	DPM and	Design access	Pre-construction	ECO	Once	Implementati
tree belts to avoid fragmentation of vegetated areas or	Contractor	roads to follow			during the	on of the
croplands		fence lines and			design and	approved
		avoid vegetated			once prior	layout
		areas			to	
					constructio	
					n	
- Access roads must only be developed on pre-planned	Contractor	Construction of	During the	ECO once	Once	Implementati
and approved roads.		access roads only	construction	during the	during the	on of the
		on pre-planned	phase	design	design and	approved
		and approved		dEO	weekly	layout
		access roads			during the	
					constructio	

Impact Management Actions	Implementation			Monitoring	Monitoring		
						<b>1</b>	
	Responsible	Method of	of	Timeframe fo	Responsible	Frequency	Evidence of
	person	implementation		implementation	person		compliance
						n of access	
						roads	

#### 5.5 Fencing and Gate installation

Impact management outcome: Minimise impact to the environment and ensure safe and controlled access to the site through the erection of fencing and gates where required.

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Use existing gates provided to gain access to all parts of the area authorised for development, where possible;</li> </ul>	Contractor	Identify and inform all relevant staff of the existing gates to be used	Pre-construction & Construction	dEO	Monthly	Existing gates are utilised on a frequent basis and only limited new access gates are developed
<ul> <li>Existing and new gates to be recorded and documented in accordance with section 4.9: photographic record;</li> </ul>	ECO	Existing and newgates willberecordedanddocumentedaspertherequirementsofsection 4.9	During the construction phase	ECO	Once, when the constructio n of all new gates have been completed	Photographic record of the existing and new gates as per the requirements of section4.9

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>All gates must be fitted with locks and be kept locked at all times during the development phase, unless otherwise agreed with the landowner;</li> </ul>	Contractor	Ensure all relevant gates are fitted with locks and are always locked	Construction and Operation	ECO monthly, Operation and maintenance team and cEO	Bi-weekly (every second week)	All gates are locked and no complaints from landowners are received in this regard
<ul> <li>At points where the line crosses a fence in which there is no suitable gate within the extent of the line servitude, on the instruction of the DPM, a gate must be installed at the approval of the landowner;</li> </ul>	dEO	Install new gates where required with the approval of the affected landowner	During the construction phase	ECO	Once, prior to constructio n and during the constructio n phase, as and when required	New gates are installed where the power line crosses fences
<ul> <li>Care must be taken that the gates must be so erected that there is a gap of no more than 100 mm between the bottom of the gate and the ground;</li> </ul>	Contractor	Install gates in a manner so that there is a gap of no more than 100mm between the bottom of the gate and the ground	During the construction phase	CEO	Once, during the erection of the gates during the constructio n phase	New gates installed as per the requirement
<ul> <li>Where gates are installed in jackal proof fencing, a suitable reinforced concrete sill must be provided beneath the gate;</li> </ul>	Contractor	Implement a reinforced concrete sill beneath gates installed for jackal proofing	During the construction phase	CEO	Once, during the erection of the gates during the constructio n phase	New gates installed as per the requirement

Impact Management Actions	Implementatio	on		Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
<ul> <li>Original tension must be maintained in the fence wires;</li> </ul>	Contractor	Maintain original tension of fences through required activities	During the construction phase	ECO	Monthly	No tension reduction on fence wires	
<ul> <li>All gates installed in electrified fencing must be re- electrified;</li> </ul>	Contractor	Electrify gates installed in electrified fencing	During the construction phase	ECO	Once, during the erection of the gates during the constructio n phase	Gates installed in electrified fencing is electrified	
<ul> <li>All demarcation fencing and barriers must be maintained in good working order for the duration of the development activities;</li> </ul>	Contractor	Undertake maintenance activities on fences and barriers	During the construction phase	ECO	Monthly	Photographic record of maintained fences and barriers	
<ul> <li>Fencing must be erected around the camp, batching plants, hazardous storage areas, and all designated access restricted areas, where applicable;</li> </ul>	Contractor	Fence construction camps, batching plants, hazardous storage areas and access restricted areas. Avoid sensitive flora	During the construction phase	ECO	Once during the erection of fencing	Photographic record of fences erected	
<ul> <li>Any temporary fencing to restrict the movement of life- stock must only be erected with the permission of the land owner.</li> </ul>	dEO/ cEO Contractor	Obtain written approval from the relevant landowner where temporary fencing is required to	During the construction phase	ECO	To be monitored as temporary fencing is required	Written approval to be provided by the dEO	

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible person	Method of implementation restrict livestock movement	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
<ul> <li>All fencing must be developed of high quality material bearing the SABS mark;</li> </ul>	Contractor	Make use of high quality materials approved by SABS	During the construction phase	CEO	To be monitored as fencing is erected during the constructio n phase	Use of high quality materials for fencing approved by SABS	
<ul> <li>The use of razor wire as fencing must be avoided;</li> </ul>	Contractor	Razor wire must not be sourced or used for the erection of fencing	During the construction phase	ECO	To be monitored as fencing is erected during the constructio n phase	Fences erected do not make use of razor wire	
<ul> <li>Fenced areas with gate access must remain locked after hours, during weekends and on holidays if staff is away from site. Site security will be required at all times;</li> </ul>	DSS and Contractor	Ensure fenced areas are locked as required through the implementation of a formalised process. Appoint a security company	During the construction phase	CEO	Weekly and as and when required	Fences are locked and no complaints from landowners are received. A security company is appointed	
<ul> <li>On completion of the development phase all temporary fences are to be removed;</li> </ul>	Contractor	Removal of all temporary fences	At the end of the Construction Phase	ECO dEO	Once, following the completion	No temporary fences associated	

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>The contractor must ensure that all fence uprights are appropriately removed, ensuring that no uprights are cut</li> </ul>	Contractor	Appropriate removal of all	At the end of the Construction	ECO dEO	of the constructio n phase Once, following	with the project is present following the completion of the construction phase No fence uprights
at ground level but rather removed completely.		fence uprights	Phase		the completion of the constructio n phase	associated with the project is present following the completion of the construction phase

# 5.6 Water Supply Management

Impact management outcome: Undertake responsible water usage.

Impact Management Actions	Implementation	n				Monitoring		
	Responsible person	Method implementat	of	Timeframe implementation	for n	Responsible person	Frequency	Evidence of compliance
<ul> <li>All abstraction points or bore holes must be registered with the DWS and suitable water meters installed to ensure that the abstracted volumes are measured on a daily basis;</li> </ul>	DPM and Contractor	Obtaining re registrations DWS installation water meters	levant from and of	Pre-constructio	n	CEO	To be monitored with the installation of water meters and daily during constructio n and operation	Use of high quality water meters
<ul> <li>The Contractor must ensure the following:</li> <li>a. The vehicle abstracting water from a river does not enter or cross it and does not operate from within the river;</li> <li>b. No damage occurs to the river bed or banks and that the abstraction of water does not entail stream diversion activities; and</li> <li>c. All reasonable measures to limit pollution or sedimentation of the downstream watercourse are implemented.</li> </ul>	Not applicable	- water will no	t be ab	ostracted from a	river			

Impact Management Actions	Implementatio	n				Monitoring		
	Responsible	Method	of	Timeframe	for	Responsible	Frequency	Evidence of
	person	implementa	tion	implementation	on	person		compliance
- Ensure water conservation is being practiced by:	Contractor /	Implement	the	During	the	ECO	Monthly,	Successful
a. Minimising water use during cleaning of equipment;	dEO / cEO in	required	water	construction			and as and	implementati
b. Undertaking regular audits of water systems; and	consultation	conservation	า	phase			when	on of water
c. Including a discussion on water usage and	with the ECO	measures					required	conservation
conservation during environmental awareness training.		throughout	on-site					
d. The use of grey water is encouraged.		construction	1					
		processes						

# 5.7 Storm and waste water management

Impact management outcome: Impacts to the environment caused by storm water and wastewater discharges during construction are avoided.

Impact Management Actions	Implementatio	n	Monitoring					
	Responsible	Method of	Timeframe	for	Responsible	Frequency	Evidence	of
	person	implementation	implementatio	on	person		complian	ice
<ul> <li>Runoff from the cement/ concrete batching areas must be strictly controlled, and contaminated water must be collected, stored and either treated or disposed of off- site, at a location approved by the project manager;</li> </ul>	Contractor	Implement measures for the control and management of runoff	During	the	CEO	Weekly	No mismanag ment runoff contamin d water to temporar concrete batching plant	ge of or due the y

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>All spillage of oil onto concrete surfaces must be controlled by the use of an approved absorbent material and the used absorbent material disposed of at an appropriate waste disposal facility;</li> </ul>	Contractor and cEO	Obtain approved absorbent material and make use of licensed waste disposal facilities for disposal of oil	During the Construction Phase	ECO	Monthly	Availability of approved absorbent material at the construction site and proof of disposal of oil at licensed disposal facilities
<ul> <li>Natural storm water runoff not contaminated during the development and clean water can be discharged directly to watercourses and water bodies, subject to the Project Manager's approval and support by the ECO;</li> </ul>	DPM in consultation with the ECO	Consultation between the DPM and the ECO to determine if water can be discharged directly into water bodies (where present). The necessary water quality testing must be undertaken prior to discharge	During the construction phase	ECO	As and when the need arises to discharge natural stormwater runoff and clean water	Proof of consultation between the DPM and ECO and the outcomes thereof to be provided. Proof of water quality testing and the results thereof.
<ul> <li>Water that has been contaminated with suspended solids, such as soils and silt, may be released into watercourses or water bodies only once all suspended solids have been removed from the water by settling out these solids in settlement ponds. The release of settled water back into the environment must be subject to the Project Manager's approval and support by the ECO.</li> </ul>	DPM in consultation with the ECO	Consultation between the DPM and the ECO to determine if water can be released following settling.	During the construction phase	ECO	As and when the need arises to discharge settled water	Proof of consultation between the DPM and ECO and the outcomes

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
						thereof to be
						provided.

# 5.8 Solid and hazardous waste management

Impact management outcome: Wastes are appropriately stored, handled and safely disposed of at a recognised waste facility.

Impact Management Actions	Implementation					Monitoring		
	Responsible	Method o	of	Timeframe	for	Responsible	Frequency	Evidence of
	person	implementation		implementation	n	person		compliance
- All measures regarding waste management must be	Contractor	Develop an	d	During	the	ECO	Monthly	Implementati
undertaken using an integrated waste management		implement	а	construction				on of the
approach;		waste		phase				waste
		management						management
		plan						plan and
								proof of
								waste
								management
								through proof
								of responsible
								disposal
- Sufficient, covered waste collection bins (scavenger and	Contractor	Provision c	of	During	the	cEO	Weekly	Appropriate
weatherproof) must be provided;		appropriate wast	e	construction				waste
		collection bir	าร	phase				collection

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		strategically placed throughout the site				bins are available throughout the site
<ul> <li>A suitably positioned and clearly demarcated waste collection site must be identified and provided;</li> </ul>	DPM and Contractor	Identify an appropriate location for the waste collection site which must be clearly demarcated through signage and temporary fencing	Design and Construction Phase	ECO	Once, prior to the commence ment of constructio n	A waste collection site is appropriately placed and demarcated
<ul> <li>The waste collection site must be maintained in a clean and orderly manner;</li> </ul>	Contractor	Regular collection of waste and maintenance of the area must be undertaken as per the waste requirements for the project during construction	During the Construction Phase	CEO	Weekly	The waste collection site is maintained and clean
<ul> <li>Waste must be segregated into separate bins and clearly marked for each waste type for recycling and safe disposal;</li> </ul>	Contractor	Provide separate and marked bins for the different waste types associated with the construction phase	During the Construction Phase	CEO	Weekly	Separate waste bins are available on site and waste generated is separated

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance into the	
<ul> <li>Staff must be trained in waste segregation;</li> </ul>	cEO / dEO in consultation with the ECO	Include waste segregation as part of the environmental awareness training material.	Pre-construction Construction	ECO	Monthly, and as and when required	relevant bins Environmenta I awareness training material requirements checklist	
<ul> <li>Bins must be emptied regularly;</li> </ul>	Contractor	Bins must be emptied before reaching total capacity and on a regular basis as required for the project	During the construction phase	ECO	Monthly	No mismanagem ent of bins.	
<ul> <li>General waste produced onsite must be disposed of at registered waste disposal sites/ recycling company;</li> </ul>	Contractor	Disposal of general waste at licensed waste disposal facilities must be undertaken as per the waste management plan	During the construction phase	ECO	Monthly	Disposal certificates of disposal at licensed facilities to be provided	
<ul> <li>Hazardous waste must be disposed of at a registered waste disposal site;</li> </ul>	Contractor	Disposal of hazardous waste at licensed waste disposal facilities must be undertaken as per the waste	During the construction phase	ECO	Monthly	Disposal certificates of disposal at licensed facilities to be provided	

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
		management plan					
<ul> <li>Certificates of safe disposal for general, hazardous and recycled waste must be maintained.</li> </ul>	Contractor	Obtain certificates for safe disposal of waste	During the construction phase	ECO	Monthly	Disposal certificates of disposal at licensed facilities to be provided and filed as part of the filing system	

#### 5.9 Protection of watercourses and estuaries

Impact management outcome: Pollution and contamination of the watercourse environment and or estuary erosion are prevented.

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- All watercourses must be protected from direct or	Not					
indirect spills of pollutants such as solid waste, sewage,	applicable -					
cement, oils, fuels, chemicals, aggregate tailings, wash	no					
and contaminated water or organic material resulting	watercourses					
from the Contractor's activities;	present					
- In the event of a spill, prompt action must be taken to	Contractor	Develop a	During the	cEO	Weekly	Feedback
clear the polluted or affected areas;	and cEO	management plan	construction			must be
		or process for	phase			provided by

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		implementation should a spill take place				the contractor in terms of how the spill was handled and photographi c evidence of the feedback must be provided and kept on record
<ul> <li>Where possible, no development equipment must traverse any seasonal or permanent wetland</li> </ul>	Not applicable – no watercourses present					
<ul> <li>No return flow into the estuaries must be allowed and no disturbance of the Estuarine functional Zone should occur;</li> </ul>	Not applicable – no estuaries present					
<ul> <li>Development of permanent watercourse or estuary crossing must only be undertaken where no alternative access to tower position is available;</li> </ul>	Not applicable – no watercourses present					
<ul> <li>There must not be any impact on the long term morphological dynamics of watercourses or estuaries;</li> </ul>	Not applicable - no					

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
	watercourses present					
<ul> <li>Existing crossing points must be favored over the creation of new crossings (including temporary access)</li> </ul>	Not applicable – no watercourses present					
<ul> <li>When working in or near any watercourse or estuary, the following environmental controls and consideration must be taken:         <ul> <li>a) Water levels during the period of construction;</li> <li>No altering of the bed, banks, course or characteristics of a watercourse</li> <li>b) During the execution of the works, appropriate measures to prevent pollution and contamination of the riparian environment must be implemented e.g. including ensuring that construction equipment is well maintained;</li> <li>c) Where earthwork is being undertaken in close proximity to any watercourse, slopes must be stabilised using suitable materials, i.e. sandbags or geotextile fabric, to prevent sand and rock from entering the channel; and</li> <li>d) Appropriate rehabilitation and re-vegetation measures for the watercourse banks must be implemented timeously. In this regard, the banks should be appropriately and incrementally stabilised as soon as development allows.</li> </ul> </li> </ul>	Not applicable – no watercourses present					

# 5.10 Vegetation clearing

Impact management outcome: Vegetation clearing is restricted to the authorised development footprint of the proposed infrastructure.

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
General:						
<ul> <li>Indigenous vegetation which does not interfere with the development must be left undisturbed;</li> </ul>	cEO and contractor	Demarcate areas of indigenous vegetation to be avoided before clearance is	Construction and operation (i.e. for maintenance purposes)	ECO monthly, Operation and maintenance team weekly	Weekly, and as and when required	No unnecessary clearance of indigenous vegetation is
<ul> <li>Protected or endangered species may occur on or near the development site. Special care should be taken not to damage such species;</li> </ul>	Contractor	undertakenDemarcateareascontainingprotectedprotectedorendangeredspeciestoavoidedbyconstructionactivities	During the Construction Phase	ECO monthly and Operation and maintenance team weekly	Weekly, and as and when required	undertaken No clearance of protected or endangered species other than those permitted to be removed
<ul> <li>Search, rescue and replanting of all protected and endangered species likely to be damaged during project development must be identified by the relevant specialist and completed prior to any development or clearing;</li> </ul>	Relevant specialist in consultation with the Contractor	Develop and implement a Plant Search and Rescue Plan	Pre-construction & Construction	CEO	Weekly, and as and when required	Implementati on of the Plant Search and Rescue Plan and photographi c evidence and notes of the

Impact Management Actions	Implementatic	Implementation				
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						implementati on of the plan
<ul> <li>Permits for removal must be obtained from the relevant CA prior to the cutting or clearing of the affected species, and they must be filed;</li> </ul>	DPM	Undertake the permitting process in order to obtain the relevant permits for the removal of protected species. Permits must be kept on file	Pre-construction	ECO	Once, prior to the commence ment of the constructio n phase and removal of the protected species	CA permits on file
<ul> <li>The Environmental Audit Report must confirm that all identified species have been rescued and replanted and that the location of replanting is compliant with conditions of approvals;</li> </ul>	ECO	Ensure that the audit report indicates all species rescued and replanted and provides feedback in terms of compliance with the conditions of permits for replanting	During the Construction Phase and following the completion of the Construction Phase	ECO	Once off or as and when required	ECO confirmed rescued and replanted programme implemented correctly.
<ul> <li>Trees felled due to construction must be documented and form part of the Environmental Audit Report;</li> </ul>	ECO	Ensure that the audit report documents the details of trees felled	DuringtheConstructionPhaseandfollowingthecompletion of the	ECO	Once, prior to the commence ment of the constructio n phase	CA permits on file

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
			Construction Phase		and removal of the protected species	
<ul> <li>Rivers and watercourses must be kept clear of felled trees, vegetation cuttings and debris;</li> </ul>	Contractor	Felled trees, vegetation cuttings and debris must be disposed of at a licensed waste disposal facility	During the Construction Phase	ECO	Monthly	No felled trees, vegetation cuttings and debris are dumped in inappropriate locations and disposal certificates are available as proof of responsible disposal
<ul> <li>Only a registered pest control operator may apply herbicides on a commercial basis and commercial application must be carried out under the supervision of a registered pest control operator, supervision of a registered pest control operator or is appropriately trained;</li> </ul>	DPM and Contractor	A suitably qualified pest control operator must be appointed	Construction and Operation	ECO	As and when the use of herbicides is required	Only registered pest control operators must be appointed and proof of their registration must be provided

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
<ul> <li>A daily register must be kept of all relevant details of herbicide usage;</li> </ul>	DPM and Contractor	A suitably qualified pest control operator must be appointed	Construction and Operation	ECO	As and when the use of herbicides is required	Only registered pest control operators must be appointed and proof of their registration
						must be provided
<ul> <li>No herbicides must be used in estuaries</li> </ul>	Not Applicable	e – no estuaries applic	able			
- All protected species and sensitive vegetation not	Contractor in	Spatially	During the	ECO	Once,	Demarcation
removed must be clearly marked and such areas	consultation	demarcate	construction		during the	and fencing
fenced off in accordance to Section 5.3: Access	with the cEO	protected species	phase		undertaking	is undertaken
restricted areas.		and sensitive			of the	in-line with
		vegetation and			demarcatio	the
		implement			n of the	requirements
		appropriate			areas and	of section 5.3
		fencing where			the erection	
		required as per			of the	
		section 5.3			fencing	
- Alien invasive vegetation must be removed and	Contractor	Undertake	Construction and	ECO	Monthly,	Proof must be
disposed of at a licensed waste management facility.		removal of alien	Operation	Operation	and as and	provided that
		invasive		and	when	alien invasive
		vegetation in		maintenance	required	vegetation
		accordance with		team		has been
		the relevant				cleared in
		guideline and				accordance
		ensure the				to the
		vegetation is				relevant

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		disposed of at a				guideline and
		licensed waste				that the
		disposal facility				vegetation
						was disposed
						of at a
						licensed
						waste
						disposal
						facility

#### 5.11 Protection of fauna

Impact management outcome: Disturbance to fauna is minimised.

Impact Management Actions	Implementation			Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Fraguanay	Evidence of
	person	implementation	implementation	person	Frequency	compliance
- No interference with livestock must occur without the	dEO / cEO	Develop a	Pre-construction	ECO	Once, prior	Written
landowner's written consent and with the landowner or	Contractor	procedure for	and during the		to the	consent
a person representing the landowner being present;		dealing with	construction		commence	provided by
		livestock within the	phase		ment of	the
		affected			construction	landowner
		properties			and as and	and proof of
					when	representatio
					required	n of the
					during the	landowner

Impact Management Actions	Implementation	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
					construction phase	during interference
<ul> <li>The breeding sites of raptors and other wild birds species must be taken into consideration during the planning of the development programme;</li> </ul>	dEO / cEO in consultation with the Contractor	Ensure that the planning and development programme considers breeding sites for wild bird species	Pre-construction & Construction	ECO	Once, prior to the commence ment of construction and as and when required	The planning and development programme includes the consideration of breeding sites for wild bird species
<ul> <li>Breeding sites must be kept intact and disturbance to breeding birds must be avoided. Special care must be taken where nestlings or fledglings are present;</li> </ul>	dEO / cEO in consultation with the Contractor	Avoid breeding sites and ensure that special care is taken in the presence of nestlings and fledglings	During the Construction Phase Operation Phase	ECO monthly, cEO and Operation and maintenanc e team weekly	Weekly, and as an when required during the construction . Monthly, and as and when required during operation	Photographic record of intact breeding sites
<ul> <li>Special recommendations of the avian specialist must be adhered to at all times to prevent unnecessary disturbance of birds;</li> </ul>	dEO / cEO in consultation with the Contractor	All mitigation measures recommended by the avifauna specialist must be implemented	During the Construction Phase Operation Phase	ECO Operation and maintenanc e team	Monthly during construction and monthly during operation	Photographic record of compliance and successful implementati on of the

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						recommend ed measures
<ul> <li>No poaching must be tolerated under any circumstances. All animal dens in close proximity to the works areas must be marked as Access restricted areas;</li> </ul>	dEO / cEO in consultation with the Contractor	All site staff must be informed of this requirement during the Environmental Awareness Training and the consequences of not adhering to the requirement. These areas must be demarcated as Access Restricted Areas	During the Construction Phase	ECO	Monthly, and as and when required	No instances of poaching is reported
<ul> <li>No deliberate or intentional killing of fauna is allowed;</li> </ul>	dEO / cEO in consultation with the Contractor	All site staff must be informed of this requirement during the Environmental Awareness Training and the consequences of not adhering to the requirement. These areas must be demarcated as Access Restricted Areas	During the Construction Phase	ECO	Monthly, and as and when required	No instances of deliberate or intentional killing is reported

Impact Management Actions	Implementation	n		Monitoring	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance		
<ul> <li>In areas where snakes are abundant, snake deterrents to be deployed on the pylons to prevent snakes climbing up, being electrocuted and causing power outages; and</li> </ul>	dEO / cEO in consultation with the Contractor	Implement and maintain snake deterrents on pylons in areas where snakes are abundant	During the Construction Phase Operation Phase	ECO Operation and maintenanc e team	Once, during the construction of the pylons and as and when required. Monthly during operation	Photographic record of the implementati on and maintenance of snake deterrents		
<ul> <li>No Threatened or Protected species (ToPs) and/or protected fauna as listed according NEMBA (Act No. 10 of 2004) and relevant provincial ordinances may be removed and/or relocated without appropriate authorisations/permits.</li> </ul>	DPM in consultation with the dEO	Undertake a permitting process to obtain the required permits	Pre-construction	ECO	Once, prior to the commence ment of construction and as and when required	Permits for removal and/relocati on must be kept on file and be readily available		

# 5.12 Protection of heritage resources

Impact management outcome: Impact to heritage resources is minimised.

Impact Management Actions	Implementation	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Identify, demarcate and prevent impact to all known sensitive heritage features on site in accordance with the No-Go procedure in Section 5.3: Access restricted areas;</li> </ul>	DPM and a suitably qualified specialist dEO / cEO in consultation with the Contractor and ECO	and demarcate areas of heritage significance as per the Heritage Impact Assessment and the Heritage	Pre-construction	ECO	Once, prior to the commence ment of constructio n	Proof of avoidance of sensitive heritage features through details of avoidance and photographi c records
<ul> <li>Carry out general monitoring of excavations for potential fossils, artefacts and material of heritage importance;</li> </ul>	dEO (in consultation with specialists if/as required).	Ensure construction staff are adequately informed (via environmental awareness training) to carry out monitoring of excavations for fossils, artefacts and important heritage material	During the Construction Phase	ECO	Monthly, or as required	Environment al awareness training includes measures relating to monitoring for chance finds

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- All work must cease immediately, if any human remains	dEO / cEO in	Develop and	During the	ECO	As and	Proof of work
and/or other archaeological, palaeontological and	consultation	implement	Construction		when	ceased and
historical material are uncovered. Such material, if	with the	procedures for	Phase		required	the required
exposed, must be reported to the nearest museum,	Contractor	situations where				procedures
archaeologist/ palaeontologist (or the South African	and ECO	human remains,				followed in
Police Services), so that a systematic and professional		archaeological,				cases where
investigation can be undertaken. Sufficient time must be		palaeontolgoical				material is
allowed to remove/collect such material before		or historical				discovered.
development recommences.		material are				
		uncovered				

# 5.13 Safety of the public

Impact management outcome: All precautions are taken to minimise the risk of injury, harm or complaints.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Identify fire hazards, demarcate and restrict public access to these areas as well as notify the local authority of any potential threats e.g. large brush stockpiles, fuels etc.;</li> </ul>	cEO in consultation with the Contractor	Develop an Emergency Preparedness, Response and Fire Management Plan specific to the project	Pre-construction Construction	CEO	Once, prior to the commence ment of constructio n and weekly during the	Compliance with the Emergency Preparedness , Response and Fire Managemen t Plan

Impact Management Actions	Implementatio	on		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency constructio n phase	Evidence of compliance
<ul> <li>All unattended open excavations must be adequately fenced or demarcated;</li> </ul>	Contractor	Ensure that all excavations undertaken is fenced and demarcated within a reasonable timeframe and in instances where excavations will be open for long- periods of time	During the Construction Phase	CEO	Weekly	Excavations are fenced where required and photographi c proof can be provided
<ul> <li>Adequate protective measures must be implemented to prevent unauthorised access to and climbing of partly constructed towers and protective scaffolding;</li> </ul>	Contractor	All staff must be easily identifiable and the climbing of towers and scaffolding must only be undertaken by authorised personnel as managed by the Contractor	During the construction phase	ECO	Monthly, and as and when required	No incidents of unauthorised climbing is reported
<ul> <li>Ensure structures vulnerable to high winds are secured;</li> </ul>	Contractor	Ensure that sufficient stabilisation measures are implemented to	During the construction phase	cEO	Weekly, and as and when required	No incidents of unstable structures due to high

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		secure structures				winds is
		vulnerable to high				reported
		winds				
- Maintain an incidents and complaints register in which	cEO	Compile and	During the	ECO	Monthly,	The incidents
all incidents or complaints involving the public are		regularly update	construction		and as and	and
logged.		as incidents and	phase		when	complaints
		complaints are			required	register is
		submitted from the				complete
		public and				and provides
		indicate the				all the
		actions taken to				required
		resolve the				details
		complaint				

#### 5.14 Sanitation

**Impact management outcome:** Clean and well maintained toilet facilities are available to all staff in an effort to minimise the risk of disease and impact to the environment.

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Mobile chemical toilets are installed onsite if no other ablution facilities are available;</li> </ul>	Contractor	Mobile chemical toilets must be placed appropriately and in areas that avoid	During the Construction Phase	cEO	Weekly	Mobile toilets are installed and avoid environment al sensitivities

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation environmental sensitivities	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>The use of ablution facilities and or mobile toilets must be used at all times and no indiscriminate use of the veld for the purposes of ablutions must be permitted under any circumstances;</li> </ul>	Contractor in consultation with the cEO	All site staff must be informed of this requirement during the Environmental Awareness Training and the consequences of not adhering to the requirement.	Pe-construction & Construction	ECO	Monthly, and as and when required	No evidence of non- compliance identified
<ul> <li>Where mobile chemical toilets are required, the following must be ensured:</li> <li>a) Toilets are located no closer than 100 m to any watercourse or water body;</li> <li>b) Toilets are secured to the ground to prevent them from toppling due to wind or any other cause;</li> <li>c) No spillage occurs when the toilets are cleaned or emptied and the contents are managed in accordance with the EMPr;</li> <li>d) Toilets have an external closing mechanism and are closed and secured from the outside when not in use to prevent toilet paper from being blown out;</li> <li>e) Toilets are emptied before long weekends and workers holidays, and must be locked after working hours;</li> <li>f) Toilets are serviced regularly and the ECO must inspect toilets to ensure compliance to health standards;</li> </ul>	Contractor in consultation with the cEO	The installation of the toilets by the Contractor must be as per the listed requirements	During the Construction Phase	CEO	Weekly	No evidence of non- compliance identified

Impact Management Actions	Implementatio	n	Monitoring	Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- A copy of the waste disposal certificates must be	Contractor	Certificates	During the	ECO	Monthly,	Certificates
maintained.		obtained from the	Construction		and as and	for waste
		licensed waste	Phase		when	disposal from
		disposal facility			required	the licensed
		with the emptying				waste
		of the toilets must				disposal
		be kept on file				facility
						available on
						site

#### 5.15 Prevention of disease

Impact Management outcome: All necessary precautions linked to the spread of disease are taken.

Impact Management Actions	Implementation	n		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- Undertake environmentally-friendly pest control in the	Contractor	Only	During the	ECO	As and	Contractor to
camp area;		environmentally-	Construction		when pest	provide proof
		friendly pest	Phase		control is	of pest
		control must be			required for	control used
		used, when			the project	being
		required				environment
						ally-friendly
- Ensure that the workforce is sensitised to the effects of	cEO /	The effects of	Pre-construction &	ECO	Once, prior	Environment
sexually transmitted diseases, especially HIV AIDS;	Contractor in	sexually	Construction		to the	al awareness
		transmitted			commence	training

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
	consultation with the ECO	diseases and HIV/ AIDS must be covered in the Environmental Awareness Training			ment of constructio n and monthly during constructio n	material requirements checklist
<ul> <li>The Contractor must ensure that information posters on AIDS are displayed in the Contractor Camp area;</li> </ul>	Contractor	Develop and place information posters on HIV/ AIDS	During the Construction Phase	CEO	Weekly	Photographic evidence of poster placement
<ul> <li>Information and education relating to sexually transmitted diseases to be made available to both construction workers and local community, where applicable;</li> </ul>	CEO / Contractor in consultation with the ECO	Information and education of sexually transmitted diseases must be covered in the Environmental Awareness Training.	Pre-construction & Construction	ECO	Monthly	Environment al awareness training material requirements checklist
<ul> <li>Free condoms must be made available to all staff on site at central points;</li> </ul>	Contractor	Placement of free condoms in mobile toilets and at the construction camps	During the Construction Phase	ECO	Monthly	Proof of placement of free condoms by the contractor to be provided
<ul> <li>Medical support must be made available;</li> </ul>	dEO / cEO in consultation with the Contractor	Ensure that designated personnel with first aid training are	Construction and Operations	ECO	Monthly	Check the availability of first aid trained

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		available on site and that first aid kits to provide medical support is readily available				personnel and medical kits (including if these are complete in terms of supplies)
<ul> <li>Provide access to Voluntary HIV Testing and Counselling Services.</li> </ul>	Contractor	Compile a HIV testing schedule and provide counselling services where required	During the Construction Phase	ECO	Quarterly, and as and when required	Voluntary testing schedules and proof of counselling (where undertaken)

#### 5.16 Emergency procedures

Impact management outcome: Emergency procedures are in place to enable a rapid and effective response to all types of environmental emergencies.

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Compile an Emergency Response Action Plan (ERAP) prior to the commencement of the proposed project;</li> </ul>	Contractor	Develop an Emergency Preparedness, Response and Fire Management Plan specific to the project	Pre-construction	ECO	Once, prior to the commence ment of constructio n	Emergency Preparedness , Response and Fire Managemen t Plan compiled
<ul> <li>The Emergency Plan must deal with accidents, potential spillages and fires in line with relevant legislation;</li> </ul>	Contractor	Develop an Emergency Preparedness, Response and Fire Management Plan specific to the project which covers accidents, potential spillages and fires	Pre-construction	ECO	Once, prior to the commence ment of constructio n	Emergency Preparedness , Response and Fire Managemen t Plan includes required specifications
<ul> <li>All staff must be made aware of emergency procedures as part of environmental awareness training;</li> </ul>	cEO / dEO in consultation with the ECO	Develop environmental awareness training material which covers the relevant	Pre-construction	ECO	Prior to the commence ment of the environmen tal	Environment al awareness training material requirements checklist

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		emergency procedures			awareness training	
<ul> <li>The relevant local authority must be made aware of a fire as soon as it starts;</li> </ul>	Contractor in consultation with the ECO	Develop and include a procedure in the Emergency Preparedness, Response and Fire Management Plan for the event of a fire and the procedure to be followed for informing the local authority	Construction	ECO	As and when a fire occurs	The local authority was informed as per the relevant procedure set out in the Emergency Preparedness , Response and Fire Managemen t Plan
<ul> <li>In the event of emergency necessary mitigation measures to contain the spill or leak must be implemented (see Hazardous Substances section 5.17).</li> </ul>	Contractor	Implement the required mitigation measures in the event of a spill or leak as per the requirements of Section 5.17.	Construction and Operations	ECO	As and when a spill or leak occurs	The mitigation measures included under Section 5.17 have been adhered to

#### 5.17 Hazardous substances

Impact management outcome: Safe storage, handling, use and disposal of hazardous substances.

Impact Management Actions	Implementation			Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>The use and storage of hazardous substances to be minimised and non-hazardous and non-toxic alternatives substituted where possible;</li> </ul>	cEO in consultation with the Contractor	Develop a strategy of how hazardous substances can be and should be minimised	Pre-construction & Construction	ECO	Once, prior to the commence ment of constructio n and monthly during the constructio n phase	Contractor to provide evidence of substances used for proof of compliance
<ul> <li>All hazardous substances must be stored in suitable containers as defined in the Method Statement;</li> </ul>	Contractor	Develop a Method Statement for the storage of hazardous substances in suitable containers	Pre-construction & Construction	ECO	Once, prior to the commence ment of constructio n and monthly during the constructio n phase	Photographic proof that hazardous substances are stored in suitable containers as per the requirements of the relevant Method Statements

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Containers must be clearly marked to indicate contents, quantities and safety requirements;</li> </ul>	Contractor	Where hazardous waste is stored these must be clearly marked indicating the required details of the contents	During the Construction Phase	ECO	Monthly	Photographic proof that containers are marked as per the requirements
<ul> <li>All storage areas must be bunded. The bunded area must be of sufficient capacity to contain a spill / leak from the stored containers;</li> </ul>	Contractor	Ensure that storage areas are sufficiently bunded which are of sufficient capacity to contain a spill / leak from the stored containers	During the Construction Phase	ECO	Monthly during the Constructio n Phase	Photographic proof that storage areas are bunded and proof that the bund areas are of sufficient capacity to contain a spill / leak from the stored containers
<ul> <li>Bunded areas to be suitably lined with a SABS approved liner;</li> </ul>	Contractor	Ensure that bunded storage areas are suitably lined	During the Construction Phase	ECO	Once, during the Constructio n Phase	Photographic proof that bunded storage areas are suitably lined
<ul> <li>An Alphabetical Hazardous Chemical Substance (HCS) control sheet must be drawn up and kept up to date on a continuous basis;</li> </ul>	CEO / Contractor	Compile and update an Alphabetical Hazardous Chemical	During the Construction Phase	ECO	Monthly, and as and when required	Complete and up to date control sheet provided by

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
		Substance (HCS) control sheet specific to the project				the Contractor	
<ul> <li>All hazardous chemicals that will be used on site must have Material Safety Data Sheets (MSDS);</li> </ul>	CEO / Contractor	Keep a record of all hazardous chemicals and the respective MSDS	During the Construction Phase	ECO	Monthly, and as and when required	Record of hazardous chemicals and the respective MSDS	
<ul> <li>All employees working with HCS must be trained in the safe use of the substance and according to the safety data sheet;</li> </ul>	CEO / Contractor	Provide training for personnel working with HCS	Pre-construction	ECO	Once, prior to the commence ment of constructio n and as and when required	Record of training provided to personnel working with HCS	
<ul> <li>Employees handling hazardous substances / materials must be aware of the potential impacts and follow appropriate safety measures. Appropriate personal protective equipment must be made available;</li> </ul>	cEO / Contractor	Develop environmental awareness training material which covers the relevant impacts and safety measures. Provide appropriate training and personal	Pre-construction & Construction	ECO	Prior to the commence ment of the environmen tal awareness training and monthly during the constructio n phase for personal	Environment al awareness training material requirements checklist and all relevant personnel have undergone appropriate training and have access	

Impact Management Actions	Implementation			Monitoring	Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
		protective equipment for the relevant personnel handling hazardous substances and materials			protective equipment	to personal protective equipment	
<ul> <li>The Contractor must ensure that diesel and other liquid fuel, oil and hydraulic fluid is stored in appropriate storage tanks or in bowsers;</li> </ul>	Contractor	Appropriate storage facilities must be constructed or obtained for the storing of diesel, other liquid fuel, oil and hydraulic fluid	During the Construction Phase	ECO	Monthly, and as and when required	Storage tanks for the project are appropriate and no incidents are reported in this regard	
<ul> <li>The tanks/ bowsers must be situated on a smooth impermeable surface (concrete) with a permanent bund. The impermeable lining must extend to the crest of the bund and the volume inside the bund must be 130% of the total capacity of all the storage tanks/ bowsers (110% statutory requirement plus an allowance for rainfall);</li> </ul>	Contractor	Appropriate storage facilities must be constructed or obtained for tanks as per the requirements listed	During the Construction Phase	ECO	Monthly, and as and when required	Storage areas for the tanks/ bowsers for the project are appropriate and no incidents are reported in this regard	
<ul> <li>The floor of the bund must be sloped, draining to an oil separator;</li> </ul>	Contractor	Appropriate storage facilities must be constructed as per	During the Construction Phase	ECO	Once, during constructio n	Bunded storage areas are constructed according to	

Impact Management Actions	Implementatio	on		Monitoring	Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	or Responsible person	Frequency	Evidence of compliance	
		the requirements listed				the requirements	
<ul> <li>Provision must be made for refueling at the storage area by protecting the soil with an impermeable groundcover. Where dispensing equipment is used, a drip tray must be used to ensure small spills are contained;</li> </ul>	Contractor	Appropriately constructed refuelling facility must be developed as per the requirements. Drip trays must be provided for use	During th Construction Phase	e ECO cEO	Monthly Weekly	Soils at the refuelling facility are protected as required and drip trays are provided and used	
<ul> <li>All empty externally dirty drums must be stored on a drip tray or within a bunded area;</li> </ul>	Contractor	Ensure that empty dirty drums are stored appropriately as per the requirements	During th Construction Phase	e ECO cEO	Monthly Weekly	Drip trays or bunded areas are used for the storage of dirty drums	
<ul> <li>No unauthorised access into the hazardous substances storage areas must be permitted;</li> </ul>	Contractor	Ensure through the implementation of procedures that no unauthorised access is undertaken into the storage areas	During th Construction Phase	e ECO	Monthly	Proof of the implementati on of the relevant procedure must be provided by the contractor	
<ul> <li>No smoking must be allowed within the vicinity of the hazardous storage areas;</li> </ul>	Contractor	Inform all employees of the requirement and develop and place relevant	During th Construction Phase	e ECO cEO	Monthly Weekly	Photographic record of the signage placed must be provided	

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible person	Method of implementation signage in the relevant areas	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
<ul> <li>Adequate fire-fighting equipment must be made available at all hazardous storage areas;</li> </ul>	Contractor	Hazardous storage areas must be fitted with adequate fire- fighting equipment	During the Construction Phase	ECO	Monthly	Adequate fire-fighting equipment is available and has been serviced	
<ul> <li>Where refueling away from the dedicated refueling station is required, a mobile refueling unit must be used. Appropriate ground protection such as drip trays must be used;</li> </ul>	Contractor	Provide a mobile refuelling unit as well as suitable ground protection, where required	During the Construction Phase	ECO	Monthly, and as and when required	A mobile refuelling unit and suitable ground protection is available for use	
<ul> <li>An appropriately sized spill kit kept onsite relevant to the scale of the activity/s involving the use of hazardous substance must be available at all times;</li> </ul>	Contractor	Provide an appropriate spill kit for the project for the use of hazardous substances	During the Construction Phase	ECO	Monthly, and as and when required	Appropriate spill kits are available for use	
<ul> <li>The responsible operator must have the required training to make use of the spill kit in emergency situations;</li> </ul>	cEO and Contractor	Provide training on the use of spill kits to the relevant employees	Pre-construction	ECO	Once, prior to the commence ment of constructio n	Proof of training to be provided by the contractor	
<ul> <li>An appropriate number of spill kits must be available and must be located in all areas where activities are being undertaken;</li> </ul>	cEO and Contractor	Provide an appropriate number of spill kits in relevant areas	During the Construction Phase	ECO	Monthly	Proof of appropriate number of spill kits in	

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						appropriate areas to be provided by the contractor
<ul> <li>In the event of a spill, contaminated soil must be collected in containers and stored in a central location and disposed of according to the National Environmental Management: Waste Act 59 of 2008. Refer to Section 5.7 for procedures concerning storm and waste water management and 5.8 for solid and hazardous waste management.</li> </ul>	cEO and Contractor	Storage and disposal of contaminated soil must be in accordance with the National Environmental Management: Waste Act and sections 5.7 and 5.8 of this EMPr	During the Construction Phase	ECO	Monthly, and as and when required	Proof of storage and disposal in terms of the National Environment al Managemen t: Waste Act must be provided. Certificates of disposal at licensed waste disposal facilities must be provided

# 5.18 Workshop, equipment maintenance and storage

Impact management outcome: Soil, surface water and groundwater contamination is minimised.

Impact Management Actions	Implementatio	on			Monitoring			
	Responsible person	Method of implementation	Timeframe implementation	for	Responsible person	Frequency	Evidence of compliance	
<ul> <li>Where possible and practical all maintenance of vehicles and equipment must take place in the workshop area;</li> </ul>	Contractor	Demarcate specific areas for the maintenance of vehicles and equipment	During t Construction Phase	the	ECO	Monthly	A dedicated area for the maintenance of vehicles and machinery is used.	
<ul> <li>During servicing of vehicles or equipment, especially where emergency repairs are effected outside the workshop area, a suitable drip tray must be used to prevent spills onto the soil. The relevant local authority must be made aware of a fire as soon as it starts;</li> </ul>	Contractor	Ensure that a drip tray is available for any emergency repairs required	During t Construction Phase	the	ECO	Monthly	Contractor to provide evidence of drip tray use for emergency repairs	
<ul> <li>Leaking equipment must be repaired immediately or be removed from site to facilitate repair;</li> </ul>	Contractor	Ensure that where leaking equipment is identified it is repaired immediately or removed from site for repairs	During t Construction Phase	the	ECO	Monthly	Contractor to provide details of equipment repaired or removed from site	
<ul> <li>Workshop areas must be monitored for oil and fuel spills;</li> </ul>	CEO	Undertake regular inspections of the workshop areas for oil and fuel spills	During t Construction Phase	he	ECO	Monthly	Register of inspection	

Impact Management Actions	Implementatio	n		Monitoring	Monitoring			
	Responsible	Method of	Timeframe fo	Responsible	Frequency	Evidence of		
	person	implementation	implementation	person		compliance		
		and keep an						
		updated register						
		of inspection on						
		site						
- Appropriately sized spill kit kept onsite relevant to the	Contractor	Provide an	During the	ECO	Monthly,	Appropriate		
scale of the activity taking place must be available;		appropriate spill kit	Construction		and as and	spill kits are		
		for the project	Phase		when	available for		
					required	USE		
- The workshop area must have a bunded concrete slab	Contractor	Ensure that the	During the	ECO	Once,	Workshop		
that is sloped to facilitate runoff into a collection sump or		workshop area is	Construction		during the	area is		
suitable oil / water separator where maintenance work		sufficiently bunded	Phase		Constructio	bunded in		
on vehicles and equipment can be performed;		in accordance			n Phase	accordance		
		with the required			and as and	with the		
		specification			when	required		
					required	specification		
- Water drainage from the workshop must be contained	Contractor	Ensure that water	During the	ECO	Monthly	Workshop		
and managed in accordance Section 5.7: Storm and		drainage from	Construction			drainage is		
waste water management.		workshop area is	Phase			managed in		
		managed as per				accordance		
		the requirements				with the		
		of section 5.7				requirements		

# 5.19 Batching plants

Impact management outcome: Minimise spillages and contamination of soil, surface water and groundwater.

Impact Management Actions	Implementatio	on	Monitoring				
	Responsible person	Method of implementation	Timeframe implementatio	for	Responsible person	Frequency	Evidence of compliance
<ul> <li>Concrete mixing must be carried out on an impermeable surface;</li> </ul>	Contractor	Provide impermeable surface for the mixing of concrete	During Construction Phase	the	CEO	Weekly	No concrete mixing is undertaken on open ground
<ul> <li>Batching plants areas must be fitted with a containment facility for the collection of cement laden water.</li> </ul>	Contractor	Implement measures for the control and management of cement laden water	During construction phase	the	CEO	Weekly	No mismanage ment of laden water due to the temporary concrete batching plant
<ul> <li>Dirty water from the batching plant must be contained to prevent soil and groundwater contamination</li> </ul>	Contractor	Implement measures for the control and management of dirty water to prevent soil and groundwater contamination	During construction phase	the	CEO	Weekly	No mismanage ment of dirty water due to the temporary concrete batching plant and no/minimal soil and

Impact Management Actions	Implementatio	on		Monitoring	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance		
						groundwater contaminatio n		
<ul> <li>Bagged cement must be stored in an appropriate facility and at least 10 m away from any water courses, gullies and drains;</li> </ul>	Contractor	Demarcate and provide a storage area for bagged cement in-line with the listed requirements	During the Construction Phase	CEO	Weekly	Photographic proof of bagged cement stored within the demarcated area		
<ul> <li>A washout facility must be provided for washing of concrete associated equipment. Water used for washing must be restricted;</li> </ul>	Contractor	Provide a washout facility for the washing of associated equipment. Enforce limitations on water use for washing of equipment	During the Construction Phase	CEO	Weekly	No cement laden water is released into the environment. Only minimal water is used for washing		
<ul> <li>Hardened concrete from the washout facility or concrete mixer can either be reused or disposed of at an appropriate licensed disposal facility;</li> </ul>	Contractor	Make use of hardened concrete where possible or dispose of concrete in a suitable manner	During the Construction Phase	ECO	Monthly	Certificates of disposal of concrete at licensed waste disposal facility		
<ul> <li>Empty cement bags must be secured with adequate binding material if these will be temporarily stored on site;</li> </ul>	Contractor	Bind empty cement bags and temporarily store it	During the Construction Phase	ECO	Monthly	Proof of binding of empty cement bags		

Impact Management Actions	Implementatio	'n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		in an appropriate area on site				and storage in an appropriate are on site to be provided by the Contractor
<ul> <li>Sand and aggregates containing cement must be kept damp to prevent the generation of dust (Refer to Section 5.20: Dust emissions)</li> </ul>	Contractor	Ensure that sand and aggregates are kept damp or otherwise protected from dust generation	During the Construction Phase	ECO	Monthly	Proof of damping (or alternative dust suppression) of sand and aggregates must be provided by the Contractor
<ul> <li>Any excess sand, stone and cement must be removed or reused from site on completion of construction period and disposed at a registered disposal facility;</li> </ul>	Contractor	Ensure that all excess sand, stone and cement is removed or reused	At the completion of the Construction Phase	ECO	Once, with the completion of constructio n	Certificates for the disposal of sand, stone and cement at licensed waste disposal facilities or proof of reuse must be provided

Impact Management Actions	Implementation				Monitoring			
	Deserversilete			Time of the second of	£	De un e recite le	<b>F</b>	Evidence of
	Responsible	Method	d of	Timeframe	for	Responsible	Frequency	Evidence of
	person	implem	entation	implementation	۱	person		compliance
- Temporary fencing must be erected around batching	Contractor	Erect	Temporary	During	the	cEO	Weekly	Temporary
plants in accordance with Section 5.5: Fencing and gate		fencing	)	construction				fencing
installation.				phase				around
								batching
								plants

#### 5.20 Dust emissions

**Impact management outcome:** Dust prevention measures are applied to minimise the generation of dust.

Impact Management Actions	Implementatio	n	Monitoring	Monitoring			
	Responsible person	Method of implementation	Timeframe fo implementation	r Responsible person	Frequency	Evidence of compliance	
<ul> <li>Take all reasonable measures to minimise the generation of dust as a result of project development activities to the satisfaction of the ECO;</li> </ul>	Contractor	Apply appropriate dust suppressant	During the Construction Phase	Ə CEO	Weekly	Contractor to provide proof of use of appropriate dust suppressants	
<ul> <li>Removal of vegetation must be avoided until such time as soil stripping is required and similarly exposed surfaces must be re- vegetated or stabilised as soon as is practically possible;</li> </ul>	Contractor	Proper planning for vegetation removal must be undertaken as well as for the associated rehabilitation	During the Construction Phase and Rehabilitation		Weekly	Plan for implementati on must be provided by the Contractor	

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible person	Method of implementation	Timeframe fo implementation	r Responsible person	Frequency	Evidence of compliance	
<ul> <li>Excavation, handling and transport of erodible materials must be avoided under high wind conditions or when a visible dust plume is present;</li> </ul>	Contractor	Ensure that specific limitations are placed on the transport and handling of erodible materials during high wind conditions or when a visible dust plume is present	During the Construction Phase		Bi-weekly (every second week)	No complaints submitted in this regard	
<ul> <li>During high wind conditions, the ECO must evaluate the situation and make recommendations as to whether dust-damping measures are adequate, or whether working will cease altogether until the wind speed drops to an acceptable level;</li> </ul>	ECO	ECO to provide adequate recommendations	During the Construction Phase	<ul> <li>Not</li> <li>Applicable</li> </ul>			
<ul> <li>Where possible, soil stockpiles must be located in sheltered areas where they are not exposed to the erosive effects of the wind;</li> </ul>	Contractor	Place soil stockpiles in areas less affected by wind	During the Construction Phase	e cEO and ECO	Bi-weekly (every second week) Monthly	Soil stockpiles are not exposed to wind and have not been eroded	
<ul> <li>Where erosion of stockpiles becomes a problem, erosion control measures must be implemented at the discretion of the ECO;</li> </ul>	Contractor in consultation with the ECO	Contractor to implement erosion control measures as recommended and agreed with the ECO	During the Construction Phase	CEO	Weekly, until erosion is no longer a problem	Recommend ations made by the ECO have been implemented by the Contractor	

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
<ul> <li>Vehicle speeds must not exceed 40 km/h along dust roads or 20 km/h when traversing unconsolidated and non-vegetated areas;</li> </ul>	cEO / dEO / contractor	Inform all drivers of speed limits and place appropriate signage along the relevant roads	During the Construction Phase Operation Phase	ECO Operation and Maintenance team	Monthly	No complaints from community members are submitted	
<ul> <li>Straw stabilisation must be applied at a rate of one bale/10 m<sup>2</sup> and harrowed into the top 100 mm of top material, for all completed earthworks;</li> </ul>	Contractor	Ensure that straw stabilisation is undertaken as per the listed requirements	During the Construction Phase	ECO	Monthly	Photographic record of all straw stabilisation undertaken	
<ul> <li>For significant areas of excavation or exposed ground, dust suppression measures must be used to minimise the spread of dust.</li> </ul>	Contractor	Appropriate dust suppressant measures are implemented	During the Construction Phase	CEO	Weekly	Photographic record of measures being implemented and the results thereof	

# 5.21 Blasting

Impact management outcome: Impact to the environment is minimised through a safe blasting practice.

Impact Management Actions	Implementatio	n		Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
- Any blasting activity must be conducted by a suitably	cEO / dEO /	Ensure the	Pre-Construction	ECO/EO	Once off,	ECO/EO to	
licensed blasting contractor; and	contractor	contractor is	Phase		before	check all	
		suitably licensed			blasting	valid	
		with all necessary			activities	credentials	
		credentials and			commence	and	
		certifications				certifications	
						on hand.	
- Notification of surrounding landowners, emergency	cEO / dEO /	Ensure all	Pre-Construction	ECO/EO	Once off,	ECO/EO to	
services site personnel of blasting activity 24 hours prior	contractor	responsible	Phase		before	confirm all	
to such activity taking place on Site.		personnel and			blasting	necessary	
		landowners have			activities	personnel	
		been notified of			commence	and	
		blasting activities				landowners	
		24 hours in				have been	
		advance and				notified.	
		keep records of				Notification	
		notifications.				records to be	
						provided.	

Impact Management outcome: Prevent unnecessary noise to the environment by ensuring that noise from development activity is mitigated.

Impact Management Actions	Implementatio	on		Monitoring	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance		
<ul> <li>The Contractor must keep noise level within acceptable limits, Restrict the use of sound amplification equipment for communication and emergency only;</li> </ul>	Contractor	Ensure that noise limits do not exceed acceptable limits and avoid the use of amplification communication	During the Construction Phase	ECO	Monthly, and as and when required	No complaints registered in this regard. No amplification equipment is used.		
<ul> <li>All vehicles and machinery must be fitted with appropriate silencing technology and must be properly maintained;</li> </ul>	Contractor	Provide and implement silencing technology	During the Construction Phase	ECO	Monthly, and as and when required	No complaints registered in this regard. Silencing technology is utilised.		
<ul> <li>Any complaints received by the Contractor regarding noise must be recorded and communicated. Where possible or applicable, provide transport to and from the site on a daily basis for construction workers;</li> </ul>	CEO	Update complaints register. Provide daily transport to and from site for employees	During the Construction Phase	ECO	Monthly, and as and when required	Complaints register provided by the cEO and proof of transportatio n services provided		

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Develop a Code of Conduct for the construction phase in terms of behaviour of construction staff. Operating hours as determined by the environmental authorisation are adhered to during the development phase. Where not defined, it must be ensured that development activities must still meet the impact management outcome related to noise management.</li> </ul>	cEO and Contractor in consultation with the ECO	Compile a Code of Conduct for staff. Appropriate operating hours must be identified for the project.		ECO	Once, prior to the commence ment of constructio n	No complaints registered in

### 5.23 Fire prevention

Impact management outcome: Prevention of uncontrollable fires.

Impact Management Actions	Implementation			Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
<ul> <li>Designate smoking areas where the fire hazard could be regarded as insignificant;</li> </ul>	cEO / Contractor	Identify and demarcate through signage designated smoking areas	Pre-construction & Construction	ECO	Monthly	Photographic record of designated smoking area	
<ul> <li>Firefighting equipment must be available on all vehicles located on site;</li> </ul>	cEO / dEO in consultation with the Contractor	Provide all vehicles with firefighting equipment	Construction	ECO	Monthly	All vehicles are fitted with firefighting equipment and the details	

Impact Management Actions	Implementation			Monitoring			
					1		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
						thereof are	
						provided by	
						the cEO	
- The local Fire Protection Agency (FPA) must be informed	cEO in	Undertake formal	Pre-construction	ECO	Once,	Proof of	
of construction activities;	consultation	consultation to			during the	consultation	
	with the ECO	inform the local			commence	with the FPA	
		FPA of the			ment of the		
		associated			Constructio		
		construction			n Phase		
		activities					
- Contact numbers for the FPA and emergency services	dEO / cEO /	Develop	Pre-construction &	ECO	Prior to the	Environment	
must be communicated in environmental awareness	Contractor in	environmental	Construction		commence	al awareness	
training and displayed at a central location on site;	consultation	awareness training			ment of the	training	
	with the ECO	material which			environmen	material	
		covers the contact			tal	requirements	
		numbers for the			awareness	checklist and	
		FPA and			training and	photographi	
		emergency			once during	c record of	
		services.			the	contact	
		361 11663.			constructio	numbers on	
		Place the contact			n phase	display	
		numbers for the					
		FPA and					
		emergency					
		services at a visible					
		and central					
		location					
<ul> <li>Two way swop of contact details between ECO and FPA.</li> </ul>	ECO	Consultation	Pre-construction	Not			
		between the ECO		Applicable			
		and FPA in order to		1.1.1.1.1.1.1.1.0			

Impact Management Actions	Implementation	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		exchange contact				
		details				

# 5.24 Stockpiling and stockpile areas

Impact management outcome: Reduce erosion and sedimentation as a result of stockpiling.

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>All material that is excavated during the project development phase (either during piling (if required) or earthworks) must be stored appropriately on site in order to minimise impacts to watercourses, watercourses and water bodies;</li> </ul>	Contractor	Identify and demarcate an appropriate location for the storage of excavated materials	Pre-construction & Construction	ECO	Monthly	Excavated material is not stored within sensitive environment al areas
<ul> <li>All stockpiled material must be maintained and kept clear of weeds and alien vegetation growth by undertaking regular weeding and control methods;</li> </ul>	Contractor	Implement appropriate and sufficient maintenance on stockpiled material regularly	During the Construction Phase	cEO ECO	Bi-weekly (every second month) Monthly	Stockpiled material is maintained sufficiently and is clear of weeds and

Impact Management Actions	Implementatio	on			Monitoring		
	Responsible person	Method of implementation	Timeframe implementatior	for n	Responsible person	Frequency	Evidence of compliance
							alien vegetation
- Topsoil stockpiles must not exceed 2 m in height;	Contractor	Enforce limitations for the height of topsoil stockpiles	During Construction Phase	the	ceo eco	Bi-weekly (every second month) Monthly	Topsoil stockpiles do not exceed 2m in height
<ul> <li>During periods of strong winds and heavy rain, the stockpiles must be covered with appropriate material (e.g. cloth, tarpaulin etc.);</li> </ul>	Contractor	Appropriate material must be provided in order to cover stockpiles when required	During Construction Phase	the	ECO	Monthly	Contractor to provide proof of availability of appropriate material to cover stockpiles when required
<ul> <li>Where possible, sandbags (or similar) must be placed at the bases of the stockpiled material in order to prevent erosion of the material.</li> </ul>	Contractor	Sandbags must be provided in order to prevent erosion of stockpiled materials	During Construction Phase	the	ECO	Monthly	Contractor to provide proof of availability of sandbags to prevent erosion of stockpiled materials

#### 5.25 Civil works

Impact management outcome: Impact to the environment minimised during civil works to create the substation terrace.

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Where terracing is required, topsoil must be collected and retained for the purpose of re-use later to rehabilitate disturbed areas not covered by yard stone;</li> </ul>	Contractor	Collection and safe storage of topsoil for later use in rehabilitation phase	During the Construction Phase	ECO	Monthly	Visual inspection of topsoil stockpiles for later use
<ul> <li>Areas to be rehabilitated include terrace embankments and areas outside the high voltage yards;</li> </ul>	Contractor	Regard areas that do not house infrastructure as requiring rehabilitation and apply rehabilitation measures to these regions	During the Construction Phase, where the area is no longer going to be utilised	ECO	Monthly	Visual inspection of rehabilitation implementati on to ensure these areas are being rehabilitated
<ul> <li>Where required, all sloped areas must be stabilised to ensure proper rehabilitation is effected and erosion is controlled;</li> </ul>	Contractor	If required stabilise soil using recognised methods to ensure proper rehabilitation and erosion control	Duration of the construction phase	ECO	Monthly	Visual inspection of stabilised soil regions and descriptions of staff of stabilisation method used

Impact Management Actions	Implementatio	on		Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance	
<ul> <li>These areas can be stabilised using design structures or vegetation as specified in the design to prevent erosion of embankments. The contract design specifications must be adhered to and implemented strictly;</li> </ul>	Contractor	If required stabilise soil using recognised methods to ensure proper rehabilitation and erosion control	Duration of the construction phase	ECO	Monthly	Visual inspection of stabilised soil regions and descriptions of staff of stabilisation method used	
<ul> <li>Rehabilitation of the disturbed areas must be managed in accordance with Section 5.35: Landscaping and rehabilitation;</li> </ul>	Contractor	Review and ensure that all rehabilitation measures are implemented in accordance with the requirements of Section 5.35	Duration of the construction phase	ECO	Monthly	Visual inspection of rehabilitation conducted and the degree of conformanc e with the requirements set out in Section 35.5 of this report	
<ul> <li>All excess spoil generated during terracing activities must be disposed of in an appropriate manner and at a recognised landfill site; and</li> </ul>	Contractor	Dispose of all excess spoil using appropriate means and at recognised landfill sites. Keep written registers of the disposal conducted	Duration of the construction phase	ECO	Monthly	Evidence of disposal slips as applicable kept in the site environment al file	

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- Spoil can however be used for landscaping purposes	Contractor	Where spoil is	Duration of the	ECO	Monthly	Spoil material
and must be covered with a layer of 150 mm topsoil for		utilised for	construction			used in
rehabilitation purposes.		landscaping	phase			landscaping
		purposes				is suitably
		implement a				covered with
		150mm topsoil				a later of
		layer on top				topsoil at
		following shaping				least 150mm
		and compaction				deep
		to promote				
		rehabilitation				

#### 5.26 Excavation of foundation, cable trenching and drainage systems

Impact management outcome: No environmental degradation occurs as a result of excavation of foundation, cable trenching and drainage systems.

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>All excess spoil generated during foundation excavation must be disposed of in an appropriate manner and at a licensed landfill site, if not used for backfilling purposes;</li> </ul>	Contractor	Use a licensed waste disposal facility for the disposal of excess spoil	During the Construction Phase	ECO	Monthly	Certificates obtained for the disposal of excess spoil at a licensed waste

Impact Management Actions	Implementatio	on		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
						disposal facility
<ul> <li>Spoil can however be used for landscaping purposes and must be covered with a layer of 150 mm topsoil for rehabilitation purposes;</li> </ul>	Contractor	Spoil used for landscaping must be applied as per the listed requirements	Construction and Rehabilitation	ECO	Monthly	Photographic record of spoil used for landscaping purposes as well as feedback from the contractor
<ul> <li>Management of equipment for excavation purposes must be undertaken in accordance with Section 5.18: Workshop, equipment maintenance and storage; and</li> </ul>	Contractor	Undertake the management of equipment for excavation as per the requirements of section 5.18	During the Construction Phase	ECO	Monthly	Managemen t of equipment is undertaken in line with the requirements of section 5.18
<ul> <li>Hazardous substances spills from equipment must be managed in accordance with Section 5.17: Hazardous substances.</li> </ul>	Contractor	Undertake the management of hazardous substances spills from equipment as per the requirements of section 5.17	During the Construction Phase	ECO	Monthly	Managemen t of hazardous substances spills from equipment is undertaken in line with the requirements

Impact Management Actions	Implementation	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person	in equal to y	compliance
						of section
						5.17

# 5.27 Installation of foundations, cable trenching and drainage systems

Impact management outcome: No environmental degradation occurs during the installation of foundation, cable trenching and drainage system.

Impact Management Actions	Implementatio	'n				Monitoring		
	Responsible person	Method implemen	of tation	Timeframe implementati	for on	Responsible person	Frequency	Evidence of compliance
<ul> <li>Batching of cement to be undertaken in accordance with Section 5.19: Batching plants; and</li> </ul>	Contractor	Ensure batching cement	correct of	During construction phase	the	CEO	Weekly	Measures in place to ensure the batching of cement is done in accordance with Section 5.19: Batching plants
<ul> <li>Residual solid waste must be disposed of in accordance with Section 5.8: Solid waste and hazardous management.</li> </ul>	Contractor	Undertake disposal of solid wast the requ of section	f residual e as per virements	During Construction Phase	the	ECO	Monthly	The disposal of residual solid waste is undertaken in line with section 5.8.

Impact Management Actions	Implementation				Monitoring			
	Responsible person	Method of implementation	Timeframe implementation	for n	Responsible person	Frequency	Evidence of compliance	

### 5.28 Installation of equipment (circuit breakers, current Transformers, Isolators, Insulators, surge arresters, voltage transformers, earth switches)

Impact management outcome: No environmental degradation occurs as a result of installation of equipment.

Impact Management Actions	Implementatio	n		Monitoring				
<ul> <li>Management of dust must be conducted in accordance with Section 5. 20: Dust emissions;</li> </ul>	Responsible person Contractor	MethodofimplementationReviewandimplementdustmanagementactionsactordancewiththe requirement ofSection 5.20 of thisreport	Timeframe for implementation During the Construction Phase	person	Frequency Monthly	Evidence of compliance Dust managemen t actions observed to be in accordance with the requirement		
						of Section 5.20 of this report		

Impact Management Actions	Implementatio	'n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Management of equipment used for installation must be conducted in accordance with Section 5.18: Workshop, equipment maintenance and storage;</li> </ul>	Contractor	Review and implement equipment management actions in accordance with the requirement of Section 5.18 of this report	During the Construction Phase		Monthly	Equipment managemen t actions observed to be in accordance with the requirement of Section 18 of this report
<ul> <li>Management hazardous substances and any associated spills must be conducted in accordance with Section 5.17: Hazardous substances; and</li> </ul>	Contractor	Review and implement hazardous substances and any associated spills in accordance with the requirement of Section 5.17 of this report	During the Construction Phase	ECO	Monthly	Hazardous substances and any associated spills managemen t actions observed to be in accordance with the requirement of Section 5.17 of this report
<ul> <li>Residual solid waste must be recycled or disposed of in accordance with Section 5.8: Solid waste and hazardous management.</li> </ul>	Contractor	Review and dispose/recycle residual solid waste in accordance with	During the Construction Phase	ECO	Monthly	Dispose/recy cle residual solid waste observed to be in

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		the requirement of				accordance
		Section 5.8 of this				with the
		report				requirement
						of Section 5.8
						of this report

#### 5.29 Steelwork Assembly and Erection

Impact management outcome: No environmental degradation occurs as a result of steelwork assembly and erection.

Impact Management Actions	Implementatio	n		Monitoring				
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance		
<ul> <li>During assembly, care must be taken to ensure that no wasted/unused materials are left on site e.g. bolts and nuts</li> </ul>	Contractor	Conduct an inspection of the site once assembly is complete to remove all stray bolts or unused materials that may be left on site	Duration of the construction phase	ECO	Monthly	Evidence of leftover waste/unuse d materials on site following closure of assembly		
<ul> <li>Emergency repairs due to breakages of equipment must be managed in accordance with Section 5.18: Workshop, equipment maintenance and storage and Section 5.16: Emergency procedures.</li> </ul>	Contractor	Reviewandconductallemergencyrepairsinaccordancewith	Duration of the construction phase	ECO	Monthly	Evidence of emergency repairs carried out		

Impact Management Actions	Implementatio	n	Monitoring			
						_
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		Sections 5.18 and				having been
		5.16 of this report				conducted in
						accordance
						with Sections
						5.18 and 5.16
						of this report

# 5.30 Cabling and Stringing

Impact management outcome: No environmental degradation occurs as a result of stringing.

Impact Management Actions	Implementatio	n	Monitoring	Monitoring			
			1				
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
- Residual solid waste (off cuts etc.) shall be recycled or	Contractor	Undertake	During the	ECO	Monthly	Undertake	
disposed of in accordance with Section 6.8: Solid waste		recycling or	Construction			recycling or	
and hazardous Management;		disposal of solid	Phase			disposal of	
		waste as per the				solid waste as	
		requirements of				per the	
		section 6.8				requirements	
						of section 6.8	

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Management of equipment used for installation shall be conducted in accordance with Section 5.18: Workshop, equipment maintenance and storage;</li> </ul>	Contractor	Undertake the management of equipment as per the requirements of section 5.18	During the Construction Phase	ECO	Monthly	Managemen t of equipment is undertaken in line with the requirements of section 5.18
<ul> <li>Management hazardous substances and any associated spills shall be conducted in accordance with Section 5.17: Hazardous substances.</li> </ul>	Contractor	Undertake the management of hazardous substances as per the requirements of section 5.17	During the Construction Phase	ECO	Monthly	Managemen t of hazardous substances is undertaken in line with the requirements of section 5.17

### 5.31 Testing and Commissioning (all equipment testing, earthing system, system integration)

Impact management outcome: No environmental degradation occurs as a result of Testing and Commissioning.

Impact Management Actions	Implementation				Monitoring			
	Responsible	Method of	Timeframe	for	Responsible	Frequency	Evidence of	
	person	implementation	implementatio	n	person		compliance	
<ul> <li>Residual solid waste must be recycled or disposed of in accordance with Section 5.8: Solid waste and hazardous management.</li> </ul>	Contractor	Undertake recycling or disposal of solid waste as per the requirements of section 5.8	During Construction Phase	the	ECO	Monthly	Undertake recycling or disposal of solid waste as per the requirements	
							of section 5.8	

#### 5.32 Socio-economic

Impact management outcome: enhanced socio-economic development.

Impact Management Actions	Implementation				Monitoring					
	Responsible	Method	of	Timeframe	for	Responsible	Freque	ncy	Evidence	of
	person	implementatio	on	implementatio	n	person			complianc	е
- Develop and implement communication strategies to	dEO / cEO	Identify	and	Pre-construction	n &	ECO	Once,	prior	Communic	:ati
facilitate public participation;		implement		Construction			to	the	on	is
		appropriate					comme	ence	undertaker	n
		strategies	for				ment	of	as per t	the
		communicatio	on				constru	ctio	identified	
		with	the				n	and	strategies	

Impact Management Actions	Implementatio	on		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
		communities through consideration of the community needs			monthly during the constructio n	and no complaints are submitted regarding communicati on
<ul> <li>Develop and implement a collaborative and constructive approach to conflict resolution as part of the external stakeholder engagement process;</li> </ul>	Contractor	Development and implement a Grievance Mechanism which considers the community needs and provides procedures for conflict resolution	Pre-construction & Construction	ECO	Once, prior to the commence ment of constructio n and monthly during the constructio n phase	Conflict resolution is undertaken in line with the requirements of the Grievance Mechanism. No complaints on conflict resolution is submitted by the community
<ul> <li>Sustain continuous communication and liaison with neighboring owners and residents</li> </ul>	Contractor	Development and implement and Grievance Mechanism provides procedures for communication / liaison with neighbouring	Pre-construction & Construction	ECO	Once, prior to the commence ment of constructio n and monthly during the constructio n phase	Communicati on / liaison with neighbouring landowners and residents are undertaken in line with the requirements

Impact Management Actions	Implementatio	on		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
	PEISOIT	landowners and residents		person		of the Grievance Mechanism. No complaints on communicati on with neighbouring landowners and residents are submitted
<ul> <li>Create work and training opportunities for local stakeholders; and</li> </ul>	Contractor	Develop and implement a "locals first" policy for the provision of employment opportunities	Pre-construction & Construction	ECO	Once, prior to the commence ment of constructio n and monthly during the constructio n phase	The "locals first" policy is considered in terms of the employment and training opportunities
<ul> <li>Where feasible, no workers, with the exception of security personnel, must be permitted to stay over-night on the site. This would reduce the risk to local farmers</li> </ul>	Contractor	Ensure no workers are permitted to stay over night on the site	Construction	ECO	Throughout constructio n	No workers remaining on site over night

# 5.33 Temporary closure of site

Impact management outcome: Minimise the risk of environmental impact during periods of site closure greater than five days.

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	or Responsible person	Frequency	Evidence of compliance
<ul> <li>Bunds must be emptied (where applicable) and need to be undertaken in accordance with the impact management actions included in sections 5.17: Hazardous substances and 5.18: Workshop, equipment maintenance and storage;</li> </ul>	Contractor	Regular emptying of the bunds must be undertaken. This must be undertaken as per the requirements listed in sections 5.17 and 5.18	During th Construction Phase	e ECO	Prior to site closure for more than 05 days	Bunds are emptied as per the requirements listed under sections 5.17 and 5.18
<ul> <li>Hazardous storage areas must be well ventilated;</li> </ul>	Contractor	Install appropriate ventilation in all hazardous storage areas	During th construction phase	e ECO	Prior to site closure for more than 05 days	Effective ventilation is installed in hazardous storage areas
<ul> <li>Fire extinguishers must be serviced and accessible. Service records to be filed and audited at last service;</li> </ul>	Contractor / cEO	Ensure fire extinguishers are serviced, as required and are easily accessible with appropriate signage indicating location. Ensure service records and kept up to date and filed	During th Construction Phase	e ECO	Prior to site closure for more than 05 days	Signage placed indicating location of fire extinguishers and service records

Impact Management Actions	Implementation	n		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Emergency and contact details displayed must be displayed;</li> </ul>	Contractor / cEO	Place emergency and contact details which are readily available and easily accessible	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Photographic proof of contact details on display
<ul> <li>Security personnel must be briefed and have the facilities to contact or be contacted by relevant management and emergency personnel;</li> </ul>	Contractor in consultation with the ECO	Hold a workshop with all security personnel to provide a brief of the project and security requirements. Provide facilities in order to contact management and emergency personnel	Pre-construction & construction	ECO	Prior to site closure for more than 05 days	Proof of the workshop held must be kept on file by the contractor.
<ul> <li>Night hazards such as reflectors, lighting, traffic signage etc. must have been checked;</li> </ul>	Contractor	Regular checks of night hazards must be undertaken	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Proof of checks of night hazards must be provided by the contractor
<ul> <li>Fire hazards identified and the local authority must have been notified of any potential threats e.g. large brush stockpiles, fuels etc.;</li> </ul>	cEO / Contractor in consultation with the ECO	Identify any potential fire hazards and notify the relevant local authority	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Proof of notification of the fire hazards to the local authority

Impact Management Actions	Implementatio	on		Monitoring	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance		
						must be provided by the Contractor		
<ul> <li>Structures vulnerable to high winds must be secured;</li> </ul>	Contractor	Ensure structures vulnerable to wind are secure prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Structures vulnerable to wind are secured prior to site closure		
<ul> <li>Wind and dust mitigation must be implemented;</li> </ul>	Contractor	Implement wind and dust mitigation prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Wind and dust mitigation is implemented prior to site closure		
<ul> <li>Cement and materials stores must have been secured;</li> </ul>	Contractor	Ensure cement and material stores are secured prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Cement and material stores are secured prior to site closure		
<ul> <li>Toilets must have been emptied and secured;</li> </ul>	Contractor	Ensure toilets are emptied and secured prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Toilets are emptied and secured prior to site closure		
<ul> <li>Refuse bins must have been emptied and secured;</li> </ul>	Contractor	Ensure refuse bins are emptied and secured prior to site closure	During the Construction Phase	ECO	Prior to site closure for more than 05 days	Refuse bins are emptied and secured prior to site closure		

Impact Management Actions	Implementatio	n	Monitoring			
						-
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- Drip trays must have been emptied and secured.	Contractor	Ensure drip trays	During the	ECO	Prior to site	Drip trays are
		are emptied and	Construction		closure for	emptied and
		secured prior to	Phase		more than	secured prior
		site closure			05 days	to site closure

#### 5.34 Dismantling of old equipment

Impact management outcome: Impact to the environment to be minimised during the dismantling, storage and disposal of old equipment commissioning.

Impact Management Actions	Implementatio	n		Monitoring	ing		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
- All old equipment removed during the project must be	Contractor	Ensure old	During the	ECO	Monthly	Drip trays are	
stored in such a way as to prevent pollution of the		equipment is	Construction			emptied and	
environment		secured and	Phase			secured prior	
		where required,				to site closure	
		stored in					
		contained areas					
		where no spillage					
		or pollution may					
		result					
- Oil containing equipment must be stored to prevent	Contractor	Ensure old	During the	ECO	Monthly	Drip trays are	
leaking or be stored on drip trays;		equipment is	Construction			emptied and	
		secured and	Phase				

Impact Management Actions	Implementatio	n		Monitoring				
	Responsible person	Method of implementation	Timeframe f implementation	or Responsible person	Frequency	Evidence of compliance		
		where required, stored in contained areas where no spillage or pollution may result				secured prior to site closure		
<ul> <li>All scrap steel must be stacked neatly and any disused and broken insulators must be stored in containers;</li> </ul>	Contractor	Store defunct insulators in containers and scrap steel in one single place, neatly secured	During t Construction Phase	ne ECO	Monthly	Where needed, insulators observed to be stored in containers and scrap stored neatly as determined by the ECO		
<ul> <li>Once material has been scrapped and the contract has been placed for removal, the disposal Contractor must ensure that any equipment containing pollution causing substances is dismantled and transported in such a way as to prevent spillage and pollution of the environment;</li> </ul>	Contractor , cEO	Ensure dismantling and packaging of scrapped material is transported in such a way as to prevent spillage and pollution of the environment;	During t Construction Phase	ne ECO	Monthly	Where needed, insulators observed to be stored in containers and scrap stored neatly as determined by the ECO		
<ul> <li>The Contractor must also be equipped to contain and clean up any pollution causing spills; and</li> </ul>	cEO and Contractor	Provide training on the use of spill kits	During tl Construction Phase	ne ECO	Monthly	Proof of training to be provided by		

Impact Management Actions	Implementation	n			Monitoring	Aonitoring			
	Responsible	Method of	Timeframe	for	Responsible	Frequency	Evidence of		
	person	implementation	implementatior	า	person		compliance		
		to the relevant					the		
		employees					contractor		
- Disposal of unusable material must be at a licensed	cEO and	Ensure a registered	During	the	ECO	Monthly	Visual		
waste disposal site.	Contractor	waste disposal site	Construction				inspection of		
		is utilised and keep	Phase				disposal		
		disposal slips and					record		
		record in the site					documentati		
		environmental file					on and		
							registration of		
							the waste		
							disposal site		
							utilised.		

#### 5.35 Landscaping and rehabilitation

Impact management outcome: Areas disturbed during the development phase are returned to a state that approximates the original condition.

Impact Management Actions	Implementation				Monitoring	onitoring			
	Responsible person	Method implementati	of on	Timeframe implementation	for n	Responsible person	Frequency	Evidence compliance	
<ul> <li>All areas disturbed by construction activities must be subject to landscaping and rehabilitation; All spoil and waste must be disposed of to a registered waste site;</li> </ul>	Contractor	Develop implement rehabilitation for	and a plan the	Pre-constructio Rehabilitation	n &	CEO	Weekly	Rehabilitati of t disturbed areas undertaker	he is

Impact Management Actions	Implementation	n		Monitoring				
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance		
		rehabilitation of all disturbed areas. Dispose of all spoil and waste at a licensed waste disposal facility				as per the rehabilitation plan. All certificates of waste disposal at licensed facilities are available.		
<ul> <li>All slopes must be assessed for contouring, and to contour only when the need is identified in accordance with the Conservation of Agricultural Resources Act, No 43 of 1983</li> </ul>	Contractor in consultation with the ECO	Assess all slopes and determine whether contouring is required	Rehabilitation	cEO	Weekly	All slopes are assessed and contoured as required		
<ul> <li>All slopes must be assessed for terracing, and to terrace only when the need is identified in accordance with the Conservation of Agricultural Resources Act, No 43 of 1983;</li> </ul>	Contractor in consultation with the ECO	Assess all slopes and determine whether terracing is required	Rehabilitation	CEO	Weekly	All slopes are assessed and terraced as required		
<ul> <li>Berms that have been created must have a slope of 1:4 and be replanted with indigenous species and grasses that approximates the original condition;</li> </ul>	Contractor	Ensure all berms have a slope of 1:4 and is replanted with indigenous species and grasses	Rehabilitation	CEO	Weekly	All berms have a slope of 1:4 and is replanted with indigenous species and grasses		
<ul> <li>Where new access roads have crossed cultivated farmlands, that lands must be rehabilitated by ripping which must be agreed to by the holder of the EA and the landowners;</li> </ul>	Not applicable		·	·				
<ul> <li>Rehabilitation of access roads outside of farmland;</li> </ul>	Not applicable	}						

Impact Management Actions	Implementatio	on		Monitoring		
	Responsible person	Method of implementation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Indigenous species must be used for with species and/grasses to where it compliments or approximates the original condition;</li> </ul>	Contractor	Make use of indigenous species for rehabilitation	Rehabilitation	CEO	Weekly	Indigenous species are used for rehabilitation
<ul> <li>Stockpiled topsoil must be used for rehabilitation (refer to Section 5.24: Stockpiling and stockpiled areas);</li> </ul>	Contractor	Ensure stockpiled topsoil is used as per the requirements listed under section 5.24	Rehabilitation	CEO	Weekly	Stockpiled topsoil is used as per the requirements listed under section 5.24
<ul> <li>Stockpiled topsoil must be evenly spread so as to facilitate seeding and minimise loss of soil due to erosion;</li> </ul>	Contractor	Ensure that topsoil is spread evenly	Rehabilitation	CEO	Weekly	Topsoil is spread evenly
<ul> <li>Before placing topsoil, all visible weeds from the placement area and from the topsoil must be removed;</li> </ul>	Contractor	Remove all visible weeds from placement area and topsoil before spreading the topsoil	Rehabilitation	CEO	Weekly	No weeds are visible in the placement area or the topsoil
<ul> <li>Subsoil must be ripped before topsoil is placed;</li> </ul>	Contractor	Undertake the ripping of subsoil prior to the spreading of topsoil	Rehabilitation	cEO	Weekly	Subsoil is ripped before topsoil is placed
<ul> <li>The rehabilitation must be timed so that rehabilitation can take place at the optimal time for vegetation establishment;</li> </ul>	Contractor	Plan the timeframe for rehabilitation in order to undertake vegetation planting during the optimal time for	Rehabilitation	ECO	At the start of rehabilitatio n to confirm correct timeframe	Rehabilitation is undertaken during the optimal time

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible person	Method of implementation vegetation	Timeframe for implementation	Responsible person	Frequency	Evidence of compliance
<ul> <li>Where impacted through construction related activity, all sloped areas must be stabilised to ensure proper rehabilitation is effected and erosion is controlled;</li> </ul>	Contractor	establishment All disturbed slope areas must be stabilised	Rehabilitation	CEO	Weekly	Disturbed slopes are stabilised sufficiently
<ul> <li>Sloped areas stabilised using design structures or vegetation as specified in the design to prevent erosion of embankments. The contract design specifications must be adhered to and implemented strictly;</li> </ul>	Contractor	Stabilise slopes as per the design specifications	Pre-construction & Rehabilitation	CEO	Weekly	Slopes are stabilised as per the design specifications
<ul> <li>Spoil can be used for backfilling or landscaping as long as it is covered by a minimum of 150 mm of topsoil.</li> </ul>	Contractor	Spoil used for landscaping must be applied as per the listed requirements	Rehabilitation	CEO	Weekly	Photographic record of spoil used for landscaping purposes as well as feedback from the contractor
<ul> <li>Where required, re-vegetation including hydro-seeding can be enhanced using a vegetation seed mixture as described below. A mixture of seed can be used provided the mixture is carefully selected to ensure the following: <ul> <li>a) Annual and perennial plants are chosen;</li> <li>b) Pioneer species are included;</li> <li>c) Species chosen must be indigenous to the area with the seeds used coming from the area;</li> <li>d) Root systems must have a binding effect on the soil;</li> </ul></li></ul>	Contractor in consultation with a suitably qualified specialist	Make use of a suitable vegetation seed mixture should enhancement be required	Rehabilitation	ECO	As and when required	Use of a suitable vegetation seed mixture if required

Impact Management Actions	Implementatio	n	Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
e) The final product must not cause an ecological						
imbalance in the area						

#### 6 ACCESS TO THE GENERIC EMPr

Once completed and signed, to allow the public access to the generic EMPr, the holder of the EA must make the EMPr available to the public in accordance with the requirements of Regulation 26(h) of the EIA Regulations.

#### PART B: SECTION 2

#### 7 SITE SPECIFIC INFORMATION AND DECLARATION

#### 7.1 Sub-section 1: contact details and description of the project

#### 7.1.1 Details of the applicant:

Name of applicant: AGV Projects (Pty) Ltd Contact person: Dirk Muller Tel No: Not disclosed in accordance with POPIA<sup>1</sup>. Postal Address: Physical Address: 512 Riverside Lofts, 112 Tyger Falls Blvd, Bellville, Cape Town

#### 7.1.2 Details and expertise of the EAP:

Name of EAP: Jo-Anne Thomas Tel No: 011-656-3237 Fax No: 086-684-0547 E-mail address: joanne@savannahsa.com Expertise of the EAP (Curriculum Vitae included): Refer to Appendix 2 of this EMPr for a CV of the EAP

# 7.1.3 Project name: Red Sands PV2, Northern Cape Province

# 7.1.4 Description of the project:

AGV Projects (Pty) Ltd is proposing the development of a solar PV facility and associated infrastructure on a site located approximately 26km northeast of Groblershoop, within the Tsantsabane Local Municipality and the ZF Mgcawu District Municipality in the Northern Cape Province. The project is to be known as Red Sands PV2 and will have a contracted capacity of up to 75MW.

The development area for the PV facility is located on Portion 2 of the Farm Tities Poort 386. The project site is accessible via an existing gravel farm road from an existing main gravel road off the N8 which is located southeast of the project site.

The Red Sands PV1 project is proposed to accommodate the following infrastructure, which will enable the PV facility to supply a contracted capacity of up to  $75MW_{AC}$ :

- » Solar PV array comprising PV modules and mounting structures
- » Inverters and transformers
- » Low voltage cabling between the PV modules to the inverters
- » Fence around the project development area
- » Camera surveillance
- » Internet connection

<sup>&</sup>lt;sup>1</sup> Contact details for the applicant will not be disclosed in any public documentation, due to the Protection of Personal Information Act, (No. 2 of 2013) as gazetted on 1 July 2021. This information is available on request from the EAP or the relevant authorities, with a motivation for the need to gain access to such information.

- » 33kV cabling between the project components and the facility substation
- » 33/132kV onsite facility substation<sup>1</sup>.
- » Battery Energy Storage System (BESS).
- » Site offices and maintenance buildings, including workshop areas for maintenance and storage.
- » Laydown areas.
- » Access roads (up to 6m) and internal distribution roads (up to 4m).

# 7.2 Sub-section 2: Development footprint site map

This sub-section must include a map of the site sensitivity overlaid with the preliminary infrastructure layout. The sensitivity map must be prepared from the national web based environmental screening tool, when available for compulsory use at: <a href="https://screening.environment.gov.za/screeningtool">https://screening.environment.gov.za/screeningtool</a>. The sensitivity map shall identify the nature of each sensitive feature e.g. threatened plant species, archaeological site, etc. Sensitivity maps shall identify features both within the planned working area and any known sensitive features within 50 m from the development footprint.

It must be noted that the maps provided below relate to the larger wind farm which the substations are associated with.

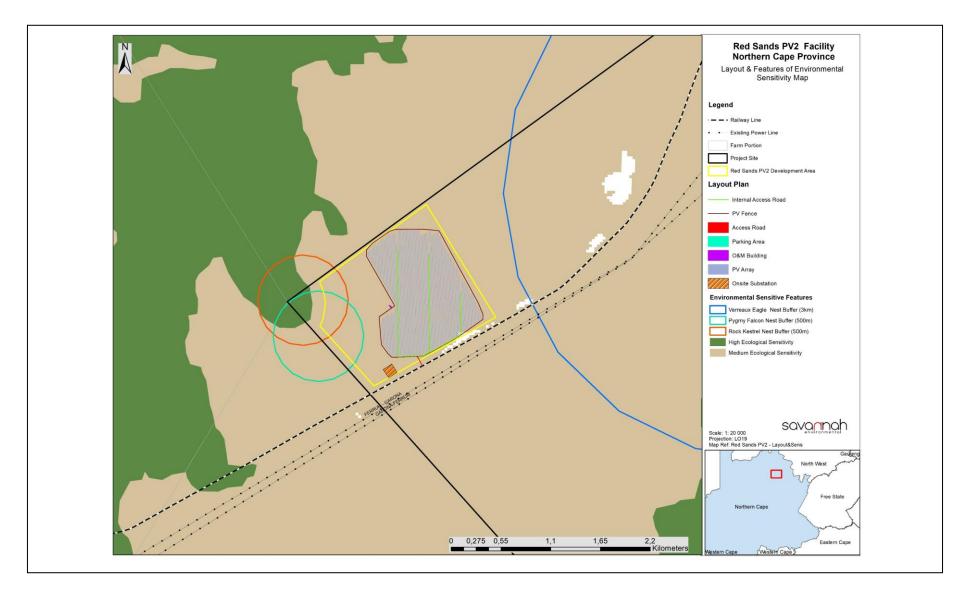


Figure 1: Environmental sensitivity map of Red Sands PV2

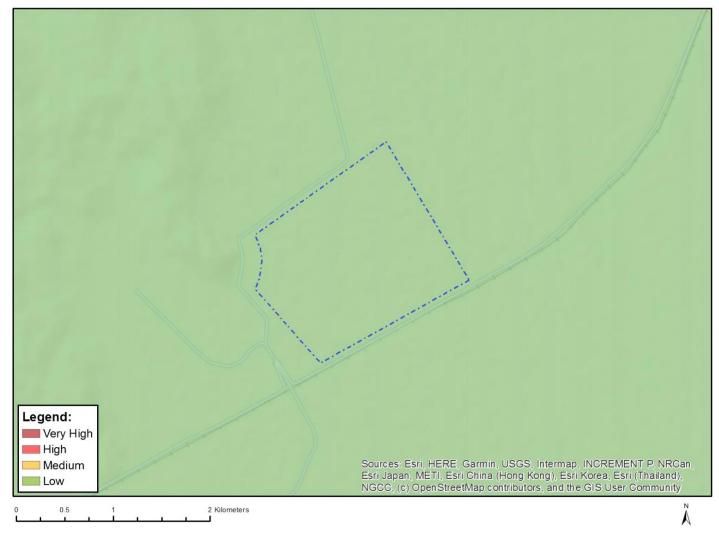


Figure 3: Map of relative agriculture theme sensitivity

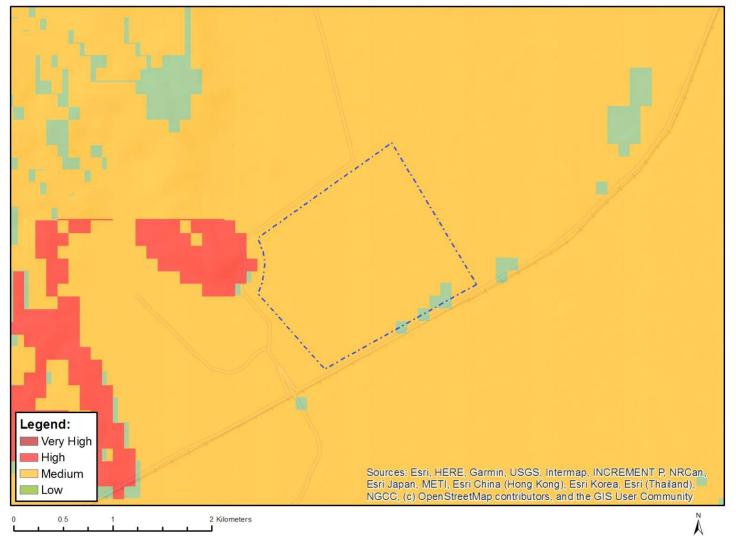


Figure 4: Map of relative animal species theme sensitivity

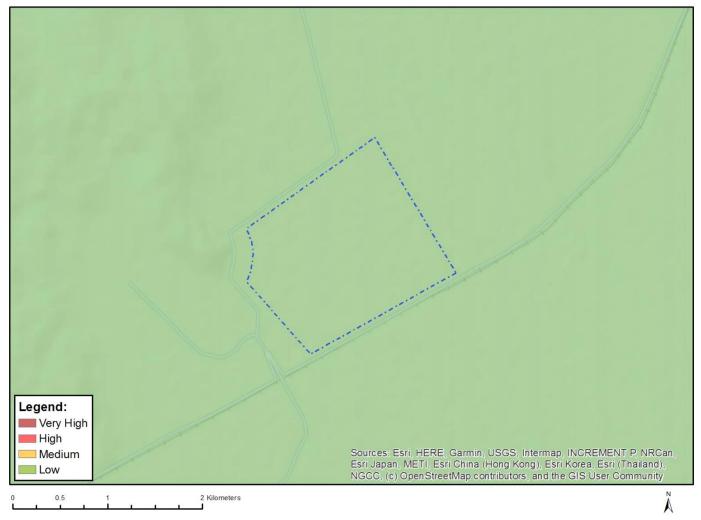


Figure 5: Map of relative aquatic biodiversity theme sensitivity

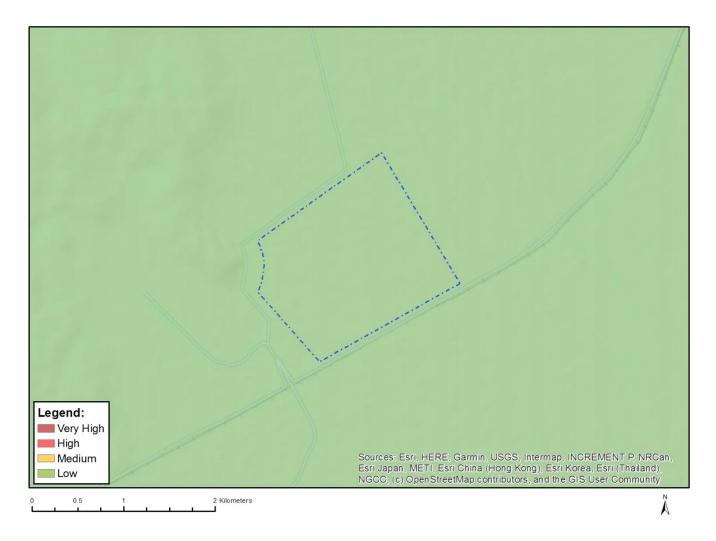


Figure 6: Map of relative archaeological and cultural heritage theme sensitivity.

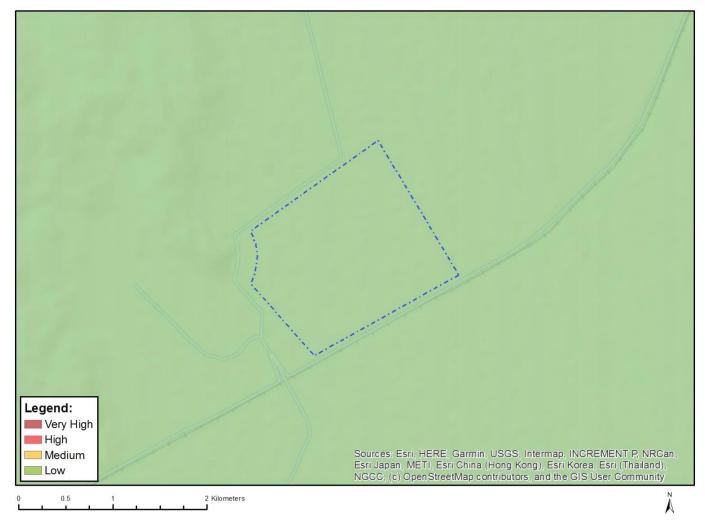


Figure 9: Map of relative civil aviation theme sensitivity

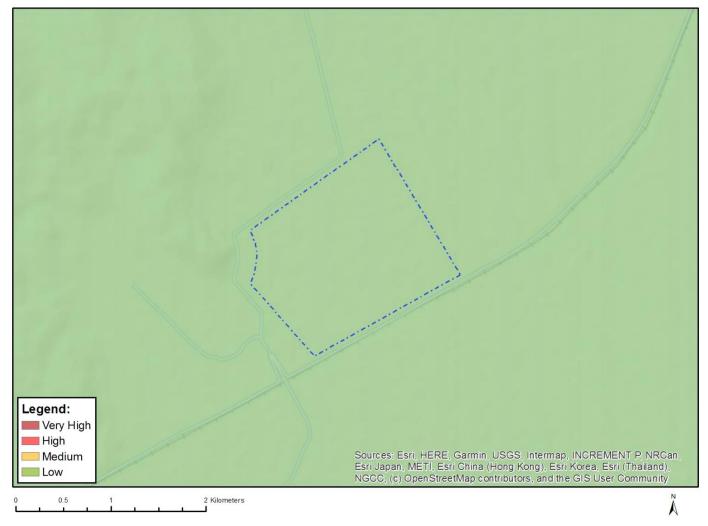


Figure 10: Map of relative defence theme sensitivity

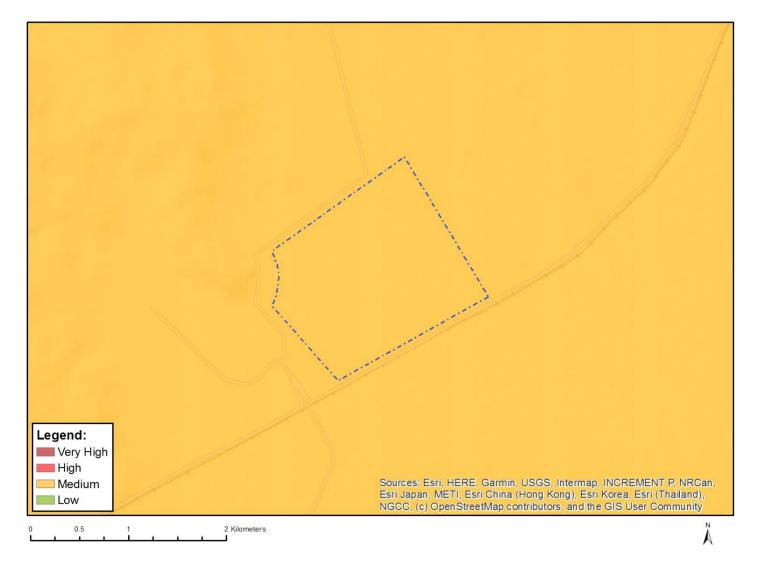


Figure 12: Map of relative palaeontological theme sensitivity

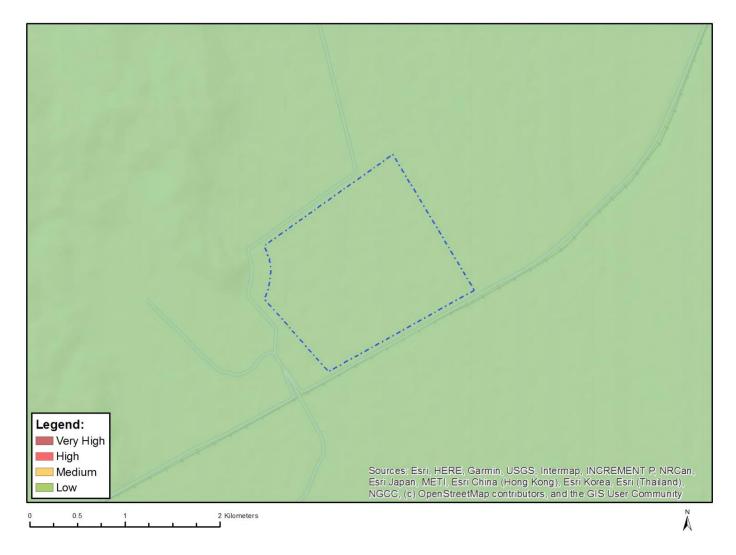


Figure 13: Map of relative plant species theme sensitivity

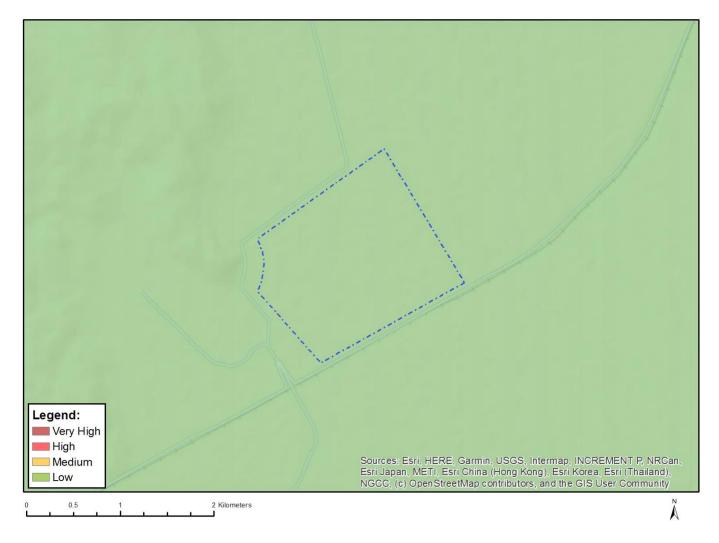


Figure 14: Map of relative RFI theme sensitivity



Figure 15: Map of relative terrestrial biodiversity theme sensitivity

# 7.3 Sub-section 3: Declaration

The proponent/applicant or holder of the EA affirms that he/she will abide and comply with the prescribed impact management outcomes and impact management actions as stipulated in part B: section 1 of the generic EMPr and have the understanding that the impact management outcomes and impact management actions are legally binding. The proponent/applicant or holder of the EA affirms that he/she will provide written notice to the CA 14 day prior to the date on which the activity will commence of commencement of construction to facilitate compliance inspections.

Signature Proponent/applicant/ holder of EA Date:

\_\_\_\_\_

\_\_\_\_\_

This declaration will be signed by the proponent/applicant/holder of the EA once the contractor is appointed and has provided inputs to this Generic EMPr as per the requirements of this template.

# 7.4 Sub-section 4: amendments to site specific information (Part B; section 2)

Should the EA be transferred to a new holder, <u>Part B: Section 2</u> must be completed by the new holder and submitted with the application for an amendment of the EA in terms of Regulations 29 or 31 of the EIA Regulations, whichever applies. The information submitted for an amendment to an environmental authorisation will be considered to be incomplete should a signed copy of <u>Part B: Section 2</u> not be submitted. Once approved, <u>Part B: Section 2</u> forms part of the EMPr for the development and the EMPr becomes legally binding to the new EA holder.

# PART C

#### 8 SITE SPECIFIC ENVIRONMENTAL ATTRIBUTES

If any specific environmental sensitivities/attributes are present on the site which require more specific impact management outcomes and actions, not included in the pre-approved generic EMPr template, to manage impacts, those impact management outcomes and impact management actions must be included in this section. These specific management controls must be referenced spatially, and must include impact management outcomes and impact management actions. The management controls including impact management outcomes and impact management actions must be presented in the format of the preapproved generic EMPr template. This applies only to additional impact management outcomes and impact management actions that are necessary.

If <u>Part C</u> is applicable to the development as authorised in the EA, it is required to be submitted to the CA together with the BAR or EIAR, for consideration of, and decision on, the application for EA. The information in this section must be prepared by an EAP and the name and expertise of the EAP, including the curriculum vitae are to be included. Once approved, <u>Part C</u> forms part of the EMPr for the site and is legally binding.

This section will **not be required** should the site contain no specific environmental sensitivities or attributes.

# **CONSTRUCTION AND DECOMMISSIONING OUTCOMES AND ACTIONS**

# 7.1 Ecology (Fauna and Flora)

Impact management outcome: Management of impacts on flora, fauna and sensitive areas.

Impact Management Actions	Implementation			Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Timeframe	Evidence of	
	person	implementation	implementati	person		compliance	
			on				
<ul> <li>Pre-construction walk-through of the final layout in order to locate species of conservation concern that can be translocated as well as comply with the provincial permit conditions</li> </ul>	dEO, Specialist	Visual inspection of the layout with walk-through report produced	Prior to construction	ECO	Once prior to commencement of construction	Walk-through report produced and kept on file during construction	
<ul> <li>Search and rescue for identified species of concern before construction.</li> </ul>	Relevant specialist in consultation with the Contractor	Develop and implement a Plant Search and Rescue Plan in accordance with relevant permits	Pre- construction & Construction	ECO	Once prior to commencement of construction	Implementation of the Plant Search and Rescue Plan and photographic evidence and notes of the implementation of the plan	
<ul> <li>Vegetation clearing to commence only after walk- through has been conducted and necessary permits obtained.</li> </ul>	cEO, Specialist, Contractor	Vegetation clearing planned to commence only after walk-through has been conducted and necessary permits obtained	Duration of construction phase	ECO	Weekly	Vegetation clearing commenced only after walk- through has been conducted and necessary	

Impact Management Actions	Implementation			Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Timeframe	Evidence of
	person	implementation	implementati on	person		compliance
			on			permits obtained.
<ul> <li>Temporary laydown areas should be located within previously transformed areas or areas that have been identified as being of low sensitivity. These areas should be rehabilitated after use.</li> </ul>	cEO, Specialist, Contractor	Laydown areas to be defined during planning of construction activities	Duration of construction phase	ECO	Weekly	Laydown areas located within previously transformed areas or areas of low sensitivity
<ul> <li>Contractor's Environmental Officer (EO) to provide supervision and oversight of vegetation clearing activities within sensitive areas.</li> </ul>	Contractor, cEO	Ensure that vegetation clearing in sensitive areas is undertaken in accordance with required mitigation measures.	Duration of the construction phase	ECO	Monthly	cEO oversees vegetation clearing in sensitive areas.
<ul> <li>Minimise the development footprint as far as possible and rehabilitate disturbed areas that are not required for the operation phase of the development.</li> </ul>	Contractor, cEO	Ensure that construction activities are restricted to the demarcated footprint and development and implement a site rehabilitation plan	Duration of the construction phase	ECO	Monthly	Construction activities restricted to development footprint All disturbed areas rehabilitated following completion of construction. Copy of rehabilitation

Impact Management Actions	Implementation			Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Timeframe	Evidence of
	person	implementation	implementati	person		compliance
			on			
						plan available
						on site
- Pre-construction environmental induction for all	cEO	Requirement for	Duration of	ECO	Monthly	Induction roster
construction staff on site to ensure that basic		induction of all staff	construction			of all staff
environmental principles are adhered to. This includes		prior to	phase			completed,
awareness of no littering, appropriate handling of		commencement				maintained and
pollution and chemical spills, avoiding fire hazards,		activities, as well as				available on
remaining within demarcated construction areas etc.		the development				site, induction
Induction should also include information with regards to		and application of				programme
fauna and, in particular, awareness about not harming		an induction				material
or collecting species such as snakes, tortoises and owls,		programme				observed and
which are often persecuted out of superstition.						on file on site.
- Demarcate all areas to be cleared with construction	dEO / cEO in	Erect appropriate	At the	ECO	Monthly	Access to
tape or other appropriate and effective means.	consultation	temporary barriers	commence			construction
However, caution should be exercised to avoid using	with the ECO	around construction	ment and for			area is closed-
material that might entangle fauna.		areas and ensure	the duration			off through
		material used is	of the			temporary
		fauna-friendly and	construction			barriers and
		must be removed	phase			barriers are
		following				maintained to a
		completion of				sufficient
		construction.				standard
						Material used to
						demarcate
						construction
						area is fauna-
						friendly and
						removed
						following

Impact Management Actions	Implementation			Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Timeframe	Evidence of
	person	implementation	implementati	person		compliance
			on			
						completion of construction.
<ul> <li>Vegetation clearing to be kept to a minimum. No unnecessary vegetation to be cleared.</li> </ul>	Contractor, cEO	Placement of infrastructure planned to minimise vegetation clearing	Duration of the construction phase	ECO	Monthly	Vegetation clearing minimised as far as possible.
<ul> <li>All construction vehicles should adhere to clearly defined and demarcated roads. No off-road driving to be allowed outside of the construction area.</li> </ul>	Contractor, cEO	Construction activities planned to ensure vehicles adhere to clearly defined and demarcated roads	Duration of the construction phase	ECO	Ongoing throughout construction	No off road driving outside of construction area.
<ul> <li>Temporary laydown areas should be located within previously transformed areas or areas that have been identified as being of low sensitivity. These areas should be rehabilitated after use.</li> </ul>	Contractor, cEO	Laydown areas planned within previously transformed or low sensitivity areas	Duration of the construction phase	ECO	Ongoing throughout construction	Laydown areas located within previously transformed or low sensitivity areas
<ul> <li>Any fauna threatened by the construction activities should be removed to safety by an appropriately qualified environmental officer.</li> </ul>	cEO, Specialist, Contractor	Implement search and relocation plan for threatened or dangerous fauna species and obtain the relevant permits for the removal of these species	Operation	Auditor	Annually	No fauna harmed as a result of maintenance activities. Necessary permits obtained prior to the removal of threatened fauna species, and copies of

Impact Management Actions	Implementatio	n		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Timeframe	Evidence of
	person	implementation	implementati	person		compliance
			on			
						permits
						observed during
						audit.
- All construction vehicles should adhere to a low speed	Contractor,	Install speed	During the	ECO	Monthly	Minimal
limit (30km/h) to avoid collisions with susceptible species	cEO	signage throughout	construction			instances of
such as snakes and tortoises.		site, include speed	phase			speeding as
		limit into induction				observed on site
		and ensure all staff				during audits
		entering site are				and as
		aware of the				evidenced in
		requirement to				the written log
		implement speed				of warnings and
		limits. Institute				fines issued for
		verbal and written				contraventions
		warnings for				
		violations and				
		appropriate fines				
		for repeat				
		contraventions.				
		Written log of fines				
		and warning issued				
		kept on site		500		
- » All hazardous materials should be stored in the	Contractor	Suitable bunding	Duration of	ECO	Monthly	Effective
appropriate manner to prevent contamination of the		and containment,	the project			bunding and
site. Any accidental chemical, fuel and oil spills that		demarcation and				containment of
occur at the site should be cleaned up in the		access control				hazardous
appropriate manner as related to the nature of the spill.		measures				materials as
		implemented for				evidenced on
		hazardous materials				site, along with suitable access
		at onsite stores. Spill				control and
		prevention and				conirol and

Impact Management Actions	Implementation			Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Timeframe	Evidence of
	person	implementation	implementati	person		compliance
			on			
		response plan				demarcation
		developed, and				provided at
		spill kits made				hazardous
		available, as well as				materials stores.
		all staff inducted				Written log of
		with spill response				spills and clean
		procedure and a				up actions
		log of inductions				implemented
		kept on file. Written				observed and
		record of spills and				kept on file at
		clean up actions				site
		kept on site				
- If trenches/tower foundations need to be dug, these	Contractor	Construction	Duration of	ECO	Weekly	Trenches/tower
should not be left open for extended periods of time as	cEO	planned such that	construction			foundations are
fauna may fall in and become trapped in them.		trenches/tower				open for the
Trenches which are standing open should have places		foundations are				least amount of
where there are soil ramps allowing fauna to escape the		open for the least				time possible.
trench.		amount of time				
		possible.				Trenches which
						are standing
		Trenches which are				open should
		standing open				have places
		should have places				where there are
		where there are soil				soil ramps
		ramps allowing				allowing fauna
		fauna to escape				to escape the
		the trench.				trench.
- The illegal collection, hunting or harvesting of any plants	Contractor	Awareness created	Duration of	ECO	Weekly	No evidence of
or animals at the site should be strictly forbidden.	cEO	regarding	construction			collection,
		prohibition on the				hunting or
		collection, hunting				harvesting of

Impact Management Actions	Implementatio	n		Monitoring	Monitoring			
	Responsible person	Method of implementation	Timeframe for implementati on	Responsible person	Timeframe	Evidence of compliance		
Personnel should not be allowed to wander off of the construction site.		or harvesting of any plants or animals				any plants or animals		
<ul> <li>No fuelwood collection should be allowed on-site</li> </ul>	cEO	Awareness created regarding the prohibition of the collection of fuelwood	Duration of construction	ECO	Weekly	No fuelwood collected		
<ul> <li>No fuelwood collection should be allowed on-site.</li> </ul>	cEO, Developer	Place signs on site indicating the fuelwood collection is prohibited and include this point in the environmental induction training	During the construction phase	ECO	Weekly	Sign prohibiting collection of fuelwood observed on site and evidence of discussion of this point contained in environmental induction training material		
<ul> <li>If any parts of the site such as construction camps must be lit at night, this should be done with low-UV type lights (such as most LEDs or HPS bulbs) as far as practically possible, which do not attract insects and which should be directed downwards.</li> </ul>	cEO, Contractor	Installation of low- UV type lights.	Operation	Auditor	Annually	Correct lighting fixtures are used.		

Impact management outcome: Management of erosion risk.

Impact Management Actions	Implementati	ion		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- Erosion management at the site should take place	cEO,	Develop and	Construction	ECO	Ongoing	Erosion
according to the Erosion Management Plan and	Specialist, Contractor	implement an Erosion			throughout construction	Management Plan and
Rehabilitation Plan.	Confractor	Management Plan			COnstruction	Rehabilitation
		and Rehabilitation				Plan developed
		Plan				and implemented
<ul> <li>All roads and other hardened surfaces should have runoff</li> </ul>	Contractor	Roads and other	Duration of the	ECO	Ongoing	Roads and other
control features which redirect water flow and dissipate any	Connacion	hardened surfaces	project	LCO	throughout	hardened
energy in the water which may pose an erosion risk.		designed to include			construction	surfaces
energy in the water which thay pose an erosion tisk.		runoff control			Consilocitori	implemented with
		features which				include runoff
		redirect water flow				control features
		and dissipate any				which redirect
		energy in the water				water flow and
		which may pose an				dissipate any
		erosion risk				energy in the
						water which may
						pose an erosion
						risk
- Regular monitoring for erosion after construction to ensure	Contractor,	Ongoing monitoring	During the	ECO	Ongoing	Monitoring for
that no erosion problems have developed as result of the	cEO	for erosion and	construction		throughout	erosion ongoing
disturbance must be undertaken, as per the Erosion		implementation of	phase		construction	and appropriate
Management and Rehabilitation Plans for the project.		appropriate				management
		management				measures
		measures where				implemented
		erosion is detected				where erosion is
						detected

Impact Management Actions	Implementati	on		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- All erosion problems observed must be rectified as soon as possible, using the appropriate erosion control structures and revegetation techniques.	Contractor cEO	Implementation of appropriate management measures where erosion is detected	During the construction phase	ECO	Ongoing throughout construction	Appropriate management measures implemented where erosion is detected
- All cleared areas must be revegetated with indigenous perennial shrubs and succulents from the local area. These can be cut when dry and placed on the cleared areas if natural recovery is slow.	CEO	Revegetation to be undertaken with indigenous perennial shrubs and succulents from the local area. Revegetated areas to be appropriately maintained.	During the construction phase	ECO	Ongoing throughout construction	Revegetation undertaken with indigenous perennial shrubs and succulents from the local area. Revegetated areas appropriately maintained.

# 7.2 Avifauna

Impact management outcome: Minimisation of disturbance and displacement of avifauna.

Impact Management Actions	Implementatio	'n		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
<ul> <li>All vehicles should adhere to clearly defined and demarcated roads, no off-road driving should be</li> </ul>	Contractor	Ensure vehicles make use of	Construction	dEO ECO	Ongoing during construction	Only demarcated
allowed	Operator	demarcated roads only				roads used
<ul> <li>Speed limits (30 km/h) should be strictly enforced to reduce unnecessary noise</li> </ul>	Contractor Operator	Employees and contractors aware of speed limit	Construction	dEO ECO	Ongoing during construction	Speed limit adhered to
<ul> <li>The movement of personnel should be restricted to the servitudes and access roads on the project site.</li> </ul>	Contractor Operator	Employees and contractors aware of requirement to restrict activities to servitudes and access roads	Construction	dEO ECO	Ongoing during construction	Movement of personnel restricted to the servitudes and access roads on the project site
<ul> <li>No dogs or cats other than those of the landowners should be allowed on site</li> </ul>	Contractor	No dogs or cats allowed on site	Construction	cEO ECO	Ongoing during construction	No dogs or cats other than those of the landowners on site
<ul> <li>Any No-go areas identified should be adhered to.</li> </ul>	Contractor Operator	Employees and contractors aware of identified no go areas.	Construction	dEO ECO	Ongoing during construction	No-go areas identified are adhered to

# **OPERATIONAL PHASE OUTCOMES AND ACTIONS**

# 7.3 Ecology (Fauna and Flora)

**Impact management outcome:** Direct loss of vegetation, including listed and protected species is reduced.

Impact Management Actions	Implementation			Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
- Any potentially dangerous fauna such as snakes or fauna threatened by the maintenance and operational activities should be removed to a safe location.	cEO, Specialist, Contractor	Develop a search and relocation plan for threatened or dangerous	Operation and maintenance	deo	As and when required	Necessary permits obtained prior to the removal of threatened	
		fauna species and obtain the relevant permits for the removal of these species				fauna species, and copies of permits observed during audit.	
<ul> <li>All hazardous materials should be stored in the appropriate manner to prevent contamination of the site. Any accidental chemical, fuel and oil spills that occur at the site should be cleaned up in the appropriate manner as related to the nature of the spill.</li> </ul>	Contractor	Suitable bunding and containment, demarcation and access control measures implemented for hazardous materials at onsite stores. Spill prevention and response plan developed, and	Duration of the project	deo	Monthly	Effective bunding and containment of hazardous materials as evidenced on site, along with suitable access control and demarcation provided at hazardous materials stores. Written log of	

Impact Management Actions	Implementation	1		Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
		spill kits made				spills and clean	
		available, as				up actions	
		well as all staff				implemented	
		inducted with				observed and	
		spill response				kept on file at	
		procedure and				site	
		a log of					
		inductions kept					
		on file. Written					
		record of spills					
		and clean up					
		actions kept on					
		site					
- If any parts of the site such as construction camps must be lit	cEO,	Installation of	Operation	Auditor	Annually	Correct lighting	
at night, this should be done with low-UV type lights (such as	Contractor	low-UV type				fixtures are used.	
most LEDs or HPS bulbs) as far as practically possible, which do		lights.					
not attract insects and which should be directed downwards.							
All vehicles accessing the site should adhere to a low speed limit	Contractor,	Install speed	During the	dEO	Monthly	Minimal	
(30km/h max for heavy vehicles and 40km/h for light vehicles) to	cEO	signature	construction			instances of	
avoid collisions with susceptible species such as snakes and		throughout site,	phase			speeding as	
tortoises.		include speed				observed on site	
		limit into				during audits	
		induction and				and as	
		ensure all staff				evidenced in	
		entering site is				the written log	
		aware of the				of warnings and	
		requirement to				fines issued for	
		implement				contraventions	
		speed limits.					
		Institute verbal					
		and written					
		warnings for					

Impact Management Actions	Implementation	Implementation				
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		violations and				
		appropriate				
		fines for repeat				
		contraventions.				
		Written log of				
		fines and				
		warning issued				
		kept on site				
- Regular monitoring for alien plants within the development	Operator	Invasive Alien	Operation	External	Annually –	Invasive alien
footprint as well as adjacent areas which receive runoff from		Plant species		Auditor, dEO	external	plant species
the facility must be undertaken as these are also likely to be		eradication and			audit and	appropriately
prone to invasion problems. Regular alien clearing should be		management			quarterly	managed
conducted using the best-practice methods for the species		programme and			dEO	
concerned. The use of herbicides should be avoided as far		implemented.				
as possible.						

# Impact management outcome: Management of erosion risk.

Impact Management Actions	Implementation			Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
- Erosion management at the site should take place	Operator	Develop and	Operation	dEO	Prior to	Erosion	
according to the Erosion Management Plan and		implement an			operation	Management	
Rehabilitation Plan.		Erosion				Plan and	
		Management Plan			Duration of	Rehabilitation	
		and Rehabilitation			operation	Plan developed	
		Plan				and implemented	

Impact Management Actions	Implementat	ion		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- All roads and other hardened surfaces should have runoff	Operator	Roads and other	Operation	dEO,	Annually	Roads and other
control features which redirect water flow and dissipate any		hardened surfaces		external		hardened
energy in the water which may pose an erosion risk.		maintained to		auditor		surfaces
		include runoff				maintained with
		control features				include runoff
		which redirect				control features
		water flow and				which redirect
		dissipate any				water flow and
		energy in the water				dissipate any
		which may pose an				energy in the
		erosion risk				water which may
						pose an erosion
						risk
- Regular monitoring for erosion after construction to ensure	Operator,	Ongoing monitoring	Operation	dEO,	Annually	Monitoring for
that no erosion problems have developed as result of the	dEO	for erosion and		external		erosion ongoing
disturbance must be undertaken, as per the Erosion		implementation of		auditor		and appropriate
Management and Rehabilitation Plans for the project.		appropriate				management
		management				measures
		measures where				implemented
		erosion is detected				where erosion is
						detected
- All erosion problems observed must be rectified as soon as	Operator	Implementation of	Operation	dEO,	Annually	Appropriate
possible, using the appropriate erosion control structures		appropriate		external		management
and revegetation techniques.		management		auditor		measures
		measures where				implemented
		erosion is detected				where erosion is
						detected
- All cleared areas must be revegetated with indigenous	Operator	Revegetation	Rehabilitation	dEO,	Annually	Revegetation
perennial shrubs and succulents from the local area. These		undertaken with		external		undertaken with
can be cut when dry and placed on the cleared areas if		indigenous		auditor		indigenous
natural recovery is slow.		perennial shrubs				perennial shrubs
						and succulents

Impact Management Actions	Implementat	ion		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
		and succulents from				from the local
		the local area.				area.
		Revegetated areas				Revegetated
		to be appropriately				areas
		maintained.				appropriately
						maintained.

# 7.4 Avifauna

Impact management outcome: Minimisation of disturbance and displacement of avifauna.

Impact Management Actions	Implementation	า		Monitoring		
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of
	person	implementation	implementation	person		compliance
- All vehicles should adhere to clearly defined and	Contractor	Ensure vehicles	Operation &	dEO	During	Only
demarcated roads, no off-road driving should be		make use of	maintenance	ECO	maintenance	demarcated
allowed	Operator	demarcated			activities	roads used
		roads only				
- Speed limits (30 km/h) should be strictly enforced to	Contractor	Employees and	Operation &	dEO	During	Speed limit
reduce unnecessary noise		contractors	maintenance	ECO	maintenance	adhered to
	Operator	aware of speed			activities	
		limit				
- The movement of personnel should be restricted to	Contractor	Employees and	Operation &	dEO	During	Movement of
the servitudes and access roads on the project site.		contractors	maintenance	ECO	maintenance	personnel
	Operator	aware of			activities	restricted to the
		requirement to				servitudes and
		restrict activities				access roads on
						the project site

Impact Management Actions	Implementation			Monitoring			
	Responsible	Method of	Timeframe for	Responsible	Frequency	Evidence of	
	person	implementation	implementation	person		compliance	
		to servitudes and					
		access roads					
- Any No-go areas identified should be adhered to.	Contractor	Employees and	Operation &	dEO	During	No-go areas	
		contractors	maintenance	ECO	maintenance	identified are	
	Operator	aware of			activities	adhered to	
		identified no go					
		areas.					

#### **APPENDIX 1: METHOD STATEMENTS**

To be prepared by the contractor prior to commencement of the activity. The method statements are **not required** to be submitted to the CA.

# APPENDIX 2: CV OF THE EAP
