ID	Task Name	Duration	Start	Finish
1	**Taung Skull World Heritage Site**	**80 days?**	**Mon 01-05-17**	**Fri 18-08-17**
2				
3	**Powerhouse**	**34 days?**	**Mon 01-05-17**	**Thu 15-06-17**
4	Site & services information to be provided: site visit	1 day	Mon 01-05-17	Mon 01-05-17
5	Conceptual Design	1 day	Tue 02-05-17	Tue 02-05-17
6	Design proposal presented to Client	1 day	Wed 03-05-17	Wed 03-05-17
7	Design signed off by Department	1 day	Thu 04-05-17	Thu 04-05-17
8	Working drawings for powerhouse complete	5 days	Fri 05-05-17	Thu 11-05-17
9	Working drawing approval by principal agent	1 day	Fri 12-05-17	Fri 12-05-17
10	Working drawings signed by Department	3 days	Mon 15-05-17	Wed 17-05-17
11	Assistance for Bill of Quantities and tender documents	14 days	Thu 18-05-17	Tue 06-06-17
12	Tender documents ready	1 day	Wed 07-06-17	Wed 07-06-17
13	Tender documents delivered	1 day	Thu 08-06-17	Thu 08-06-17
14	Submission to SAHRA	20 days	Thu 18-05-17	Wed 14-06-17
15	Approval by SAHRA	1 day?	Thu 15-06-17	Thu 15-06-17
16	Submission to council	20 days	Thu 18-05-17	Wed 14-06-17
17	Approval by council	1 day?	Thu 15-06-17	Thu 15-06-17
18				
19	**Managers office**	**33 days?**	**Tue 02-05-17**	**Thu 15-06-17**
20	Site & services information to be provided: site visit	1 day	Tue 02-05-17	Tue 02-05-17
21	Conceptual Design	1 day	Wed 03-05-17	Wed 03-05-17
22	Design proposal presented to Client	1 day	Thu 04-05-17	Thu 04-05-17
23	Design signed off by Department	1 day	Fri 05-05-17	Fri 05-05-17
24	Working drawings complete	4 days	Mon 08-05-17	Thu 11-05-17
25	Working drawing approval by principal agent	1 day	Fri 12-05-17	Fri 12-05-17
26	Working drawings signed by Department	3 days	Mon 15-05-17	Wed 17-05-17
27	Assistance for Bill of Quantities and tender documents	14 days	Thu 18-05-17	Tue 06-06-17
28	Tender documents ready	1 day	Wed 07-06-17	Wed 07-06-17
29	Tender documents delivered	1 day	Thu 08-06-17	Thu 08-06-17
30	Submission to SAHRA	20 days	Thu 18-05-17	Wed 14-06-17
31	Approval by SAHRA	1 day?	Thu 15-06-17	Thu 15-06-17
32	Submission to council	20 days	Thu 18-05-17	Wed 14-06-17
33	Approval by council	1 day?	Thu 15-06-17	Thu 15-06-17
34				
35	**Picnic site ablution**	**33 days?**	**Tue 02-05-17**	**Thu 15-06-17**
36	Site & services information to be provided: site visit	1 day	Tue 02-05-17	Tue 02-05-17
37	Conceptual Design	1 day	Wed 03-05-17	Wed 03-05-17
38	Design proposal presented to Client	1 day	Thu 04-05-17	Thu 04-05-17
39	Design signed off by Department	1 day	Fri 05-05-17	Fri 05-05-17
40	Working drawings for complete	4 days	Mon 08-05-17	Thu 11-05-17
41	Working drawing approval by principal agent	1 day	Fri 12-05-17	Fri 12-05-17
42	Working drawings signed by Department	3 days	Mon 15-05-17	Wed 17-05-17
43	Assistance for Bill of Quantities and tender documents	14 days	Thu 18-05-17	Tue 06-06-17
44	Tender documents ready	1 day	Wed 07-06-17	Wed 07-06-17
45	Tender documents delivered	1 day	Thu 08-06-17	Thu 08-06-17
46	Submission to SAHRA	20 days	Thu 18-05-17	Wed 14-06-17
47	Approval by SAHRA	1 day?	Thu 15-06-17	Thu 15-06-17
48	Submission to council	20 days	Thu 18-05-17	Wed 14-06-17
49	Approval by council	1 day?	Thu 15-06-17	Thu 15-06-17
50				
51	**Museum at Mine Managers Office**	**58 days?**	**Tue 02-05-17**	**Thu 20-07-17**
52	Site & services information to be provided: site visit	1 day	Tue 02-05-17	Tue 02-05-17
53	Conceptual Design	10 days	Thu 04-05-17	Wed 17-05-17
54	Design proposal presented to Client	1 day	Thu 25-05-17	Thu 25-05-17
55	Design proposal reviewed	5 days	Fri 26-05-17	Thu 01-06-17
56	Design signed off by Department	1 day	Fri 02-06-17	Fri 02-06-17
57	Working drawings for complete	14 days	Mon 05-06-17	Thu 22-06-17
58	Working drawing approval by principal agent	1 day	Fri 23-06-17	Fri 23-06-17
59	Working drawings signed by Department	3 days	Mon 26-06-17	Wed 28-06-17
60	Assistance for Bill of Quantities and tender documents	14 days	Thu 29-06-17	Tue 18-07-17
61	Tender documents ready	1 day	Wed 19-07-17	Wed 19-07-17
62	Tender documents delivered	1 day	Thu 20-07-17	Thu 20-07-17
63	Submission to SAHRA	15 days	Thu 29-06-17	Wed 19-07-17
64	Approval by SAHRA	1 day?	Thu 20-07-17	Thu 20-07-17
65	Submission to council	15 days	Thu 29-06-17	Wed 19-07-17
66	Approval by council	1 day?	Thu 20-07-17	Thu 20-07-17
67				
68	**Mining compound**	**45 days?**	**Thu 25-05-17**	**Wed 26-07-17**
69	Site & services information to be provided: site visit	1 day	Thu 25-05-17	Thu 25-05-17
70	Conceptual Design	8 days	Fri 26-05-17	Tue 06-06-17
71	Design proposal presented to Client	1 day	Wed 07-06-17	Wed 07-06-17
72	Design signed off by Department	1 day	Thu 08-06-17	Thu 08-06-17
73	Working drawings for complete	14 days	Fri 09-06-17	Wed 28-06-17
74	Working drawing approval by principal agent	1 day	Thu 29-06-17	Thu 29-06-17
75	Working drawings signed by Department	3 days	Fri 30-06-17	Tue 04-07-17
76	Assistance for Bill of Quantities and tender documents	14 days	Wed 05-07-17	Mon 24-07-17
77	Tender documents ready	1 day	Tue 25-07-17	Tue 25-07-17
78	Tender documents delivered	1 day	Wed 26-07-17	Wed 26-07-17
79	Submission to SAHRA	15 days	Wed 05-07-17	Tue 25-07-17
80	Approval by SAHRA	1 day?	Wed 26-07-17	Wed 26-07-17
81	Submission to council	15 days	Wed 05-07-17	Tue 25-07-17
82	Approval by council	1 day?	Wed 26-07-17	Wed 26-07-17
83				
84	**Tumeng waterfall ablution design**	**52 days?**	**Tue 02-05-17**	**Wed 12-07-17**
85	Site & services information to be provided: site visit	1 day	Tue 02-05-17	Tue 02-05-17
86	Conceptual Design	5 days	Tue 09-05-17	Mon 15-05-17
87	Design proposal presented to Client	1 day	Tue 16-05-17	Tue 16-05-17
88	Design signed off by Department	1 day	Thu 25-05-17	Thu 25-05-17
89	Working drawings for complete	14 days	Fri 26-05-17	Wed 14-06-17
90	Working drawing approval by principal agent	1 day	Thu 15-06-17	Thu 15-06-17
91	Working drawings signed by Department	3 days	Fri 16-06-17	Tue 20-06-17
92	Assistance for Bill of Quantities and tender documents	14 days	Wed 21-06-17	Mon 10-07-17
93	Tender documents ready	1 day	Tue 11-07-17	Tue 11-07-17
94	Tender documents delivered	1 day	Wed 12-07-17	Wed 12-07-17
95	Submission to SAHRA	15 days	Wed 21-06-17	Tue 11-07-17
96	Approval by SAHRA	1 day?	Wed 12-07-17	Wed 12-07-17
97	Submission to council	15 days	Wed 21-06-17	Tue 11-07-17
98	Approval by council	1 day?	Wed 12-07-17	Wed 12-07-17
99				
100	**Hiking trail details**	**53 days?**	**Wed 07-06-17**	**Fri 18-08-17**
101	Site & services information to be provided: site visit	1 day	Wed 07-06-17	Wed 07-06-17
102	Conceptual Design	5 days	Thu 08-06-17	Wed 14-06-17
103	Design proposal presented to Client	1 day	Thu 15-06-17	Thu 15-06-17
104	Design signed off by Department	10 days	Fri 16-06-17	Thu 29-06-17
105	Working drawings for complete	14 days	Fri 30-06-17	Wed 19-07-17
106	Working drawing approval by principal agent	3 days	Thu 20-07-17	Mon 24-07-17
107	Working drawings signed by Department	3 days	Tue 25-07-17	Thu 27-07-17
108	Assistance for Bill of Quantities and tender documents	14 days	Fri 28-07-17	Wed 16-08-17
109	Tender documents ready	1 day	Thu 17-08-17	Thu 17-08-17
110	Tender documents delivered	1 day	Fri 18-08-17	Fri 18-08-17
111	Submission to SAHRA	15 days	Fri 28-07-17	Thu 17-08-17
112	Approval by SAHRA	1 day?	Fri 18-08-17	Fri 18-08-17
113	Submission to council	15 days	Fri 28-07-17	Thu 17-08-17
114	Approval by council	1 day?	Fri 18-08-17	Fri 18-08-17
115				
116	**Stone miners cottage**	**46 days?**	**Wed 07-06-17**	**Wed 09-08-17**
117	Site & services information to be provided: site visit	1 day	Wed 07-06-17	Wed 07-06-17
118	Conceptual Design	5 days	Thu 08-06-17	Wed 14-06-17
119	Design proposal presented to Client	1 day	Thu 15-06-17	Thu 15-06-17
120	Design signed off by Department	3 days	Fri 16-06-17	Tue 20-06-17
121	Working drawings for complete	14 days	Wed 21-06-17	Mon 10-07-17
122	Working drawing approval by principal agent	3 days	Tue 11-07-17	Thu 13-07-17
123	Working drawings signed by Department	3 days	Fri 14-07-17	Tue 18-07-17
124	Assistance for Bill of Quantities and tender documents	14 days	Wed 19-07-17	Mon 07-08-17
125	Tender documents ready	1 day	Tue 08-08-17	Tue 08-08-17
126	Tender documents delivered	1 day	Wed 09-08-17	Wed 09-08-17
127	Submission to SAHRA	15 days	Wed 19-07-17	Tue 08-08-17
128	Approval by SAHRA	1 day?	Wed 09-08-17	Wed 09-08-17
129	Submission to council	15 days	Wed 19-07-17	Tue 08-08-17
130	Approval by council	1 day?	Wed 09-08-17	Wed 09-08-17
131				
132	**Geology laboratory**	**77 days?**	**Tue 02-05-17**	**Wed 16-08-17**
133	Site & services information to be provided: site visit	1 day	Tue 02-05-17	Tue 02-05-17
134	Conceptual Design Reviewed	5 days	Thu 15-06-17	Wed 21-06-17
135	Design proposal presented to Client	1 day	Thu 22-06-17	Thu 22-06-17
136	Design signed off by Department	3 days	Fri 23-06-17	Tue 27-06-17
137	Working drawings for complete	14 days	Wed 28-06-17	Mon 17-07-17
138	Working drawing approval by principal agent	3 days	Tue 18-07-17	Thu 20-07-17
139	Working drawings signed by Department	3 days	Fri 21-07-17	Tue 25-07-17
140	Assistance for Bill of Quantities and tender documents	14 days	Wed 26-07-17	Mon 14-08-17
141	Tender documents ready	1 day	Tue 15-08-17	Tue 15-08-17
142	Tender documents delivered	1 day	Wed 16-08-17	Wed 16-08-17
143	Submission to SAHRA	15 days	Wed 26-07-17	Tue 15-08-17
144	Approval by SAHRA	1 day?	Wed 16-08-17	Wed 16-08-17
145	Submission to council	15 days	Wed 26-07-17	Tue 15-08-17
146	Approval by council	1 day?	Wed 16-08-17	Wed 16-08-17
147				
148	**Site works**	**69 days?**	**Tue 02-05-17**	**Fri 04-08-17**
149	Site & services information to be provided: site visit	1 day	Tue 02-05-17	Tue 02-05-17
150	Conceptual Design	5 days	Mon 05-06-17	Fri 09-06-17
151	Design proposal presented to Client	1 day	Mon 12-06-17	Mon 12-06-17
152	Design signed off by Department	3 days	Tue 13-06-17	Thu 15-06-17
153	Working drawings for complete	14 days	Fri 16-06-17	Wed 05-07-17
154	Working drawing approval by principal agent	3 days	Thu 06-07-17	Mon 10-07-17
155	Working drawings signed by Department	3 days	Tue 11-07-17	Thu 13-07-17
156	Assistance for Bill of Quantities and tender documents	14 days	Fri 14-07-17	Wed 02-08-17
157	Tender documents ready	1 day	Thu 03-08-17	Thu 03-08-17
158	Tender documents delivered	1 day	Fri 04-08-17	Fri 04-08-17
159	Submission to SAHRA	15 days	Fri 14-07-17	Thu 03-08-17
160	Approval by SAHRA	1 day?	Fri 04-08-17	Fri 04-08-17
161	Submission to council	15 days	Fri 14-07-17	Thu 03-08-17
162	Approval by council	1 day?	Fri 04-08-17	Fri 04-08-17

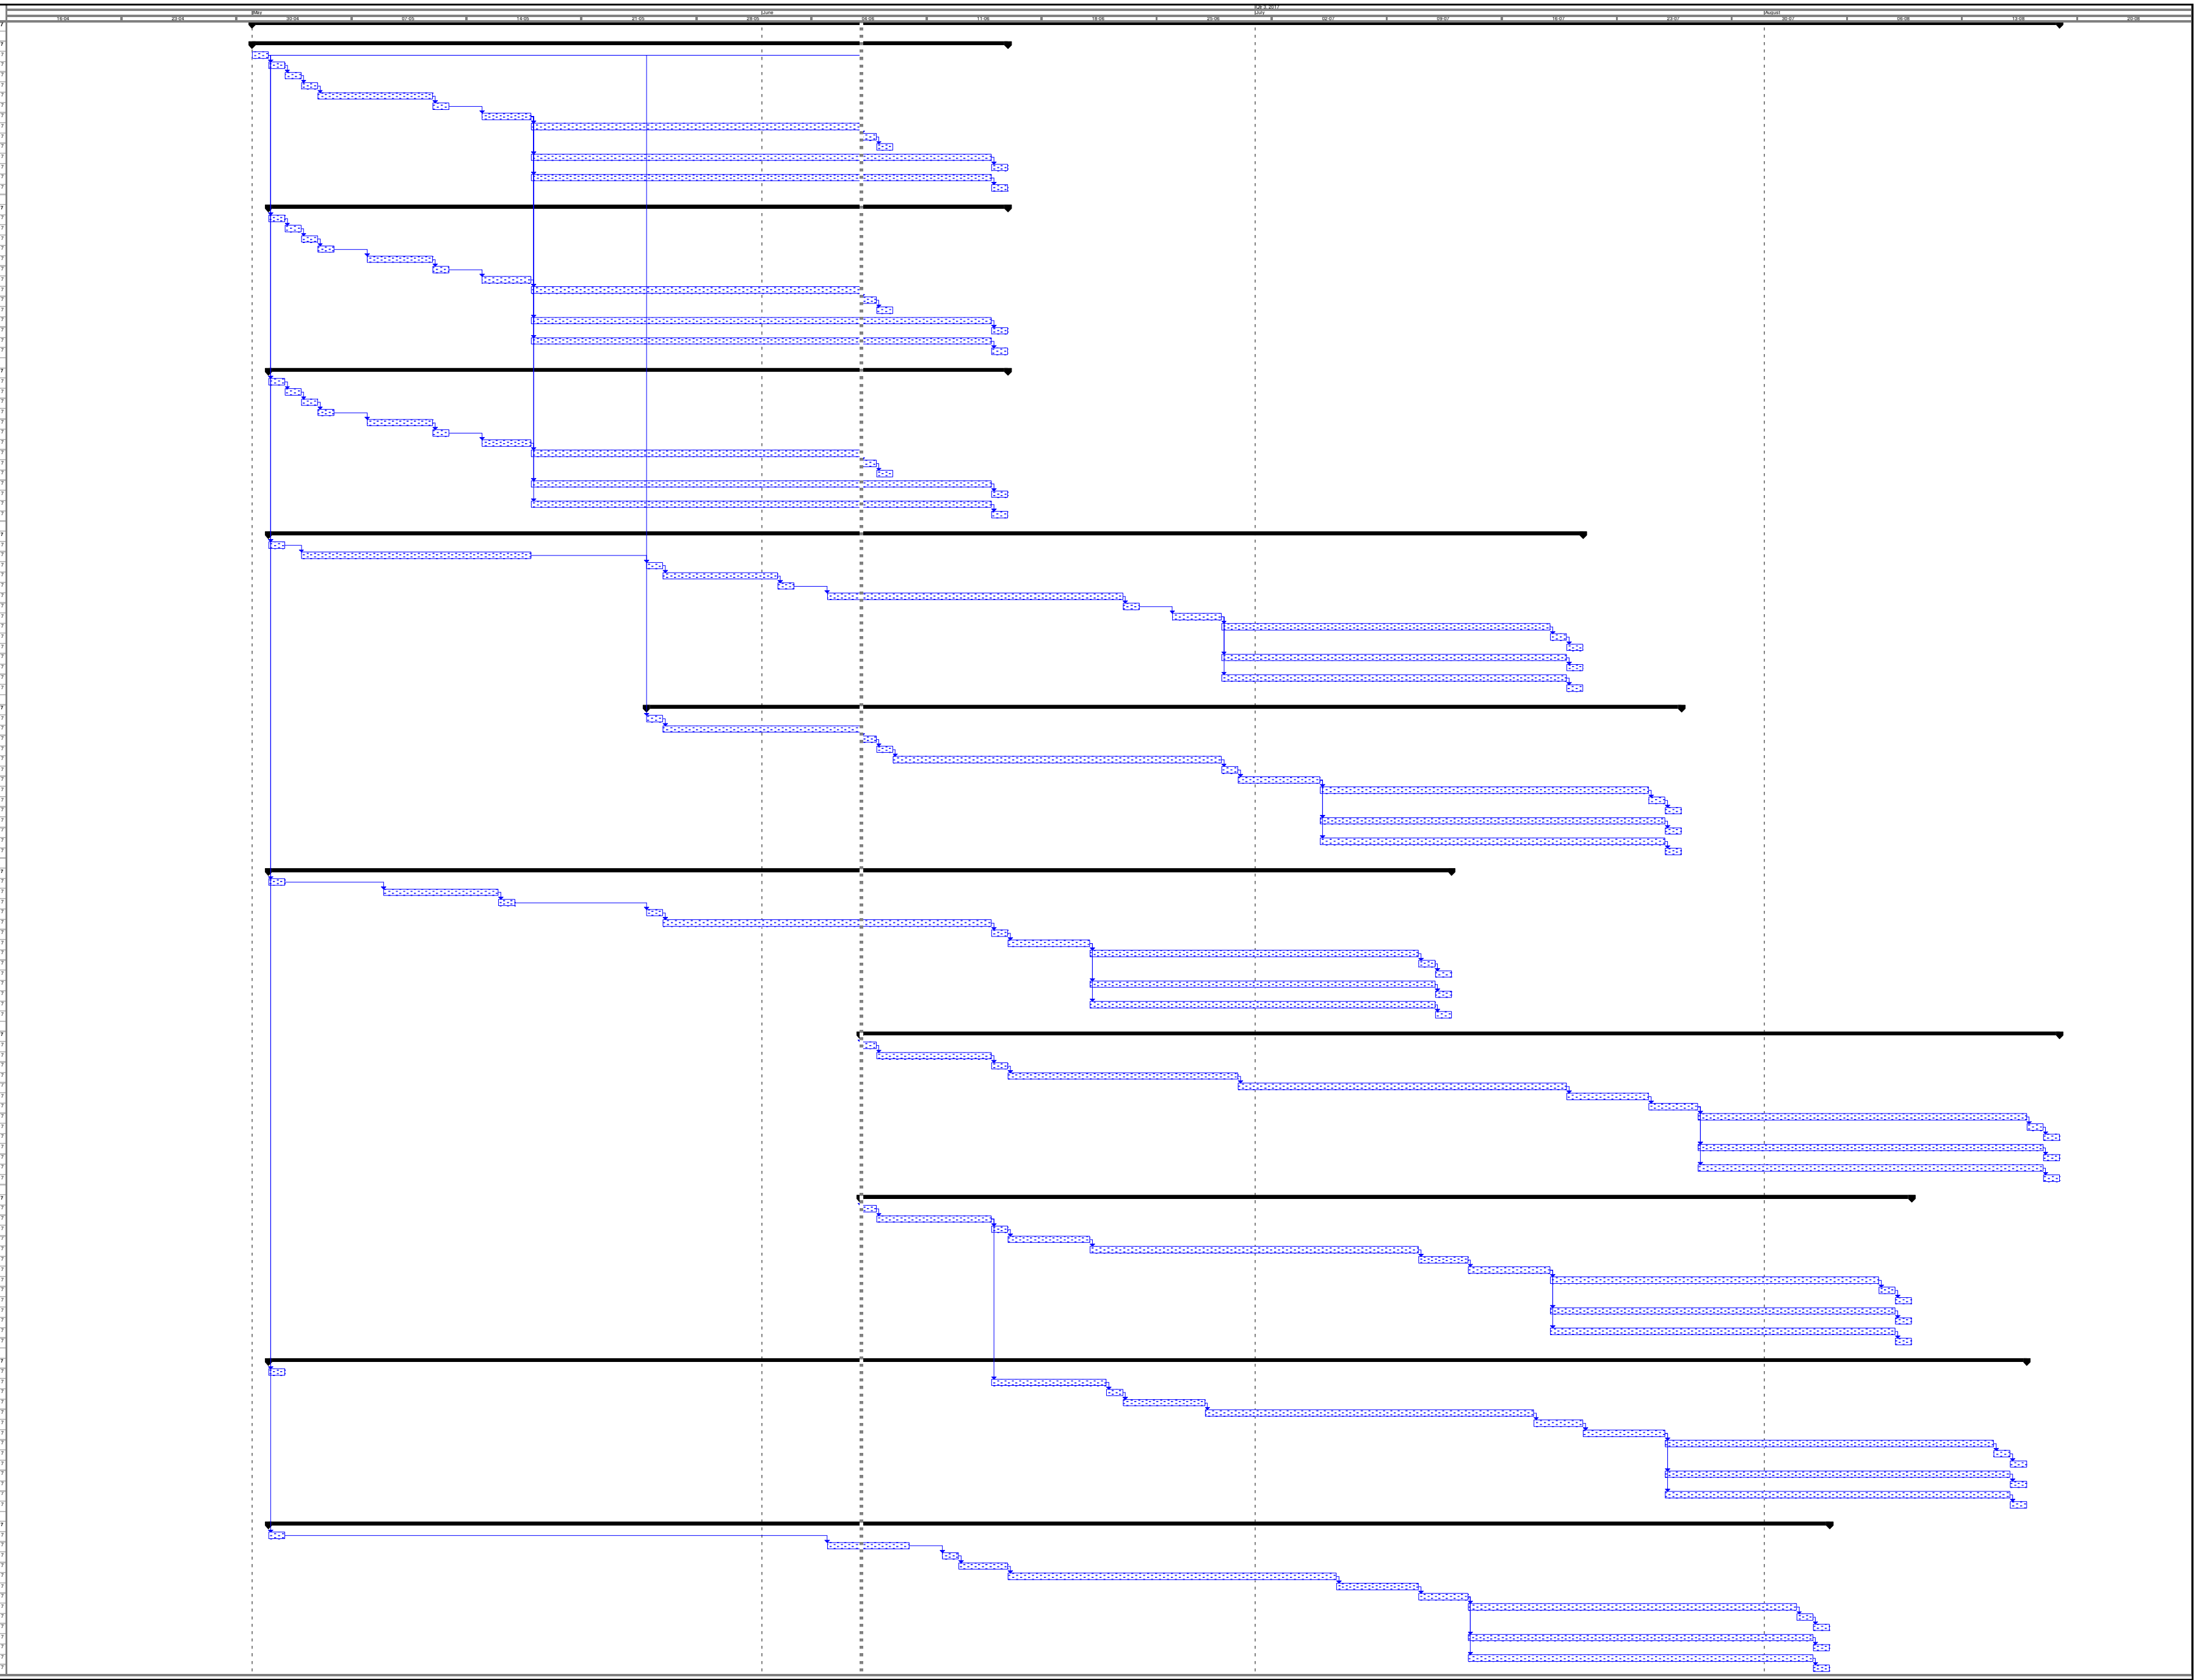

Project: taung programme rev2.mpp
Date: Wed 07-06-17

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
